
# Vol. 4 of 5 EP-457/2013/D Central Kowloon Route Yau Ma Tei West Contract No. HY/2014/20 &

Buildings, Electrical and Mechanical Works

Contract No. HY/2019/13

(Yau Ma Tei West area)

December 2023

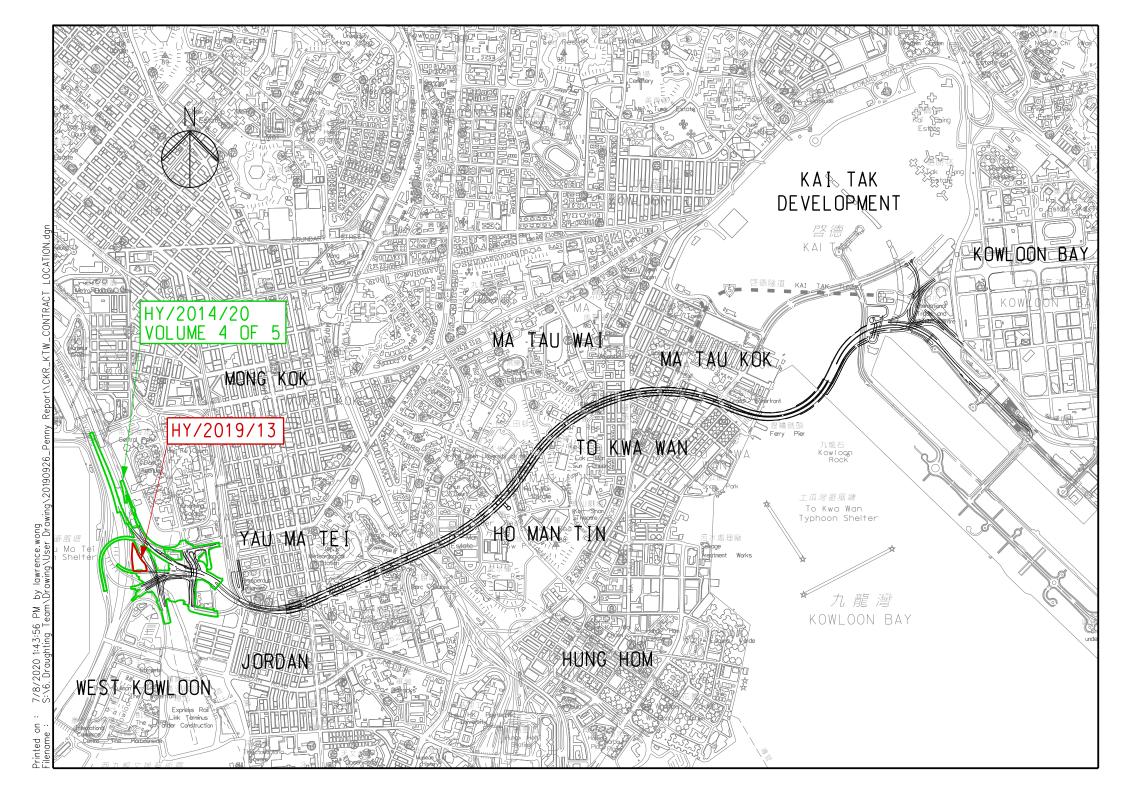

# Central Kowloon Route Yau Ma Tei West Contract No. HY/2014/20





### Environmental Permit No. EP-457/2013/D

### **Central Kowloon Route**

### **Independent Environmental Checker Verification**

Works Contract:	Yau Ma Tei West (HY/2014/20)
Reference Document/Plan	
Document/ <del>Plan</del> to be <del>Certified</del> / Verified:	Monthly EM&A Report No.59 (December 2023)
Date of Report:	9 January 2024 (Rev. 1)
Date received by IEC:	10 January 2024

### **Reference EP Condition**

Environmental Permit Condition: 3.4

Submission of Monthly EM&A Report of the Project

3.4 Four hard copies and one electronic copy of monthly EM&A Report shall be submitted to the Director within 2 weeks after the end of each reporting month throughout the entire construction period. The EM&A Reports shall include a summary of all non-compliance. The submissions shall be certified by the ET Leader and verified by the IEC as complying with the requirements as set out in the EM&A Manual before submission to the Director. Additional copies of the submission shall be provided to the Director upon request by the Director.

### **IEC Verification**

I hereby verify that the above referenced document/<del>plan</del> complies with the above referenced condition of EP-457/2013/D.

Ms Mandy To

Mondy 20.

Date:

10 January 2024

Independent Environmental Checker

Our ref: 0436942\_IEC Verification Cert\_YMTW\_Monthly EM&A Rpt No.59.docx





# Build King – SK ecoplant Joint Venture

# Central Kowloon Route Contract HY/2014/20

Section of Yau Ma Tei West Section

Monthly EM&A Report No. 59

(Period from 1 to 31 December 2023)

Rev. 1

(9 January 2024)

	Name	Signature
Prepared by	Kako H.L. Ho (Assistant Environmental Consultant)	Ho
Checked & Reviewed by	Y.H. LAW (Senior Environmental Consultant)	Malan
Approved & Certified by	Kevin W. M. Li (Environmental Team Leader)	K

### **TABLE OF CONTENTS**

### **EXECUTIVE SUMMARY**

1.	BASIC PROJECT INFORMATION	7
2.	ENVIRONMENTAL STATUS	10
3.	MONITORING RESULTS	12
4.	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS	20
5.	EM&A SITE INSPECTION	22
6.	FUTURE KEY ISSUES	23
7	CONCLUSION AND RECOMMENDATIONS	24

### LIST OF APPENDICES

- A. Alignment and Works Area for the Contract No. HY/2014/20
- B. Construction Programme
- C. Project Organization Chart
- D. Dust Event-Action Plan (EAP)
- E. Noise Event-Action Plan (EAP)
- F. Environmental Mitigation Implementation Schedule (EMIS)
- G. Monitoring Schedules of the Reporting Month
- H. Calibration Certificate (Air Monitoring)
- I. Calibration Certificate (Noise)
- J. The Certification of Laboratory with HOKLAS Accredited Analytical Tests
- K. Location Plan of Noise and Air Quality Monitoring Station
- L. Monitoring Data (Air Monitoring)
- M. Monitoring Data (Noise)
- N. Waste Flow Table
- O. Statistics on Complaint, Notifications of Summons and Successful Prosecutions
- P. Monitoring Schedule of the Coming Month
- Q. Interim Report for the Complaint

### **EXECUTIVE SUMMARY**

- A.1 Build King SK ecoplant Joint Venture ("Contractor") commenced the construction works of Highway Department (HyD) Central Kowloon Route Contract No. HY/2014/20 Section of Yau Ma Tei West ("The Project") on 12 February 2019. This is the 59<sup>th</sup> monthly Environmental Monitoring and Audit (EM&A) report presenting the EM&A works carried out during the period from 1 December 2023 to 31 December 2023.
- A.2 A summary of the construction works reported by Main Contractor for the Project during the reporting month is listed below.

### **Construction Activities undertaken**

- Socket H-Pile (Landscaped Deck and Bridges) at Portion 1B and 1D
- Noise Barrier C02, C03 & S01 (along Lin Cheung Road) at Portion 1E
- Bridge C2 Deck 5 construction at Portion 1B and 1G
- Bridge B2 Deck 4 construction at Portion 1B and 1G
- Bridge Deck Construction at Bridge C Deck 3 and Bridge B Deck 2 in Portion 1B
- Vent. Adit Ch 175~240 at Zone 4B, 4C and A1 at Portion 1E
- Abutment Wall Construction at Slip Road E in Portion 1B
- Slip Road E in Portion 1A
- Subway Construction at Portion 1B
- Pile Cap, Pier and Upstand Wall at Segments 1 & 2 including B2P4 & C2P5 in Portion 1B
- Pile Cap, Pier and Upstand Wall at Segment 3 including B2P5 & C2P6 in Portion 1B
- Landscaped Deck at Segment 3 at Portion 1B
- Landscaped Deck at Segment 4 at Portion 1B
- Sump pit construction at Portion 1F
- Landscaped Construction at Segment 10 in Portion 1F
- Landscaped Construction at Segment 11 in Portion 1F
- Landscaped Construction at Segment 12A in Portion 1F
- Reinforced Concrete Works for Escape Route 1 and 2 in Portion 1F
- Pile Cap, Wall and Column Construction along Hoi Wang Road East side (Segments 5, 6, 7, 8 and 9) at Portion 1D
- A.3 A summary of regular construction noise and construction dust monitoring activities in this reporting period is listed below:

### Regular construction noise monitoring during normal working hours

W-N1A, W-P11, W-N18, W-N25A 5 times

**Construction dust (24-hour TSP) monitoring** 

W-A1 5 times W-A6 5 times

**Construction dust (1-hour TSP) monitoring** 

W-A1, W-A6 15 times

- A.4 Bi-weekly inspection of the implementation of landscape and visual mitigation measures was conducted on 14 and 28 December 2023. Details of the audit findings and implementation status are presented in Section 5.
- A.5 Joint weekly site inspections were conducted by representatives of the Contractor, Engineer and Contractor's ET on 7, 14, 21 and 28 December 2023. A joint site inspection with IEC was undertaken on 21 December 2023. Details of the audit findings and implementation status are presented in Section 5.
- A.6 Details of waste management are presented in Section 3.
- A.7 Three Action Levels of construction noise were triggered during the reporting month as documented complaints were received. No exceedance of Limit Level of construction noise was recorded in the reporting month. No exceedance of the Action and Limit Level of 24 hour TSP and 1 hour TSP was recorded in the reporting month.
- A.8 Three environmental complaints were received in the reporting month. After investigation with Contractor, precautionary measures had been proposed to the Contractor by ET. The interim report for the complaint is shown in Appendix Q.
- A.9 No notification of summon or prosecution was received in this reporting period.
- A.10 A summary of the construction activities provided by Main Contractor in the next reporting month is listed below:

### **Construction Activities to be undertaken**

- Remaining Socket H-Pile at Segments 5, 8b and 9 (to complete) at Portion 1B and 1D
- Noise Barrier S01 Bay 3 installation of Steel Structure, panel and Roadworks (along Lin Cheung Road) at Portion 1E
- Noise Barrier C02 Panel and Road Works in progress at Portion 1E
- Bridge Deck Construction at Bridge C2 (Deck 5) and Bridge B2 (Deck 4) in Portion 1B and 1G
- Road D Structure I Construction at Portion 1E
- Reinforced Concrete Works at Vent. Adit Ch 175~240 at Zone 4C and A1 in Portion 1E
- Backfilling works at Abutment Wall along Slip Road E in Portion 1A and 1B
- Slip Road E and F Construction in Portion 1A
- Reinforced Concrete Works for Escape Route Staircase No. 1 to 2 in Portion 1F and 10
- Reinforced Concrete Works at Staircase North Side and continue Excavation and Lateral Support works and Excavation at South Side in Portion 1B
- Upstand Wall and Column Construction at Segments 1 to 3 in Portion 1B and 1D
- Landscaped Deck Construction at Segment 3 at segment 1B
- Landscaped Deck Construction at Segment 4 (to start Roadworks) at segment 1B

### **Construction Activities to be undertaken**

- Landscaped Deck Construction at Segment 10 (Roadworks) at segment 1F
- Sump Pit construction at Segment 10 in Portion 1F
- Late Cast at OHVA and Road Works at Segment 11 in Portion 1F
- Landscaped Deck Construction at Segment 12a and to start Segment 12b in Portion 1F
- Piling Works at Segment 5, 8 and 9 (West Side) in Portion 1D

### 1. Basic Project Information

- 1.1. Central Kowloon Route (CKR) is a 4.7 km long dual 3-lane trunk road in Central Kowloon linking Yau Ma Tei Interchange in West Kowloon with the road network on Kai Tak Development and Kowloon Bay in East Kowloon.
- 1.2. The Central Kowloon Route Design and Construction Environmental Impact Assessment Report (Register No.: AEIAR-171/2013) was approved with conditions by the Environmental Protection Department (EPD) on 11 July 2013. An Environmental Permit (EP 457/2013) was issued on 9 December 2013. Variations of EP (VEP) was subsequently applied for and the latest EP (EP-457/2013/D) was issued by EPD on 15 June 2021.
- 1.3. The construction of the CKR had been divided into different sections. This Contract No. HY/2014/20 Section of Yau Ma Tei West (YMTW) covers part of the construction activities located at Yau Ma Tei under the EP which includes:
  - Section of Yau Ma Tei West
  - i. Construction of an approximately 250m long Depressed Road at the western tunnel portal of CKR;
  - ii. Construction of a Landscaped Deck structure above the western tunnel portal and Hoi Wang Road, including the associated civil engineering provisions and coordination with CKR-RMW contractor in respect of the remaining works for the Landscaped Deck;
  - iii. Construction of an underground Ventilation Adit connecting the tunnel ventilation system with the Yau Ma Tei Ventilation Building;
  - iv. Construction of approach roads and slip roads, including bridges and other associated structures, connecting CKR with the existing road networks:
    - Bridge B
    - Bridge C
    - Bridge D
    - Bridge G
    - Road D Structure
    - Box Structure E
    - Diversion of a section of existing drainage box culvert of approximately 215m in length;
  - v. Design and construction of the noise mitigation measures at Slip Roads A, C2, D, E, G, Hoi Wang Road, Lai Cheung Road and Lin Cheung Road;
  - vi. Design and construction of Smoke Ventilation System including Smoke Ventilator System including Smoke Ventilator System, Linear Heat Detection System, Pneumatic Air Supply System, the associated plant rooms, control system and power supply system for part of the Landscaped Deck;
  - vii. Design and construction of the façade system of the Landscaped Deck;
  - viii. Design and construction of lifts at the Landscaped Deck;

- ix. Associated roadworks, footpath, drainage, sewerage, watermains, street lighting, traffic aids, landscaping, electrical and mechanical works, instrument monitoring works and utility diversion works;
- x. Construction of civil engineering provisions and coordination with future tunnel E&M and TCSS contractor for installation of tunnel E&M and TCSS equipment;

The alignment and works area for the Contract No. HY/2014/20 – are shown in Appendix A.

1.4. A summary of the major construction activities undertaken in this reporting period is shown in Table 1.1. The construction programme is presented in Appendix B.

Table 1.1 Summary of the construction activities reported by Main Contractor during the Reporting Month.

### **Construction Activities undertaken**

- Socket H-Pile (Landscaped Deck and Bridges) at Portion 1B and 1D
- Noise Barrier C02, C03 & S01 (along Lin Cheung Road) at Portion 1E
- Bridge C2 Deck 5 construction at Portion 1B and 1G
- Bridge B2 Deck 4 construction at Portion 1B and 1G
- Bridge Deck Construction at Bridge C Deck 3 and Bridge B Deck 2 in Portion 1B
- Vent. Adit Ch 175~240 at Zone 4B, 4C and A1 at Portion 1E
- Abutment Wall Construction at Slip Road E in Portion 1B
- Slip Road E in Portion 1A
- Subway Construction at Portion 1B
- Pile Cap, Pier and Upstand Wall at Segments 1 & 2 including B2P4 & C2P5 in Portion 1B
- Pile Cap, Pier and Upstand Wall at Segment 3 including B2P5 & C2P6 in Portion 1B
- Landscaped Deck at Segment 3 at Portion 1B
- Landscaped Deck at Segment 4 at Portion 1B
- Sump pit construction at Portion 1F
- Landscaped Construction at Segment 10 in Portion 1F
- Landscaped Construction at Segment 11 in Portion 1F
- Landscaped Construction at Segment 12A in Portion 1F
- Reinforced Concrete Works for Escape Route 1 and 2 in Portion 1F
- Pile Cap, Wall and Column Construction along Hoi Wang Road East side (Segments 5, 6, 7, 8 and 9) at Portion 1D
- 1.5. The project organisational chart specifying management structure and contact details are shown in Appendix C.
- 1.6. A summary of the valid permits, licences, and /or notifications on environmental protection for this Project is presented in Table 1.2

Table 1.2 Summary of the Status of Valid Environmental Licence Notification, Permit and Documentations

Permit/ Licences/	Valid Period			
Notification			Status	Remark
/Reference No.	From	То	200002	
<b>Environmental Permit</b>				
EP-457/2013/D	15 Jun 2021	End of Project	Valid	-
Wastewater Discharge Li	cense			
WT00033736-2019	1 May 2020	31 May 2024	Valid	-
Notification of Constructi	on Works under	the Air Pollution	Control (Construct	on Dust) Regulation
438845	31 Oct 2018	End of Project	Notified	-
<b>Chemical Waste Produce</b>				
WPN5213-229-B2527-02	31 Oct 2018	End of Project	Valid	-
Billing Account for Dispo				1
7032430	2 Nov 2018	End of Project	Valid	-
Disposal of Special Was	ste at Landfills	Admission Tick	et	_
Nil	-	-	-	-
<b>Collection of Public Fill</b>	at Public Fill			
TM38-HY/2014/20-04	7 Jul 2023	30 Dec 2023	Valid	-
<b>Construction Noise Permi</b>	it			
			Superseded by	
GW-RE1111-23	15 Sep 2023	14 Dec 2023	GW-RE1540-23	General Site Activities
				General Site Activities
GW-RE1540-23	15 Dec 2023	14 Mar 2024	Valid	
GW-RE1198-23	10 Oct 2023	23 Dec 2023	Expired during	Remaining Works of Portal Frame Removal at
			reporting month	Lin Cheung Road (Stage 1 & 2)
GW-RE1284-23	19 Oct 2023	23 Dec 2023	Superseded by	Pasurfacing Works at Lin
OW-RE1204-23	19 Oct 2023	23 Dec 2023	GW-RE1566-23	Resurfacing Works at Lin Cheung Road Southbound
GW-RE1566-23	27 Dec 2023	24 Feb 2024	Valid	
				Portal Frame Removal at
GW-RE1468-23	28 Nov 2023	23 Feb 2024	Valid	Lin Cheung Road
				Northbound
				Drawpit Construction and
GW-RE1529-23	7 Dec 2023	9 Feb 2024	Valid	Crossroad Ducts Laying
		,		
				at Lai Cheung Road
			Expired during	Road Marking Works for
GW-RE1523-23	2 Dec 2023	30 Dec 2023	, ,	Hoi Wang Road
			reporting month	Re-alignment (Phase 3)
	–			Portal Frame Removal at
GW-RE1570-23	14 Dec 2023	24 Feb 2024	Valid	Lin Cheung Road
				Southbound
<u> </u>	l .	1		

### 2. ENVIRONMENTAL STATUS

2.1. Environmental permit (EP) conditions under the EIAO, submission status under the EP and implementation status of mitigation measures had been reviewed and implemented on schedule. The status of required submissions under the EP (EP-457/2013/D) as of the reporting period for the Project are summarised in Table 2.1.

Table 2.1 Summary of Status of Required Submission for EP-457/2013/D for the Project

EP Condition (EP-457/2013/D)	Submission	Submission date
Condition 3.4	Monthly EM&A Report (November 2023)	14 December 2023

2.2. Details of the major construction activities undertaken in this reporting period are shown in Table 2.2.

Table 2.2 Summary of the Construction Activities Undertaken during the Reporting Month.

Construction activities undertaken	Remarks on progress
• Socket H-Pile (Landscaped Deck and Bridges) at Portion 1B and	•99% completion
1D	
• Noise Barrier C02, C03 & S01 (along Lin Cheung Road) at Portion 1E	•98% completion
Bridge C2 Deck 5 Construction at Portion 1B and 1G	•50% completion
Bridge B2 Deck 4 Construction at Portion 1B and 1G	•70% completion
• Bridge Deck Construction at Bridge C Deck 3 and Bridge B Deck 2 in Portion1B	•Completed
• Vent. Adit Ch 175~240 at Zone 4B, 4C and A1 at Portion 1E	•70% completion
• Abutment Wall Construction at Slip Road E in Portion 1B	•97% completion
• Slip Road E in Portion 1A	• 90% completion
• Subway Construction (North Side) at Portion 1B	• 55% completion
• Pile Cap, Pier and Upstand Wall at Segments 1 & 2 including B2P4 & C2P5 in Portion 1B	• 85% completion
• Pile Cap, Pier and Upstand Wall at Segment 3 including B2P5 & C2P6 in Portion 1B	• 95% completion
• Landscaped Deck at Segment 3 in Portion 1B	• 50% completion
• Landscaped Deck at Segment 4 in Portion 1B	• Completed
• Sump pit construction at Portion 1F	• 45% completion
• Landscaped Construction at Segment 10 in Portion 1F	• Completed
• Landscaped Construction at Segment 11 in Portion 1F	• 25% completion
• Landscaped Construction at Segment 12A in Portion 1F	• 45% completion
• Reinforced Concrete Works for Escape Route 1 and 2 in Portion 1F	• 48% completion

Construction activities undertaken	Remarks on progress
• Pile Cap, Wall and Column Construction along Hoi Wang Road	• 97% completion
East Side(Segments 5, 6, 7, 8 and 9) at Portion 1D	

2.3. The drawing showing the project layout and the location of the monitoring station and environmental sensitive receivers are attached in Appendix A and Appendix K. Co-ordinates of the monitoring location are shown in Table 2.3.

Table 2.3 Summary of the location of the monitoring stations

<b>Monitoring Location</b>	<b>Location ID</b>	Latitude	Longitude
Yau Ma Tei Catholic Primary School (Hoi Wang Road)*	W-A1/ W-N1A	22.31345	114.16409
Man Cheong Building	W-A6	22.308185	114.166033
Hydan Place	W-N18	22.30858	114.170185
Prosperous Garden Block 1	W-N25A	22.309846	114.168072
The Coronation Tower 1	W-P11	22.309824	114.165616

Remark: \*The High Volume Sampler (HVS) at dust impact monitoring location W-A1 had been relocated on 6 Sep 2022 due to installation work of PV panel at Yau Ma Tei Catholic Primary School. The relocation of HVS was approved by ER and agreed with IEC.

### 3. MONITORING RESULTS

3.1. Monitoring Parameters

### **Air Quality**

- 3.1.1. The impact monitoring had been carried out in accordance with section 5.8 of the approved EM&A Manual to determine the 1-hour and 24-hour total suspended particulates (TSP) levels at the monitoring locations in the reporting month.
- 3.1.2. The sampling frequency of at least once in every 6 days, shall be strictly observed at the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least 3 times in every 6 days should be undertaken when the highest dust impact occurs.
- 3.1.3. General meteorological conditions (wind speed, direction and precipitation) and notes regarding any significant adjacent dust producing sources had also been recorded throughout the impact monitoring period.

### **Noise**

- 3.1.4. Construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ).  $L_{eq}$  (30min) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays.
- 3.1.5. For all other time periods, Leq (5min) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria.
- 3.1.6. As supplementary information for data auditing, statistical results such as  $L_{10}$  and  $L_{90}$  shall also be obtained for reference.
- 3.2. Monitoring Equipment

### **Air Quality**

- 3.2.1. 1-hour TSP levels and 24-hour TSP had been measured with direct reading dust meter and High Volume Samplers respectively. It has been demonstrated its capability in achieving comparable results with high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50).
- 3.2.2. The 1-hour TSP meter was calibrated by the manufacturer prior to purchasing. Zero response of the instrument was checked before and after each monitoring event. Operation of the 1-hour TSP meter followed manufacturer's Operation and Service Manual. The 24-hour TSP meter was calibrated against firmware 80570-8100-V1.0.4, annually. Operation of the 24-hour TSP meter followed manufacturer's Operation and Service Manual. Valid calibration certificates of dust monitoring equipment are attached in Appendix H.
- 3.2.3. A summary of the equipment that was deployed for the 24- hour averaged monitoring is shown in Table 3.1. The TSP monitoring was conducted as per the schedule presented in Appendix G.

3.2.4. The equipment used for 1-hour TSP and 24-hour TSP measurement and calibration are summarised in Table 3.1

	0 1 1			
Monitoring Parameter	Monitoring Equipment	Serial Number	Date of Calibration	
	LD-5R Digital Dust Indicator	0Z4545	1 Mar 2023	
1 hour TCD	LD-5R Digital Dust Indicator	992820	1 Mar 2023	
1-hour TSP	PC-3A(E) Digital Dust Indicator	JC2002225	8 Apr 2023	
	PC-3A(E) Digital Dust Indicator	JC220710222	22 Jun 2023	
24-hour TSP	TE-5170X High Volume	1084	1 Dec 2023 and	
	Sampler		14 Dec 2023	
	TE-5170X High Volume	1050	1 Dec 2023 and	
	Sampler		14 Dec 2023	
	TE-5028A Calibration Kit	3702	31 Mar 2023	

Table 3.1 Construction Dust Monitoring Equipment

### **Noise**

- 3.2.5. Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications has been used for carrying out the noise monitoring. The sound level meter has been checked using an acoustic calibrator. The wind speed and other metrological data has been recorded from Hong Kong Observatory- King's Park meteorological station, along with portable wind speed meter stand by as back up when the information are not available from HKO.
- 3.2.6. Acoustic calibrators and sound level meters using for the monitoring is within the valid period and were calibrated per year. Valid calibration certificate of noise monitoring equipment is attached in Appendix I.
- 3.2.7. The details of equipment using for monitoring are listed in Table 3.2, as below:

<b>Monitoring Equipment</b>	Serial Number	Date of Calibration
Nti XL2 Sound Level Meter	A2A-13663-F0	15 Feb 2023
Rion NC-75 Sound Level Calibrator	34724244	3 Aug 2023

Table 3.2 Monitoring Equipment Used in Monitoring

3.3. Monitoring Methodology and QA/QC results

### **Air Quality**

- 3.3.1. The 1-hour TSP monitor, portable dust meters (Sibata Digital Dust Indicator Model LD-5R and PC-3A(E) digital dust indicator) was used for the impact monitoring. The 1-hour TSP meters provides a real time 1-hour TSP measurement based on 90° light scattering. Three 1-hour TSP level were logged per every six days.
- 3.3.2. The 24-hour TSP monitor, High Volume Samplers (Tisch TE-5170X High Volume Air Sampler) were used for the impact monitoring. The 24-hour TSP monitoring consists of the following:

- ◆ The HVS was set at the monitoring location, with electricity supply connected and secured:
- ♦ HVS was calibrated before commencing the 1<sup>st</sup> measurement;
- ◆ The filter paper was weight and provided by HOKLAS lab (Acumen Laboratory and Testing Limited and ALS Technichem (HK) Pty Ltd) before and after the sampling. Certificate of HOKLAS accredited laboratory can be referred to Appendix J;
- The airflow over time during sampling process was recorded by the HVS.
- 3.3.3. HVSs was free-standing with no obstruction. The following criteria were considered in the installation of the HVS:
  - ◆ Appropriate support to secure the samples against gusty wind needed to be provided the monitoring station;
  - ◆ A minimum of 2m separation from walls, parapets and penthouses was required for rooftop samplers;
  - ♦ No furnace or incinerator flues was nearby;
  - ◆ Airflow around the sampler was unrestricted; and
  - Permission could be obtained to set up the samplers and gain access to the monitoring station.

### 3.3.4. Preparation of Filter Papers

- Glass fiber filters were labelled and sufficient filters that were clean and without pinholes were selected;
- ◆ All filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25°C and not varied by more than ±3°C; the relative humidity (RH)was 40%; and
- ◆ Acumen Laboratory and Testing Limited and ALS Technichem (HK) Pty Limited, as HOKLAS accredited laboratory, implemented comprehensive quality assurance and quality control programmes on the filters.

### 3.3.5. Field Monitoring

- The power supply was checked to ensure that the HVS was working properly;
- ◆ The filter holder and area surrounding the filter were cleaned:
- ◆ The filter holder was removed by loosening the foul bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully;
- ◆ The filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter;
- ◆ The swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges;
- The shelter lid was closed and secured with an aluminum strip;
- ◆ The HVS was warmed- up for about 5 minutes to establish run- temperature conditions;
- ◆ A new flow rate record sheet was inserted into the flow recorder;
- ◆ The flow rates of the HVS was checked and adjusted to between 0.64-1.52m³min⁻¹, which was within the range specified in the EM&A Manual (i.e. 0.6-1.7 m³min⁻¹);

- ◆ The programmable timer was set for a sampling period of 24 hours, and the starting time, weather condition and filter number were recorded;
- ◆ The initial elapsed time was recorded;
- ◆ At the end of sampling, the sampled filter was removed carefully and folded in half so that only surfaces with collected particulate matter were in contact;
- ◆ The filter paper was placed in a clean plastic envelope and sealed; all monitoring information was recorded on a standard data sheet and
- ◆ The filters were sent to (Acumen Laboratory and Testing Ltd and ALS Technichem (HK) Pty Ltd) for analysis.

### 3.3.6. Maintenance and Calibration

- ◆ The HVS and their accessories were maintained in a good working condition. For example, motor brushes were replaced routinely and electrical wiring was checked to ensure a continuous power supply; and
- ♦ The flow rate of each HVS with mass flow controller was calibrated using an orifice calibrator, Initial calibrations of the dust monitoring equipment were conducted upon installation and prior to commissioning. Five- point calibration was carried out for HVS using TE-5025 Calibration Kit. HVS is calibrated bimonthly. The calibration records for the HVS is given in Appendix H.

### 3.3.7. Wind Data Monitoring

◆ The wind speed has been recorded from Hong Kong Observatory- King's Park meteorological station, along with portable wind speed meter stand by as back up when the information are not available from HKO.

### Noise

- 3.3.8. All noise measurements by the meter were set to FAST response and on the A-weighted equivalent continuous sound pressure level (L<sub>eq</sub>) in decibels dB(A). L<sub>Aeq(30mins)</sub> was used as the monitoring metric for the time period between 0700 –1900 hours on normal weekdays. The measured noise levels were logged every 5 minutes throughout the monitoring period.
- 3.3.9. Prior to the noise measurement, the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Checking was conducted before and after the monitoring. The calibration level before and after the noise measurement is agreed to within 1.0 dB(A).
- 3.3.10. Noise measurements should not be made in presence of fog, rain, wind with a steady speed exceeding 5 ms<sup>-1</sup> or wind with gusts exceeding 10 ms<sup>-1</sup>. The wind speed was checked with a portable wind speed meter capable of measuring with speeds in ms<sup>-1</sup>.

### 3.4. Monitoring Locations

### **Air Quality**

3.4.1. During the site visit, both of the original proposed dust monitoring locations were rejected due to the condition at The Coronation was not favourable for monitoring and

the access was declined by the management office of Hong Kong Community College (HKCC) of PolyU. Two alternative air monitoring stations Yau Ma Tei Catholic Primary School (Hoi Wang Road) and Man Cheong Building had been proposed by ET and approved by IEC. 2 designated air monitoring locations were identified and agreed with IEC and EPD. Details of air monitoring stations are described in Table 3.3. The location plan of air quality monitoring stations is shown in Appendix K.

Air Quality Monitoring Station

W-A1

W-A6

Dust Monitoring
Station

Yau Ma Tei Catholic Primary School (Hoi Wang
Road)

Man Cheong Building

Table 3.3 Location of the Dust Monitoring Stations

### **Noise**

3.4.2. During the site visit, one of the original proposed noise monitoring locations Tak Cheong Building was rejected by the president of the owner's corporation. Alternative noise monitoring station Hydan place had been proposed by ET and approved by IEC. 4 noise sensitive receivers designated noise monitoring locations were identified and agreed with IEC and EPD. The designated monitoring stations are identified and access was granted by the premises. The details of noise monitoring stations are described in Table 3.4 and the location plan of noise monitoring station is shown in Appendix K.

Noise Monitoring Station	Identified Noise Monitoring Station	Type of Measurement
W-N1A	Yau Ma Tei Catholic Primary School (Hoi Wang Road)	Façade
W-N18	Hydan Place	Façade
W-N25A	Prosperous Garden Block 1	Façade
W-P11	The Coronation Tower 1	Façade

Table 3.4 Noise Monitoring Stations

- 3.5. Monitoring date, time, frequency and duration
- 3.5.1. A summary of impact monitoring duration, sampling parameter and frequency is presented in Table 3.5.

Impact Monitoring	Duration	Sampling Parameter	Frequency
Dust	1-hour continuous measurement	1-hour TSP	3 times per six days
Dust	24-hour continuous sampling	24-hour TSP	Once per six days
Noise	30-minute continuous measurement	Leq 30 min, L10 and L90 as reference.	Once per week (0700-1900)

Table 3.5 Summary of Impact Monitoring Programme

3.6. Result Summary

### **Air Quality**

3.6.1. According to our field observations, the major dust source identified at the designated air quality monitoring stations in the reporting month are summarised in Table 3.6.

Table 3.6 Observation at Dust Monitoring Stations

Monitoring Station	Major Dust Source
W-A1	Nearby traffic
W-A6	Nearby traffic

- 3.6.2. Air quality impact monitoring for the reporting month was carried out on 4, 9, 15, 21, 27 and 28 December 2023. Due to equipment malfunction, 24-hr TSP monitoring at W-A6 on 27 December 2023 has been postponed to 28 December 2023.
- 3.6.3. The results for 1-hour TSP and 24-hour TSP are summarized in Table 3.7 and Table 3.8. The measurement data and details of influencing factors such as weather conditions and site observation are presented in Appendix L.

Table 3.7 Summary of 1-hour TSP Monitoring Results

<b>Monitoring Location</b>	Range(µg/m³)	Action Level(µg/m3)	Limit Level(µg/m3)
W-A1	55 – 69	319	500
W-A6	54 – 70	306	500

Table 3.8 Summary of 24-hour TSP Monitoring Results

<b>Monitoring Location</b>	Range(µg/m³)	Action Level(μg/m3)	Limit Level(µg/m3)
W-A1	41 – 114	167	260
W-A6	52 – 120	166	260

### **Noise**

3.6.4. According to our field observations, the major noise source identified at the designated noise monitoring station in the reporting month are summarised in Table 3.9:

Table 3.5 Observation at Tyoise Monitoring Stations	
Monitoring Station	Major Noise Source
W-N1A	Nearby traffic
W-N18	Nearby traffic
W-N25A	Nearby traffic
W_P11	Nearby traffic

Table 3.9 Observation at Noise Monitoring Stations

- 3.6.5. The construction noise impact monitoring for the reporting month was carried out on 4, 9, 15, 21 and 27 December 2023.
- 3.6.6. The result for noise monitoring is summarized in Table 3.10. The measurement data are shown in Appendix M.

Table 3.10 Summary of Noise Monitoring Results

Time	Monitoring			Range, dB(A)	)		
	location	~   Parameter □	$L_{ m eq}$	$L_{10}$	L <sub>90</sub>	Action Level	Limit Level#
	W-N1A*		61.7 – 66.7	64.0 – 72.5	58.9 – 61.2		70dB(A) or 65 dB(A) during examination
Normal working hour	W-N18	T	68.4 – 70.9	71.9 – 74.7	64.3 – 66.2	When one documented	
from 0700- 1900	W-N25A	Leq 30min	65.1 – 68.9	71.4 – 72.7	58.9 – 65.1	complaint is received	75dB(A)#
	W-P11		65.4 – 68.9	70.0 – 73.0	59.3 – 65.5		

Remarks:

- 1. # If works are to be carried out during restricted hours, the conditions in the construction noise permit by the Noise Control Authority have to be followed.
- 2. \*No examination was scheduled at Yau Ma Tei Catholic Primary School during the reporting month. The limit level of W-N1A would be 70 dB(A).

### **Waste management**

3.6.7. The waste generated from this Project includes inert C&D materials, and non-inert C&D materials. Non-inert C&D materials are made up of general refuse, vegetative wastes and recyclable wastes such as plastics and paper/cardboard packaging waste. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarised in Table 3.11. Details of cumulative waste management data are presented as a waste flow table in Appendix N.

Table 3.11 Quantities of waste generated from the Project

			Q	uantity		
				Non-inert C&	D Materials	
Reporting period	Inert C&D  Materials  (in 'tonnes)	Chemical Waste (in'000 Kg)	Others, e.g. General Refuse disposed at Landfill (in 'tonnes)	Paper/card board (in '000 Kg)	Plastics (in '000 Kg)	Metals (in '000 Kg)
Dec 2023	4395.58	0.00	138.96	0.012	0.042	57.60

# 4. SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS

4.1. The Environmental Complaint Handling Procedure is shown in below Table 4.1:

Table 4.1 Environmental Complaint Handling Procedure

Complaint Received via Project Hotline	Complaint Received via 1823 or from other		
Complaint Necessed via 1 roject frotime	-		
	government departments		
Contractor notify ER, ET and IEC	ER notify Contractor, ET and IEC		
Contractor log complaint and date of receipt o	onto the complaint database. Contractor, ER and ET to		
conduct inves	stigation of complaint		
If complaint is considered not valid	If complaint is found valid		
ET or ER to reply the complainant if necessary	Contractor to identify and implement remedial		
	measures in consultation with the IEC, ET and		
	ER.		
	The ER, ET and IEC to review the effectiveness		
	of the Contractor's remedial measures and the		
	updated situation; ET to undertake additional		
	monitoring and audit to verify the situation if		
	necessary, and oversee that circumstances leading		
	to the complaint do not recur. ER to conduct		
	further inspection as necessary.		
If the complaint is referred by the EPD, the C	ontractor to prepare interim report on the status of the		
complaint investigation and follow-up actions	stipulated above, including the details of the remedial		
measures and additional monitoring identified	d or already taken, for submission to EPD within the		
	assigned by the EPD		
The ET to record the details of the second inter-	popults of the investigation subsequent estions taken to		

The ET to record the details of the complaint, results of the investigation, subsequent actions taken to address the complaint and updated situation including the effectiveness of the remedial measures, supported by regular and additional monitoring results in the monthly EM&A reports

- 4.2. Should non-compliance of the criteria occur, action in accordance with the Event and Action Plan in Appendix D and Appendix E shall be carried out.
- 4.3. Three Action Levels of construction noise were triggered during the reporting month as documented complaints were received. No exceedance of Limit Level of construction noise was recorded in the reporting month. No exceedance of the Action and Limit Level of 24 hour TSP and 1 hour TSP was recorded in the reporting month.
- 4.4. Three environmental complaints were received in the reporting month. After investigation with Contractor, precautionary measures had been proposed to the Contractor by ET. The interim report for the complaint is shown in Appendix Q.
  - 4.5. Statistics on complaints, notifications of summons and successful prosecutions are summarized in Appendix O.

### 5. EM&A SITE INSPECTION

- 5.1. Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting period, four (4) site inspections were carried out on 7, 14, 21 and 28 December 2023, along with bi-weekly inspection of the implementation of landscape and visual mitigation measures conducted on 14 and 28 December 2023.
- 5.2. A joint site inspection with IEC were undertaken on 7 and 21 December 2023. Minor deficiency was observed during weekly site inspection. Key observations during the site inspections are summarized in Table 5.1.

**Environmental Observations Follow-up Status** Date NRMM label should be provided on excavator NRMM label had been 7 December 2023 near Noise Barrier. displayed. Cement mixing platform should be covered at 1. 1. 3 sides and top dust screen had 3 sides and top at Segment 3. been provided. 14 December 2023 2. NRMM label should be displayed on air 2. NRMM label had been compressor at Landscaped Deck. displayed. 1. 1. Drip tray should be provided for chemical Chemical containers had been 21 December containers under Bridge B and near DG store.. removed or provided with drip 2023 tray. 1. Chemical containers had been 1. Drip tray should be provided for chemical 28 December 2023 containers at Segment 12. removed.

Table 5.1 Site Observations

- 5.3. The Contractor had rectified all observation identified during environmental site inspections in the reporting period.
- 5.4. According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents are implemented as much as practical during the reporting period. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in Appendix F.

### 6. FUTURE KEY ISSUES


6.1. Work to be undertaken in the next reporting month are:


### **Construction Activities to be undertaken**

- Remaining Socket H-Pile at Segments 5, 8b and 9 (to complete) at Portion 1B and 1D
- Noise Barrier S01 Bay 3 installation of Steel Structure, panel and Roadworks (along Lin Cheung Road) at Portion 1E
- Noise Barrier C02 Panel and Road Works in progress at Portion 1E
- Bridge Deck Construction at Bridge C2 (Deck 5) and Bridge B2 (Deck 4) in Portion 1B and 1G
- Road D Structure I Construction at Portion 1E
- Reinforced Concrete Works at Vent. Adit Ch 175~240 at Zone 4C and A1 in Portion 1E
- Backfilling works at Abutment Wall along Slip Road E in Portion 1A and 1B
- Slip Road E and F Construction in Portion 1A
- Reinforced Concrete Works for Escape Route Staircase No. 1 to 2 in Portion 1F and 10
- Reinforced Concrete Works at Staircase North Side and continue Excavation and Lateral Support works and Excavation at South Side in Portion 1B
- Upstand Wall and Column Construction at Segments 1 to 3 in Portion 1B and 1D
- Landscaped Deck Construction at Segment 3 at segment 1B
- Landscaped Deck Construction at Segment 4 (to start Roadworks) at segment 1B
- Landscaped Deck Construction at Segment 10 (Roadworks) at segment 1F
- Sump Pit construction at Segment 10 in Portion 1F
- Late Cast at OHVA and Road Works at Segment 11 in Portion 1F
- Landscaped Deck Construction at Segment 12a and to start Segment 12b in Portion 1F
- Piling Works at Segment 5, 8 and 9 (West Side) in Portion 1D
- 6.2. Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise and waste management.
- 6.3. The tentative schedule of regular construction noise monitoring, 1-hour TSP and 24-hour TSP monitoring in the next reporting period is presented in Appendix P.
- 6.4. The construction programme for the Project for the next reporting month is presented in Appendix B.

### 7. CONCLUSION AND RECOMMENDATIONS


- 7.1. This 59<sup>th</sup> monthly EM&A Report presents the EM&A works undertaken during the period from 1 December 2023 to 31 December 2023 in accordance with the EM&A Manual and the requirement under EP- 457/2013/D.
- 7.2. Air quality (including 1-hour TSP and 24-hour TSP) and noise impact monitoring were carried out in the reporting period.
- 7.3. Weekly environmental site inspections were conducted during the reporting period. A joint site inspection with IEC were carried out on 7 and 21 December 2023. Minor deficiency was observed during site inspection and was rectified within the specified deadlines. The environmental performance of the Project was therefore considered satisfactory.
- 7.4. Three Action Levels of construction noise were triggered during the reporting month as documented complaints were received. No exceedance of Limit Level of construction noise was recorded in the reporting month. No exceedance of the Action and Limit Level of 24 hour TSP and 1 hour TSP was recorded in the reporting month.
- 7.5. Three environmental complaints were received in the reporting month. After investigation with Contractor, precautionary measures had been proposed to the Contractor by ET. The interim report for the complaint is shown in Appendix Q.
- 7.6. The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.




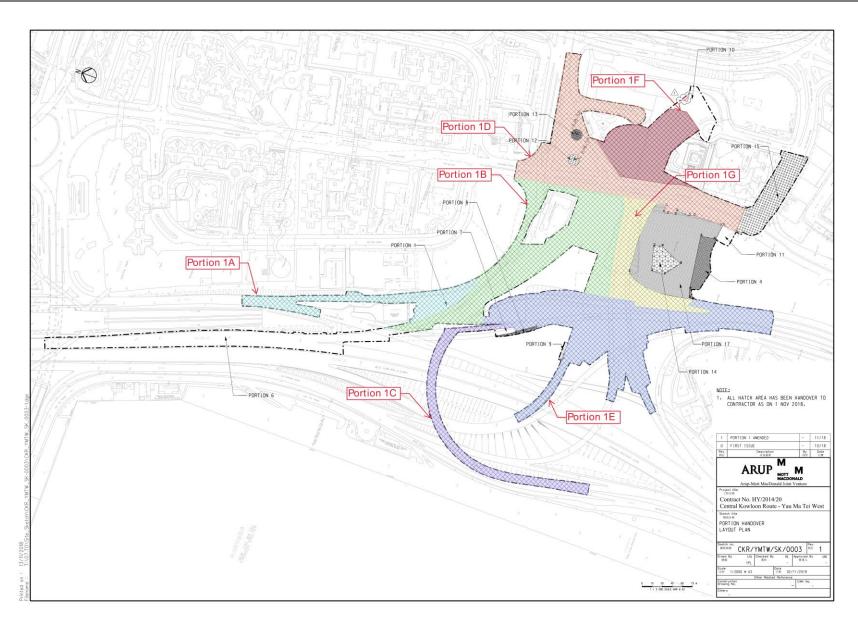




Appendix B
Construction Programme

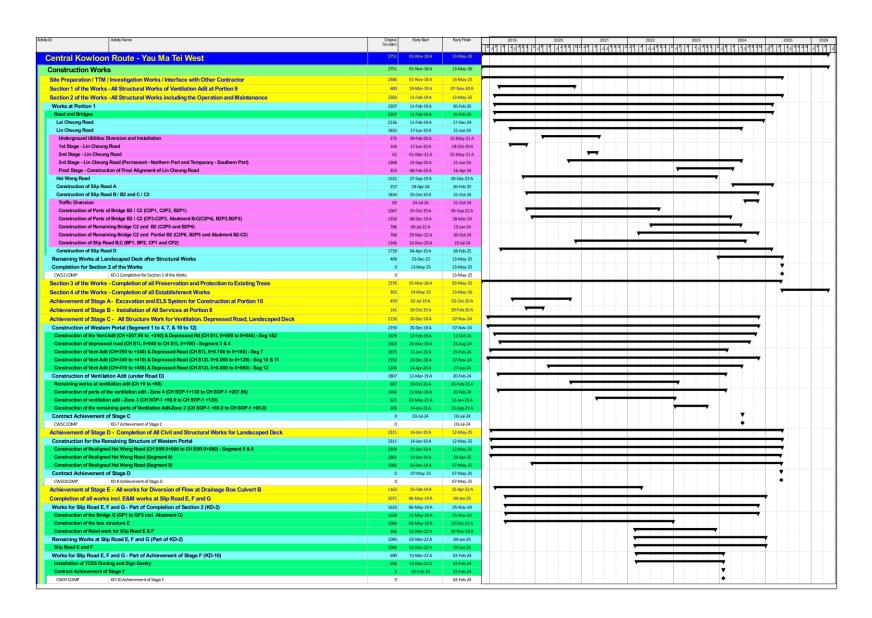


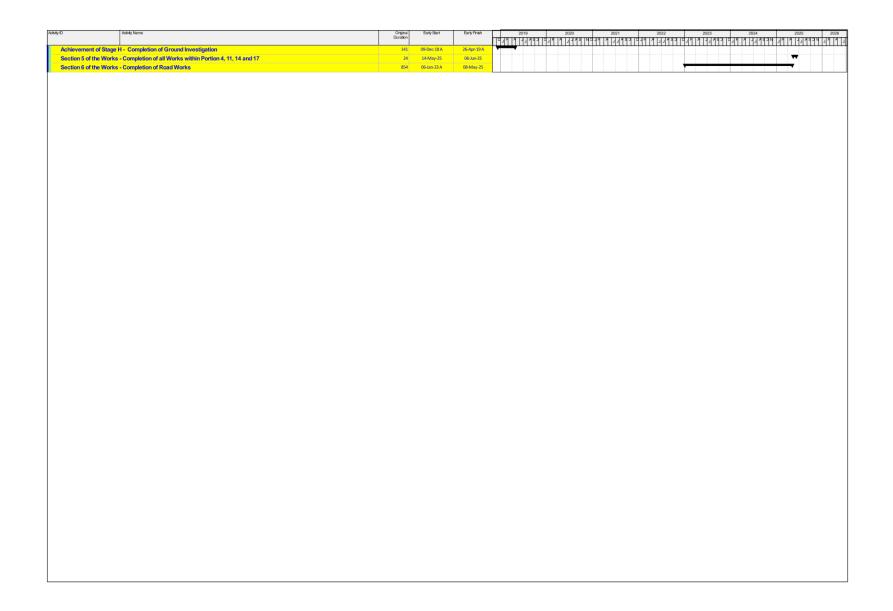

Contract No. HY/2014/20 Environmental Monitoring & Auditing
Appendix C
Project Organization Chart

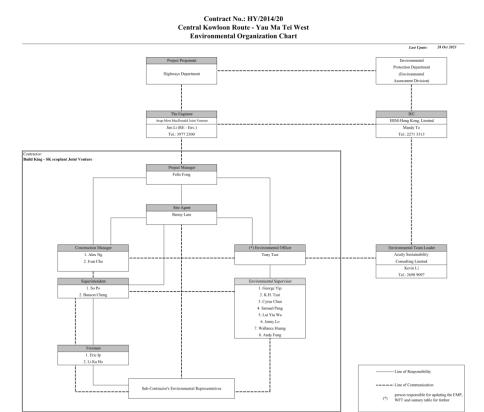

Party	Department / Company	Name of Contact Person	Position	Tel
Project Proponent	Highways Department			
The Engineer	Arup-Mott MacDonald Joint Venture	Jim Li	Resident Engineer - Environmental	3977 2300
Independent Environmental Checker	ERM-Hong Kong, Limited	Mandy To	IEC	2271 3313
Environmental Team Leader	Acuity Sustainability Consulting Limited	Kevin Li	ETL	2698 9097
Contractor	Build King - SK ecoplant Joint Venture	Felix Fong	Project Manager	3622 8300
		Benny Lam	Site Agent	3622 8300
		Alex Ng	Construction Manager	3622 8300
		Ivan Chu	Construction Manager	3622 8300
		So Po	Superintendent	9588 6977
		Banson Cheng	Superintendent	6112 8807
		Eric Ip	Foreman	9603 1445
		Li Ka Ho	Foreman	9023 9310
		Tony Tsoi	(*) Environmental Officer	9689 8956
		George Yip	Environmental Supervisor	9838 9043
		K.H. Tsui	Environmental Supervisor	9090 9052
		Cyrus Chan	Environmental Supervisor	6186 2039
		Samuel Pang	Environmental Supervisor	9876 9121
		Lai Yiu Wa	Environmental Supervisor	6997 2114
		Jenny Lo	Environmental Supervisor	6471 5156
		Wallance Huang	Environmental Supervisor	9364 1453
		Andy Fung	Environmental Supervisor	6888 4620



EVENT	ACTION							
EVENI	ET	IEC	ER	CONTRACTOR				
ACTION LEV	EL							
1.Exceedance for one sample	Identify source, investigate the causes of exceedance and propose remedial measures;     Inform IEC and ER;     Repeat measurement to confirm finding;     Increase monitoring frequency to daily.	<ol> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method.</li> </ol>	1. Notify Contractor.	<ol> <li>Rectify any unacceptable practice;</li> <li>Amend working methods if appropriate.</li> </ol>				
2.Exceedance for two or more consecutive samples	<ol> <li>Identify source;</li> <li>Inform IEC and ER;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>Repeat measurements to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Discuss with IEC and Contractor on remedial actions required;</li> <li>If exceedance continues, arrange meeting with IEC and ER;</li> <li>If exceedance stops, cease additional monitoring.</li> </ol>	<ol> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method;</li> <li>Discuss with ET and Contractor on possible remedial measures;</li> <li>Advise the ET on the effectiveness of the proposed remedial measures;</li> <li>Supervise Implementation of remedial measures.</li> </ol>	Confirm receipt of notification of failure in writing;     Notify Contractor;     Ensure remedial measures properly implemented.	<ol> <li>Submit proposals for remedial to ER within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Amend proposal if appropriate.</li> </ol>				
LIMIT LEVEL								
1.Exceedance for one sample	Identify source, investigate the causes of exceedance and propose remedial measures;     Inform ER, Contractor and	<ol> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method;</li> </ol>	Confirm receipt of     notification of failure in     writing;     Notify Contractor;	Take immediate action to avoid further exceedance;     Submit proposals for remedial actions to IEC				


EVENT	ACTION							
EVENI	ET	IEC	ER	CONTRACTOR				
	<ul> <li>EPD;</li> <li>3. Repeat measurement to confirm finding;</li> <li>4. Increase monitoring frequency to daily;</li> <li>5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.</li> </ul>	<ul><li>3. Discuss with ET and Contractor on possible remedial measures;</li><li>4. Advise the ER on the effectiveness of the proposed remedial measures;</li><li>5. Supervise implementation of remedial measures.</li></ul>	3. Ensure remedial measures properly implemented.	within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.				
2.Exceedance for two or more consecutive samples	<ol> <li>Notify IEC, ER, Contractor and EPD;</li> <li>Identify source;</li> <li>Repeat measurement to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>Arrange meeting with IEC and ER to discuss the remedial actions to be taken;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>If exceedance stops, cease additional monitoring.</li> </ol>	<ol> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>Supervise the implementation of remedial measures.</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Ensure remedial measures properly implemented;</li> <li>If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol>	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Resubmit proposals if problem still not under control;</li> <li>Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol>				

Note:

ET – Environmental Team

ER – Engineer's Representative

IEC – Independent Environmental Checker



EVEN T	ACTION								
	ET	IEC	ER	CONTRACTOR					
Action Level	<ol> <li>Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>Notify IEC and Contractor;</li> <li>Report the results of investigation to the IEC, ER and Contractor;</li> <li>Discuss with the Contractor and formulate remedial measures;</li> <li>Increase monitoring frequency to check mitigation effectiveness.</li> </ol>	<ol> <li>Review the analysed results submitted by the ET;</li> <li>Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>Supervise the implementation of remedial measures.</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>Require Contractor to propose remedial measures for the analysed noise problem;</li> <li>Ensure remedial measures are properly implemented</li> </ol>	Submit noise mitigation proposals to IEC;      Implement noise mitigation proposals.					
Limit Level	<ol> <li>Identify source;</li> <li>Inform IEC, ER, EPD and Contractor;</li> <li>Repeat measurements to confirm findings;</li> <li>Increase monitoring frequency;</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> </ol>	<ol> <li>Discuss amongst ER, ET, and         Contractor on the potential         remedial actions;</li> <li>Review Contractors remedial         actions whenever necessary to         assure their effectiveness and         advise the ER accordingly;</li> <li>Supervise the implementation of         remedial measures.</li> </ol>	<ol> <li>1.Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analysed noise problem;</li> <li>4. Ensure remedial measures properly implemented;</li> </ol>	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Resubmit proposals if problem still not under control;</li> <li>Stop the relevant portion of works as determined by the ER</li> </ol>					

EVEN T	ACTION									
	ET	IEC	ER	CONTRACTOR						
	<ul><li>6. Inform IEC, ER and EPD the causes and actions taken for the exceedances;</li><li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li></ul>		5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	until the exceedance is abated.						
	8. If exceedance stops, cease additional monitoring.									

#### Note:

ET – Environmental Team

IEC – Independent Environmental Checker

ER – Engineer's Representative

Contract No. HY/2014/20
Environmental Monitoring & Auditing

Appendix F
Environmental Mitigation Implementation
Schedule (EMIS)

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/or standards to be achieved	Implementation Status
		Cor	nstruction Dust Im	pact				
\$4.3.10	D1	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	APCO     To control the dust impact     To meet     HKAQO and     TM-EIA     criteria	Implemented, deficiency rectified after observation
S4.3.10	D2	Mitigation measures in form of regular watering under a good site practice should be adopted. Watering once per hour on exposed worksites and haul road should be conducted to achieve dust removal efficiencies of 91.7%. While the above watering frequencies are to be followed, the extent of watering may vary depending on actual site conditions but should be sufficient to maintain an equivalent intensity of no less than 1.3 L/m² to achieve the dust removal efficiency.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	APCO     To control the dust impact     To meet     HKAQO and     TM-EIA     criteria	• Implemented
S4.3.10		<ul> <li>Proper watering at exposed spoil should be undertaken throughout the construction phase;</li> <li>Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading;</li> <li>Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads;</li> <li>A stockpile of dusty material should not be extended</li> </ul>	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	APCO     To control the dust impact     To meet     HKAQO and     TM-EIA     criteria	Implemented, deficiency rectified after observation

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		beyond the pedestrian barriers, fencing or traffic cones;  The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle.  Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;  When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided and properly maintained as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period;  The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials;  Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously;						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status	
\$4.3.10	D6	sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet;  Any skip hoist for material transport should be totally enclosed by impervious sheeting;  Every stock of more than 20 bags of cement or dry-pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides;  Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system  Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabilizer within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.  Implement regular dust monitoring under EM&A	Monitoring of	Contractor	Selected rep.	Construction stage	• TM-EIA	• Implemented	
		programme during the construction stage.	dust impact		dust monitoring station			·	
	Construction Noise (Airborne)								

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
S5.4.1	N1	<ul> <li>Implement the following good site practices:</li> <li>Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme;</li> <li>Machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;</li> <li>Plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs;</li> <li>Silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works;</li> <li>Mobile plant should be sited as far away from NSRs as possible and practicable;</li> <li>Material stockpiles, mobile container site office and other structures should be effectively utilized, where practicable, to screen noise from on-site construction activities.</li> </ul>	Control construction airborne noise	Contractor	All construction sites	Construction stage	• Annex 5, TM-EIAO	• Implemented
\$5.4.1	N2	Install temporary hoarding located on the site boundaries between noisy construction activities and NSRs. The conditions of hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level zone of NSRs through partial screening	Contractor	All construction sites	Construction stage	• Annex 5, TM-EIAO	Implemented
S5.4.1	N3	Install movable noise barriers (typical design is wooden framed barrier with a small-cantilevered on a skid footing with 25mm thick internal sound absorptive lining), acoustic mat or full enclosure,	Sreen the noisy plant items to be used at all construction	Contractor	All construction sites where practicable	Construction stage	• Annex 5, TM-EIAO	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/or standards to be achieved	Implementation Status
		screen the noisy plants including air compressors, generators and handheld breakers, etc.	sites					
S5.4.1	N4	Use 'Quiet plant'	Reduce the noise levels of plant items	Contractor	All construction sites where practicable	Construction stage	Annex 5,     TM-EIAO	Implemented
S5.4.1	N5	Loading/ unloading activities should be carried out inside the full enclosure of mucking out points.	Reduce the noise levels of loading/ unloading activities	Contractor	Mucking out locations	Construction stage	Annex 5,     TM-EIAO	Implemented
\$5.4.1	N6	Sequencing operation of construction plants where practicable.	Operate sequentially within the same work site to reduce the construction airborne noise	Contractor	All construction sites where practicable	Construction stage	• Annex 5, TM-EIAO	Implemented
\$5.4.1	N7	Implement a noise monitoring programme under EM&A programme.	Monitor the construction noise levels at the selected representative locations	Contractor	Selected rep. noise monitoring station	Construction stage	• TM-EIAO	Implemented
		Water C	Quality (Construction	on Phase)				
\$6.9.1.1		In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN1/94), construction phase mitigation measures shall include	To minimize water quality impact from the construction site	Contractor	All construction sites where practicable	Construction stage	Water     Pollution     Control     Ordinance	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		<ul> <li>Construction Runoff</li> <li>At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the contractor prior to the commencement of construction;</li> <li>The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/ sediment trap. The sediment/ silt traps should be incorporated in the permanent drainage channels to enhance deposition rates;</li> <li>The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt/ sand traps should be 5 minutes under maximum flow conditions. Sizes may vary depending upon the flow rate, but for a flow rate of 0.1 m³/s a sedimentation basin of 30 m³ would be required and for a flow rate of 0.5 m³/s the</li> </ul>	runoff and general construction activities				• ProPECC PN 1/94 • TM-EIAO • TM-DSS	

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		<ul> <li>basin would be 150 m³. The detailed design of the sand/ silt traps shall be undertaken by the contractor prior to the commencement of construction;</li> <li>All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. Exposed slope surfaces should be covered by tarpaulin or other means;</li> <li>The overall slope of the site should be kept to a minimum to reduce the erosive potential of surface water flows, and all traffic areas and access roads protected by coarse stone ballast. An additional advantage accruing from the use of crushed stone is the positive traction gained during prolonged periods of inclement weather and the reduction of surface sheet flows;</li> <li>All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas;</li> <li>Measures should be taken to minimize the ingress of site drainage into excavations. If the excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from</li> </ul>						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		trenches or foundation excavations should be discharged into storm drains via silt removal facilities;  Open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50m³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system;  Manholes should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers;  Precautions be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes;  All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and site wheel washing facilities should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel wash bay to the public road should be paved with sufficient backfall toward the wheel wash bay to prevent vehicle tracking of soil and silty water to public roads and drains;  Oil interceptors should be provided in the drainage system downstream of any oil/ fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain;  Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts;  All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby;  Adopt best management practices;  All earth works should be conducted sequentially to limit the amount of construction runoff generated from exposed areas during the wet season (April to December) as far as practicable.						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
S6.9.1.2		<ul> <li>Cut-&amp;-cover tunneling work should be conducted sequentially to limit the amount of construction runoff generated from exposed areas during the wet season (April to December) as far as practicable.</li> <li>Uncontaminated discharge should pass through sedimentation tanks prior to off-site discharge;</li> <li>The wastewater with a high concentration of SS should be treated (e.g. by sedimentation tanks with sufficient retention time) before discharge. Oil interceptors would also be required to remove the oil, lubricants and grease from the wastewater;</li> <li>Direct discharge of the bentonite slurry (as a result of D-wall) is not allowed. It should be reconditioned and reused wherever practicable. Temporary storage locations (typically a properly closed warehouse) should be provided on site for any unused bentonite that needs to be transported away after all the related construction activities area completed. The requirements in ProPECC PN 1/94 should be adhered to in the handling and disposal of bentonite slurries.</li> </ul>	To minimize construction water quality impact from tunneling works	Contractor	All tunneling portion	Construction stage	<ul> <li>Water         Pollution         Control         Ordinance</li> <li>ProPECC PN         1/94</li> <li>TM-DSS</li> <li>TM-EIAO</li> </ul>	• N/A
\$6.9.1.3	W3	Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide	To minimize water quality from sewage effluent	Contractor	All construction sites where practicable	Construction stage	Water     Pollution     Control     Ordinance     TM-DSS	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.						
\$6.9.1.5	W4	<ul> <li>No direct discharge of groundwater from contaminated areas should be adopted.</li> <li>A discharge license under the WPCO through the Regional Office of EPD for groundwater discharge should be applied. Prior to the excavation works within these potentially contaminated areas, the groundwater quality should be reviewed during the process of discharge license application. The compliance to the Technical Memorandum on Standards for Effluents Discharged into Drainage on Sewerage Systems, Inland and Coastal Waters (TM-DSS) and the existence of prohibited substance should be confirmed. If the review results indicated that the groundwater to be generated from the excavation works would be contaminated, the contaminated groundwater should be either properly treated in compliance with the requirements of the TM-DSS or properly recharged into the ground.</li> <li>If wastewater treatment is deployed, the wastewater treatment unit shall deploy suitable treatment process (e.g. oil interceptor / activated carbon) to reduce the pollution level to an</li> </ul>	To minimize groundwater quality impact from contaminated area	Contractor	Excavation areas where contamination is found	Construction stage	Water     Pollution     Control     Ordinance     TM-DSS     TM-EIAO	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		acceptable standard and remove any prohibited substances (e.g. TPH) to undetectable range. All treated effluent from wastewater treatment plant shall meet the requirements as stated in TM-DSS and should be discharged into the foul sewers.  • If groundwater recharging wells are deployed, recharging wells should be installed as appropriate for recharging the contaminated groundwater back into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in the Section 2.3 of TM-DSS. The baseline groundwater quality shall be determined prior to the selection of the recharge wells, and submit a working plan (including the laboratory analytical results showing the quality of groundwater at the proposed recharge location(s) as well as the pollutant levels of groundwater to be recharged) to EPD for agreement. Pollution levels of groundwater to be recharged shall not be higher than pollutant levels of ambient groundwater at the recharge well. Prior to recharge, any prohibited substances such as TPH products should be removed as necessary by installing the petrol interceptor.						
S6.9.1.6	W6	Accidental Spillage  In order to prevent accidental spillage of chemicals, the following is recommended:	To minimize water quality impact from accidental	Contractor	All construction site where practicable	Construction stage	Water     Pollution     Control     Ordinance	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/or standards to be achieved	Implementation Status
		<ul> <li>All the tanks, containers, storage area should be bunded and the locations should be locked as far as possible from the sensitive watercourse and stormwater drains;</li> <li>The Contractor should register as a chemical waste producer if chemical wastes would be generated. Storage of chemical waste arising from the construction activities should be stored with suitable labels and warnings.</li> <li>Disposal of chemical wastes should be conducted in compliance with the requirements as stated in the Waste Disposal (Chemical Waste) (General)</li> </ul>	spillage				• ProPECC PN 1/94 • TM-EIAO • TM-DSS	
		Regulation. Waste Man	  agement (Constru	 uction Waste)				
S7.4.1	WM1	On-site sorting of C&D material  Geological assessment should be carried out by competent persons on site during excavation to identify materials which are not suitable to use as aggregate in structural concrete (e.g. volcanic rock, Aplite dyke rock, etc.). Volcanic rock and Aplite dyke rock should be separated at the source sites as far as practicable and stored at designated stockpile area preventing them from delivering to crushing facilities. The crushing plant operator should also be reminded to set up measures to prevent unsuitable rock from ending up at concrete batching plants and be turned into concrete for	Separation of unsuitable rock from ending up at concrete batching plants and be turned into concrete for structural use	Contractor	All construction sites	Construction stage	• DEVB (W) No. 6/2010	• N/A

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
\$7.5.1	WM2	structural use. Details regarding control measures at source site and crushing facilities should be submitted by the Contractor for the Engineer to review and agree. In addition, site records should also be kept for the types of rock materials excavated and the traceability of delivery will be ensured with the implementation of Trip Ticket System and enforced by site supervisory staff as stipulated under DEVB TC(W) No. 6/2010 for tracking of the correct delivery to the rock crushing facilities for processing into aggregates. Alternative disposal option for the reuse of volcanic rock and Aplite Dyke rock, etc. should be explored.  Construction and Demolition Material  Maintain temporary stockpiles and reuse excavated	Good site practice to	Contractor	All construction	Construction stage	• Land (Miscellaneo	• Implemented
		fill material for backfilling and reinstatement;  Carry out on-site sorting;  Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate;  Adopt 'selective demolition' technique to demolish the existing structures and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible;  Implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified; and  Implement an enhanced Waste Management Plan	minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal		sites		us Provisions) Ordinance  • Waste Disposal Ordinance  • ETWB TCW No. 19/2005	

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		similar to ETWBTC (Works) No. 19/2005 — "Environmental Management on Construction Sites" to encourage on-site sorting of C&D materials and to minimize their generation during the course of construction.						
\$7.5.1	WM3	<ul> <li>Standard formwork or pre-fabrication should be used as far as practicable in order to minimize the arising of C&amp;D materials. The use of more durable formwork or plastic facing for the construction works should be considered. Use of wooden hoardings should not be used, as in other projects. Metal hoarding should be used to enhance the possibility of recycling. The purchasing of construction materials will be carefully planned in order to avoid over ordering and wastage;</li> <li>The Contractor should recycle as much of the C&amp;D materials as possible on-site. Public fill and C&amp;D waste should be segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal. Where practicable, concrete and masonry can be crushed and used as fill. Steel reinforcement bar can be used by scrap steel mills. Different areas of the sites should be considered for such segregation and storage.</li> </ul>	Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction stage	Land     (Miscellaneo     us Provisions)     Ordinance     Waste     Disposal     Ordinance     ETWB TCW     No. 19/2005	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
\$7.5.1	WM5	<ul> <li>All construction plant and equipment shall be designed and maintained to minimize the risk of silt, sediments, contaminants or other pollutants being released into the water column or deposited in the locations other than designated location;</li> <li>All vessels shall be sized such that adequate draft is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash;</li> <li>Before moving the vessels which are used for transporting dredged material, excess material shall be cleaned from the decks and exposed fittings of vessels and the excess materials shall never be dumped into the sea except at the approved locations;</li> <li>Adequate freeboard shall be maintained on barges to ensure that decks are not washed by wave action.</li> <li>The Contractors shall monitor all vessels transporting material to ensure that no dumping outside the approved location takes place. The Contractor shall keep and produce logs and other records to demonstrate compliance and that journeys are consistent with designated locations and copies of such records shall be submitted to the engineers;</li> <li>The Contractors shall comply with the conditions in the dumping licence.</li> </ul>	To control pollution due to marine sediment	Contractor	Along CKR alignment	Construction stage	• ETWB TCW No. 34/2002	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		<ul> <li>All bottom dumping vessels (Hopper barges) shall be fitted with tight fittings seals to their bottom openings to prevent leakage of material;</li> <li>The material shall be placed into the disposal pit by bottom dumping;</li> <li>Contaminated marine mud shall be transported by spit barge of not less than 750m3 capacity and capable of rapid opening and discharge at the disposal site;</li> <li>Discharge shall be undertaken rapidly and the hoppers shall be closed immediately. Material adhering to the sides of the hopper shall not be washed out of the hopper and the hopper shall remain closed until the barge returns to the disposal site.</li> <li>For Type 3 special disposal treatment, sealing of contaminant with geosynthetic containment before dropping designated mud pit would be a possible arrangement. A geosynthetic containment method is a method whereby the sediments are sealed in geosynthetic containers and, the containers would be dropped into the designated contaminated mud pit where they would be covered by further mud disposal and later by the mud pit capping at the disposal site, thereby fulfilling the requirements for fully confined mud disposal.</li> </ul>						
S7.5.1	WM6	Chemical Waste     Chemical waste that is produced, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, should be handled in	Control the chemical waste and ensure proper storage,	Contractor	All construction sites	Construction stage	Waste     Disposal     (Chemical     Waste)	<ul> <li>Implemented, deficiency rectified after observation</li> </ul>

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		<ul> <li>accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes;</li> <li>Containers used for the storage of chemical wastes should be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed, have a capacity of less than 450 L unless the specification has been approved by EPD, and display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the regulation;</li> <li>The storage area for chemical wastes should be clearly labelled and used solely for the storage of chemical waste, enclosed on at least 3 sides, have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20% of the total volume of waste stored in that area, whichever is the greatest, have adequate ventilation, covered to prevent rainfall entering, and arranged so that incompatible materials are adequately separated;</li> <li>Disposal of chemical waste should be via a licensed waste collector, be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Centre which also offers a chemical waste collection service and can supply the necessary storage containers, or be to a reuser of the waste, under approval from EPD.</li> </ul>	handling and disposal				(General) Regulation  Code of Practice on the Packaging, Labelling and Storage of Chemical Waste	

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
S7.5.1	WM7	<ul> <li>General Refuse</li> <li>General refuse generated on-site should be stored in enclosed bins or compaction units separately from construction and chemical wastes;</li> <li>A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law.</li> <li>Aluminum cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. Separate labelled bins for their deposit should be provided if feasible;</li> <li>Office wastes can be reduced through the recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme should be considered by the Contractor.</li> </ul>	Minimize production of the general refuse and avoid odour, pest and litter impacts	Contractor	All construction sites	Construction stage	Waste     Disposal     Ordinance	Implemented, deficiency rectified after reminder
	ı	,	Land Contamin	ation	l			
S8.9 & Appendix 8.4	LC2	Prior to commencement of the excavation works at the contamination zone, the zone should be clearly marked out on site and the surface levels recorded. Excavation of contaminated material should be undertaken using dedicated earth-moving plant.      The excavated contaminated soils would be stockpiled at designated area on site and covered by sheet to prevent dispersion of contamination	The contaminated soil will be excavated for on-site reuse	Contractor	РВН4	Prior to commencement of construction works within the contaminated area	• Practice Guide (PG) for Investigation and Remediation of Contaminate d Land	Implemented

EIA Ref.	EM&A Log Ref.	Recomm	Recommended Mitigation Measures		Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
S8.9 &	LC3	selection of schemes and table is higher excavation. TI valid Water F discharge licer	sor should pay suitable ground discharge points or than the containe Contractor should be from EPD when						<ul> <li>Guidance         Notes for             Contaminate             d Land             Assessment             and             Remediation     </li> <li>Guidance             Manual for</li> </ul>	• Implemented
Appendix 8.4		Following completion of the excavation to the specified depth, at least one sample from the base of the excavation and four samples evenly distributed along the boundary of the excavation shall be taken for a closure assessment testing. The acceptance criterion is shown below:							Use of Risk-Based Remediation Goals (RBRGs) for Contaminate	mplemented
		Locations Testing Acceptance requirement Criteria  PBH4 PCBs RBRGs (Public Park)  • If the results of analysis below the RBRGs (Public Park), no further excavation will be required.  If the analysis indicates presence of contamination (i.e. noncompliance of the acceptance criteria), further excavation shall be carried out in 0.5m increment vertically and/or horizontally depending on the location(s) of the sample(s) which has exceeded the acceptance criteria. Further sampling shall also be conducted for compliance testing. The process of						d Land Management		


EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		excavation, sampling and compliance testing should continue until all contaminated materials are removed and should be supervised by a Land Contamination Specialist.						
Appendix 8.4	LC4	• A Remediation Report (RR) to demonstrate adequate clean-up shall be prepared and submitted to EPD for endorsement prior to the commencement of any construction/development works within the sites. No construction/development works shall be carried out prior to the endorsement of the RR by EPD.						Implemented
			Hazard to Li	fe				
\$9.18	H8	The driver and his assistant should be physically healthy, experienced and have good safe driving records. The driver should hold a proper driving licence for the approved transport truck. Dedicated training programme and regular road safety briefing sessions/ workshops should be provided to enhance their safe driving attitude and practice. Smoking should be strictly prohibited.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A
S9.18	Н9	Emergency response plans in case of road accident should be prepared and implemented. The driver and his assistant should be familiar with the emergency procedures including evacuation, and proper communication/ fire-fighting equipment should be provided to the driver and his assistant.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A
			Landscape & V	'isual				

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
S10.10.1 Table 10.11	LV3	<ul> <li>Good Site Management</li> <li>Large temporary stockpiles of excavated material shall be covered with unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance.</li> <li>Construction plant and building material shall be orderly and carefully stored in order to create a neat and tidy visual appearance.</li> </ul>	Minimize visual impact	Contractor	Within Project site	Construction stage	-	Implemented
S10.10.1 Table 10.11	LV4	<ul> <li>Screen Hoarding</li> <li>Decorative screen hoarding should be erected to screen the public from the construction area. It should be designed to be compatible with the existing urban context.</li> </ul>	Minimize visual impact	Contractor	Within Project site	Construction stage	-	Implemented
S10.10.1 Table 10.11	LV5	Lighting Control during Construction  • All lighting in the construction site shall be carefully controlled to minimize light pollution and night-time glare to nearby residencies and GIC. The Contractor shall consider other security measures, which shall minimize the visual impacts.	Minimize visual impact	Contractor	Within Project site	Construction stage	-	Implemented
S10.10.1 Table 10.11	LV6	The potential for soil erosion shall be reduced by minimizing the extent of vegetation disturbance on site and by providing a protective cover over newly exposed soil.	Minimize landscape impact	Contractor	Within Project site	Construction stage	-	• N/A
S10.10.1 Table 10.11	LV7	Tree Protection & Preservation  ■ Carefully protected during construction. Tree protection measures will be detailed at the Tree Removal Application stage and plans submitted to the relevant Government Department for approval	Minimize landscape and visual impact	Contractor	Within Project site	Construction stage	<ul> <li>'Guidelines for Tree Risk Management and Assessment</li> </ul>	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		in due course in accordance with ETWB TC no. 3/2006.					Arrangement on an Area Basis and on a Tree Basis', Greening, Landscape and Tree Management (GLTM) Section, DEVB  Latest recommende d horticultural practices from GLTM Section, DEVB	
S10.10.1 Table 10.11	LV8	Tree Transplantation  • For trees unavoidably affected by the Project that have to be removed, where practical transplantation will be chosen as the top priority method of removal. If this is not possible or practical compensatory planting will be provided for trees unavoidably felled (See LV10). For trees unavoidably affected by the Project works that are transplanted, transplantation must be carried out in accordance with ETWB TCW 2/2004 and 3/2006.	Minimize landscape and visual impact	Contractor	Within Project site and designated off-site locations	Prior to Construction stage	ETWB TCW 3/2006      Latest recommende d horticultural practices from Greening, Landscape and Tree	• Implemented

S10.10.1 Table 10.11  Section, DEVB  For trees unavoidably affected by the Project that have to be removed, where practical transportation will be chosen as the top priority method of removal but if this is not possible or practical compensatory planting will be provided for trees unavoidably felled. All felled trees shall be compensated for by planting trees to the satisfaction of relevant Government projects. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBET (3/2006.  Compensatory tree planting may be incorporated into public open spaces and along roadside amenity areas affected by the construction works and therefore be part of the bigger wider planting plans. Onsite compensation planting is preferred but if necessary, additional receptor sites outside the Works Area shall be agreed separately with Government during the Tree Felling Application process.  Cultural Heritage Impact (Construction Phase)	EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
Table 10.11  • For trees unavoidably affected by the Project that have to be removed, where practical transportation will be chosen as the top priority method of removal but if this is not possible or practical compensatory planting will be provided for trees unavoidably felled. All felled trees shall be compensated for by planting trees to the satisfaction of relevant Government projects. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006.  • Compensatory tree planting may be incorporated into public open spaces and along roadside amenity areas affected by the construction works and therefore be part of the bigger wider planting plans. Onsite compensation planting is preferred but if necessary, additional receptor sites outside the Works Area shall be agreed separately with Government during the Tree Felling Application process.								(GLTM) Section, DEVB • ETWB TCW	
	Table	LV9	<ul> <li>For trees unavoidably affected by the Project that have to be removed, where practical transportation will be chosen as the top priority method of removal but if this is not possible or practical compensatory planting will be provided for trees unavoidably felled. All felled trees shall be compensated for by planting trees to the satisfaction of relevant Government projects. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006.</li> <li>Compensatory tree planting may be incorporated into public open spaces and along roadside amenity areas affected by the construction works and therefore be part of the bigger wider planting plans. Onsite compensation planting is preferred but if necessary, additional receptor sites outside the Works Area shall be agreed separately with Government during the Tree Felling Application process.</li> </ul>	impact and also enhance landscape		,	Construction stage	ETWB TCW     3/2006     Latest     recommende     d     horticultural     practices     from     Greening,     Landscape     and Tree     Management     (GLTM)     Section,     DEVB     ETWB TCW	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
S11.4.4	CH1	The contractor should be alerted during the construction on the possibility of locating archaeological remains and as a precautionary measure, AMO shall be informed immediately in case of discovery of antiquities or supposed antiquities in the subject sites.	To preserve any cultural heritage items which may be removed and damaged by the excavation	Contractor	During construction works for cut and cover tunnels	Construction stage	AMOs requirements	• N/A
			EM&A Proje	ct				
S13.2	EM1	An Independent Environmental Checker needs to be employed as per the EM&A Manual	Control EM&A Performance	Highways Department	All construction sites	Construction stage	• EIAO Guidance Note No. 4/2010 • TM-EIAO	Implemented
S13.2-13.4	EM2	<ul> <li>An Environmental Team needs to be employed as per the EM&amp;A Manual;</li> <li>Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures;</li> <li>An environmental impact monitoring needs to be implemented by the Environmental Team to ensure all the requirements given in the EM&amp;A Manual are fully complied with.</li> </ul>	Perform environmental monitoring & auditing	Highways Department/ Contractor	All construction sites	Construction stage	• EIAO Guidance Note No. 4/2010 • TM-EIAO	Implemented



		Impa	ct Monitoring Schedule for '	YMTW		
			Dec-23			
Sun	Mon	Tue	Wed	Thu	Fri	Sat
					1	2
3	4 Impact	5	6	7	8	9 Impact
	1					
	Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A,					Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A,
	W-P11,W-N18 & W-N25A					W-P11,W-N18 & W-N25A
10	11	12	13	14	15	16
					Impact	
					Air monitoring for W-A6 &W-A1	
					Noise monitoring for W-N1A,	
					W-P11,W-N18 & W-N25A	
17	18	19	20	21	22	23
				Impact		
				Air monitoring for W-A6 &W-A1		
				Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A		
24	25	26	27	28	29	30
	23		Impact	Impact		
			Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A,	24-hr TSP monitoring for W-A6		
			W-P11,W-N18 & W-N25A			
31						
	1999 1999 1999 1999 1999 1999 1999 1999					
	AND THE RESERVE OF THE PERSON					
	100 100 100 100 100 100 100 100 100 100					
	100 100 100 100 100 100 100 100 100 100					

Contract No. HY/2014/20
Environmental Monitoring & Auditing

Appendix H
Calibration Certificates
(Air Monitoring)





#### Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

#### Information of Calibrated Equipement

		to	2-Mar-23	Next Verification Test Date:	1-Mar-24
Unit-under-Test- Model No.:		Sibata LD-5R			
Unit-under-Test Serial No.:		0Z4545			
Our Report Refrence No.:	RF	PT-23-HVS-0002	2		
Calibration Location:			E	max	

#### Standard Equipment Information


Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5025A
Equipment serial no.:	1086	3465
Last Calibration Date:	1-Mar-23	28-Jun-22
Next Calibration Date:	30-Apr-23	27-Jun-23

#### **Equipement Vertification Result**

Verification		Duration			Results from	Calibrated Equipement	Results from Standard Equipment	
Test No.	Date	Start-time	t-time End-time Elapsed Time (in min)		Total Counts	Counts/ Minute x-axis	Dust Concentration (μg/m³) y-axis	
1	1/3/2023	5013.27	5016.34	184.20	4851	26	78	
2	1/3/2023	5016.34	5019.34	180.00	6000	33	96	
3	1/3/2023	5019.34	5022.34	180.00	7740	43	129	
4	2/3/2023	5022.34	5025.34	180.00	3840	21	62	
5	2/3/2023	5025.34	5028.34	180.00	2400	13	38	
6	2/3/2023	5028.34	5031.34	180.00	3420	19	55	

#### Linear Regression of y on x





Operated By:

Andy Li Project Technician, Environmental

Date: 01-03-2023

Checked By:

Tandy Tse
Senior Consultant, Environmental

Date: 01-03-2023





#### Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

#### Information of Calibrated Equipement

Verification Test Date:	1-Mar-23	to	2-Mar-23	Next Verification Test Date:	1-Mar-24
Unit-under-Test- Model No.:		Sibata LD-5R			
Unit-under-Test Serial No.:		992820			
Our Report Refrence No.:	R	PT-23-HVS-000	1		
Calibration Location:			E	max	

#### Standard Equipment Information


	Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
1	Standard Equipment Model No.:	TE-5170X	TE-5025A
1	Equipment serial no.:	1086	3465
1	Last Calibration Date:	1-Mar-23	28-Jun-22
	Next Calibration Date:	30-Apr-23	27-Jun-23

Equipement Vertification Result

Equipement Vertification Result										
Verification	Date	Duration		Results from Calibrated Equipement		Results from Standard Equipment				
Test No.		Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration (μg/m³) y-axis			
1	1/3/2023	5013.27	5016.34	184.20	4728	26	78			
2	1/3/2023	5016.34	5019.34	180.00	5760	32	96			
3	1/3/2023	5019.34	5022.34	180.00	7800	43	129			
4	2/3/2023	5022.34	5025.34	180.00	3780	21	62			
5	2/3/2023	5025.34	5028.34	180.00	2280	13	38			
6	2/3/2023	5028.34	5031.34	180.00	3300	18	55			

#### Linear Regression of y on x





Operated By:

Andy Li
Project Technician, Environmental

Date: 01-03-2023

Checked By:

Tandy Tse
Senior Consultant, Environmental

Date: 01-03-2023





# PC-3A(E) K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Verification Test Date:	8-Apr-23	to	9-Apr-23	Next Verification Test Date:	8-Apr-24
Unit-under-Test- Model No.:		PC-3A(E)		•	
Unit-under-Test Serial No.:		JC-2002225		•	
Our Report Refrence No.:	R	PT-23-HVS-0029	9	•	
Calibration Location:			-	- Emax	
-					-

#### Standard Equipment Information


Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5028A
Equipment serial no.:	1049	3702
Last Calibration Date:	8-Apr-23	31-Mar-23
Next Calibration Date:	7-Jun-23	30-Mar-24

#### **Equipement Vertification Result**

				Equipernent	vertification it	Court	
Verification			Duration		Results from	Calibrated Equipement	Results from Standard Equipment
Test No.	Date	Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration (μg/m³) y-axis
1	8/4/2023	7339.85	7342.85	180.00	2580	14	44
2	8/4/2023	7342.85	7345.85	180.00	2220	12	36
3	8/4/2023	7345.85	7348.85	180.00	6000	33	97
4	9/4/2023	7349.74	7352.74	180.00	1440	8	29
5	9/4/2023	7352.76	7355.76	180.00	1980	11	31
6	9/4/2023	7355.77	7358.77	180.00	6000	33	102

# Linear Regression of y on x





Operated By:

Andy Li
Project Technician, Environmental

Date: 10-04-2023

Checked By:

Tandy Tse

Senior Consultant, Environmental

Date: 10-04-2023





# Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Verification Test Date:	22-Jun-23	to	25-Jun-23	Next Verification Test Date:	22-Jun-24
Unit-under-Test- Model No.:		PC-3A(E)			
Unit-under-Test Serial No.:		JC-22071022	2	-	
Our Report Refrence No.:	R	PT-23-HVS-00	153	-	
Calibration Location:				- Emax	
-					-

#### Standard Equipment Information


	otaliaala Equipilient iii	
Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5028A
Equipment serial no.:	1049	3702
Last Calibration Date:	22-Jun-23	31-Mar-23
Next Calibration Date:	21-Aug-23	30-Mar-24

#### **Equipement Vertification Result**

				Equipernent	vertification it	court	
Verification			Duration		Results from	Calibrated Equipement	Results from Standard Equipment
Test No.	Date	Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration (μg/m³) y-axis
1	22/6/2023	7339.85	7342.85	180.00	2700	15	15
2	22/6/2023	7342.85	7345.85	180.00	2820	16	15
3	22/6/2023	7345.85	7348.85	180.00	4740	26	26
4	25/6/2023	7349.74	7352.74	180.00	2160	12	12
5	25/6/2023	7352.76	7355.76	180.00	3540	20	18
6	25/6/2023	7355.77	7358.77	180.00	4920	27	27

#### Linear Regression of y on x





Operated By:

Andy Li

Project Technician, Environmental

Date: 03-07-2023

Checked By:

Tandy Tse
Senior Consultant, Environmental

Date: 03-07-2023



# RECALIBRATION DUE DATE:

March 31, 2024

# Certificate of Calibration

**Calibration Certification Information** 

Cal. Date: March 31, 2023

Calibration Model #: TE-5028A

Rootsmeter S/N: 438320

Ta: 294

Pa: 748.54

°K

Operator: Jim Tisch

m Hscn

Calibrator S/N: 3702

mm Hg

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.3110	4.1	1.50
2	3	4	1	1.0280	6.7	2.50
3	5	6	1	0.9340	8.1	3.00
4	7	8	1	0.8680	9.4	3.50
5	9	10	1	0.6580	16.2	6.00

		Data Tabulat	tion		
Vstd	Qstd	$\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}$		Qa	√∆H(Ta/Pa)
(m3)	(x-axis)	(y-axis)	Va	(x-axis)	(y-axis)
0.9929	0.7573	1.2237	0.9945	0.7586	0.7676
0.9894	0.9624	1.5798	0.9910	0.9641	0.9909
0.9875	1.0573	1.7306	0.9892	1.0591	1.0855
0.9858	1.1357	1.8693	0.9874	1.1376	1.1725
0.9767	1.4844	2.4474	0.9784	1.4869	1.5351
	m=	1.68024		m=	1.05214
<b>QSTD</b>	b=	-0.04353	QA	b=	-0.02731
	r=	0.99994		r=	0.99994

	Calculation	S	
Vstd=	ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	Va=	ΔVol((Pa-ΔP)/Pa)
Qstd=	Vstd/ΔTime	Qa= Va/ΔTime	
	For subsequent flow rat	e calculatio	ns:
Qstd=	$1/m\left(\left(\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}\right)-b\right)$	Qa=	$1/m\left(\left(\sqrt{\Delta H\left(Ta/Pa\right)}\right)-b\right)$

	Standard Conditions
Tstd:	298.15 °K
Pstd:	760 mm Hg
	Key
ΔH: calibrator	manometer reading (in H2O)
ΔP: rootsmete	er manometer reading (mm Hg)
Ta: actual abs	olute temperature (°K)
Pa: actual bar	ometric pressure (mm Hg)
b: intercept	
m: slope	

# RECALIBRATION

US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30.

Fisch Environmental, Inc. 145 South Miami Avenue /illage of Cleves, OH 45002

www.tisch-env.com

TOLL FREE: (877)263-7610 FAX: (513)467-9009





	Site Information					
Location:	Location: YMT Catholic Primary School Site ID: W-A1 Date: 01-Dec-2023					
Serial No: 1084 Model: TE-5170X Operator: Andy Li						

#### **Ambient Condition**

Actual Pressure during Calibration (P <sub>a</sub> ) (mm Hg):		Actual Temperature during Calibration (T <sub>a</sub> ) (deg K):	294.7
--	--	--	-------

#### **Calibration Orifice**

Model:	TE-5028A	Slope (m <sub>c</sub> ):	1.68024
Serial No.:	3702	Intercept (b <sub>c</sub> ):	-0.04353
Calibration Due Date:	31-Mar-24	Corr. Coeff:	0.99994

#### **Calibration Data**

Plate or	∆H <sub>2</sub> O	Qa, X-Axis	I, CFM	IC, Y-Axis
Test #	(in)	(m³/min)	(chart)	(corrected)
18	6.90	1.604	62.0	62.60
13	6.00	1.498	56.0	56.55
10	4.80	1.343	48.0	48.47
7	3.50	1.150	42.0	42.41
5	2.40	0.957	35.0	35.34

Sampler Calibtation Relationship (Qa on x-axis, IC on y-axis)

41.2821 b= -5.0228 Corr. Coeff= 0.9931


#### Calculations

$$\begin{split} Qa &= 1/m_c * [Sqrt \ (\Delta H_2 O * (P_a/P_{Std}) * (T_{Std}/T_a)) \cdot \ b_c] \\ &IC = I * (Sqrt \ (P_a/P_{Std}) * (T_{Std}/T_a)) \end{split}$$

Qa = actual flow rate IC = corrected chart response I = actual chart response

m<sub>c</sub> = calibrator slope b<sub>c</sub> = calibrator intercept

m = sampler slope b = sampler intercept  $T_{\rm 5de}$  = 298 deg K  $P_{\rm 5de}$  = 760 mm Hg  $T_{\rm a}$  = actual temperature during calibration (deg K)  $P_{\rm a}$  = actual pressure during calibration (mm Hg)



Checked by: Tandy Tse Senior Con

01-Dec-2023





#### Site Information

Location:	Man Cheong Building	Site ID:	W-A6	Date:	01-Dec-2023	
Serial No:	1050	Model:	TE-5170X	Operator:	Andy Li	

#### **Ambient Condition**

Actual Pressure during Calibration (Pa)	766.3	Actual Temperature during	204.7
(mm Hg):	766.2	Calibration (T <sub>a</sub> ) (deg K):	294.7

#### **Calibration Orifice**

Model:	TE-5028A	Slope (m <sub>c</sub> ):	1.68024
Serial No.:	3702	Intercept (b <sub>c</sub> ):	-0.04353
Calibration Due Date:	31-Mar-24	Corr. Coeff:	0.99994

#### **Calibration Data**

Plate or	∆H <sub>2</sub> O	Qa, X-Axis	I, CFM	IC, Y-Axis	
Test #	(in)	(m³/min)	(chart)	(corrected)	
18	7.00	1.616	59.0	59.58	
13	6.00	1.498	54.0	54.53	
10	4.90	1.356	49.0	49.48	
7	3.70	1.182	41.0	41.40	
5	2.70	1.013	36.0	36.35	

Sampler Calibtation Relationship (Qa on x-axis, IC on y-axis)

Corr. Coeff= 39.1205


#### Calculations

Qa =  $1/m_c^*[Sqrt (\Delta H_2O^*(P_a/P_{Std})^*(T_{Std}/T_a))-b_c]$  $IC = I*(Sqrt (P_a/P_{Std})*(T_{Std}/T_a))$ 

Qa = actual flow rate IC = corrected chart response I = actual chart response m<sub>c</sub> = calibrator slope b<sub>c</sub> = calibrator intercept

m = sampler slope b = sampler intercept T<sub>Std</sub> = 298 deg K

P<sub>Std</sub> = 760 mm Hg T<sub>a</sub> = actual temperature during calibration (deg K) P<sub>a</sub> = actual pressure during calibration (mm Hg)



Checked by:\_ 01-Dec-2023 Date:





Site Information

	One information						
Location:	YMT Catholic Primary School	Site ID:	W-A6	Date:	14-Dec-2023		
Serial No:	1084	Model:	TE-5170X	Operator:	Andy Li		

#### **Ambient Condition**

Actual Pressure during Calibration (Pa)	764.1	Actual Temperature during	206.2
(mm Hg):	764.1	Calibration (T <sub>a</sub> ) (deg K):	290.3

#### **Calibration Orifice**

Model:	TE-5028A	Slope (m <sub>c</sub> ):	1.68024
Serial No.:	3702	Intercept (b <sub>c</sub> ):	-0.04353
Calibration Due Date:	31-Mar-24	Corr. Coeff:	0.99994

#### **Calibration Data**

Plate or	∆H <sub>2</sub> O	Qa, X-Axis	I, CFM	IC, Y-Axis
Test#	(in)	(m³/min)	(chart)	(corrected)
18	11.80	2.082	60.0	60.34
13	9.40	1.861	55.0	55.31
10	6.70	1.575	44.0	44.25
7	4.90	1.351	37.0	37.21
5	3.30	1.113	31.0	31.17

Sampler Calibtation Relationship (Qa on x-axis, IC on y-axis)

m=	31.3097	b= -4.3254	Corr. Coeff=	0.9969

#### Calculations

Qa =  $1/m_c*[Sqrt (\Delta H_2O*(P_a/P_{Std})*(T_{Std}/T_a))-b_c]$ 

 $IC = I*(Sqrt (P_a/P_{Std})*(T_{Std}/T_a))$ 


Qa = actual flow rate IC = corrected chart response I = actual chart response m<sub>c</sub> = calibrator slope

b<sub>c</sub> = calibrator intercept

m = sampler slope b = sampler intercept T<sub>Std</sub> = 298 deg K P<sub>Std</sub> = 760 mm Hg

T<sub>a</sub> = actual temperature during calibration (deg K)

P<sub>a</sub> = actual pressure during calibration (mm Hg)







#### Site Information

Location:	Man Cheong Building	Site ID:	W-A6	Date:	14-Dec-2023
Serial No:	1050	Model:	TE-5170X	Operator:	Andy Li

#### **Ambient Condition**

	V-0.00000000000000000000000000000000000	The state of the s		-
Actual Pressure during Calibration (P <sub>a</sub> ) (mm Hg):	764.1	Actual Temperature during Calibration (T <sub>a</sub> ) (deg K):	296.3	1

#### **Calibration Orifice**

Model:	TE-5028A	Slope (m <sub>c</sub> ):	1.68024
Serial No.:	3702	Intercept (b <sub>c</sub> ):	-0.04353
Calibration Due Date:	31-Mar-24	Corr. Coeff:	0.99994

#### **Calibration Data**

Plate or	∆H <sub>2</sub> O	Qa, X-Axis	I, CFM	IC, Y-Axis
Test #	(in)	(m³/min)	(chart)	(corrected)
18	12.00	2.099	61.0	61.34
13	9.60	1.880	53.0	53.30
10	7.50	1.665	49.0	49.28
7	4.80	1.337	39.0	39.22
5	3.30	1.113	33.0	33.19

Sampler Calibtation Relationship (Qa on x-axis, IC on y-axis)

28.0041 1.9274 Corr. Coeff= 0.9974

#### Calculations

Qa =  $1/m_c^*[Sqrt (\Delta H_2O^*(P_a/P_{Std})^*(T_{Std}/T_a)) - b_c]$ 

 $IC = I*(Sqrt (P_a/P_{Std})*(T_{Std}/T_a))$ 


Qa = actual flow rate IC = corrected chart response I = actual chart response

m<sub>c</sub> = calibrator slope b<sub>c</sub> = calibrator intercept

m = sampler slope b = sampler intercept T<sub>Std</sub> = 298 deg K

P<sub>Std</sub> = 760 mm Hg T<sub>a</sub> = actual temperature during calibration (deg K)

P<sub>a</sub> = actual pressure during calibration (mm Hg)



Checked by: 14-Dec-2023 Date:

Contract No. HY/2014/20 Environmental Monitoring & Auditing
Annandiy I
Appendix I
Calibration Certificates (Noise)



# **Manufacturer Calibration Certificate**

The following instrument has been tested and calibrated to the manufacturer specifications. The calibration is traceable in accordance with ISO/IEC 17025 covering all instrument functions.

Device Type:

XL2 Audio and Acoustic Analyzer

· Serial Number:

A2A-13663-F0

· Certificate Issued:

15 February 2023

· Certificate Number:

44972-A2A-13663-F0

· Results:

**PASSED** 

(for detailed report see next page)

Tested by:

M. Frick

Signature:

m alten Riet 102

Stamp:

Li - 9494 Schaan www.nti-audio.com

NTi Audio AG • Im alten Riet 102 • 9494 Schaan • Liechtenstein • Europe • Tel: +423 239 6060 www.nti-audio.com • HR-Nr: 2.012.557 • MwStNr: 54306 • Bank: VP Bank, Vaduz, Acc No: 322.235.015

Calibration of:

XL2 Audio and Acoustic Analyzer

Serial Number:

A2A-13663-F0 15 February 2023

Date:

· Detailed Calibration Test Results:

	RMS Level @ 1kHz, XLR		reference 0.1 1	actual 0.100 0.999	unit V V	actual error ≤0.1% -0.1% -0.2%	XL2 tolerance ±0.5% ±0.5%	calibration uncertainty <sup>2</sup> ±0.10% ±0.09%
	Flatness, XLR Input <sup>1</sup>	20 Hz 20 kHz	10 1 1	9.982 0.995 1.003	V V	-0.2% -0.5% 0.3%	±1.1% ±1.1%	±0.09% ±0.09%
	Frequency		1000	1000.00	Hz	≤0.003%	±0.003%	±0.01%
	Residual Noise	XLR		< 2 uV			<2 uV	±0.50%
	THD+N @ 0 dBu, 1 kHz,	XLR Inpu	t	-100.5	dB		typ100 dB	±0.50%
•	Test Conditions:	Temper Relative	rature: Humidity:	24.9 19.8	°C %			

#### · Calibration Equipment Used:

- Agilent Multimeter, Typ 34401A, Serial No. MY 5300 4607 Last calibration: 15.09.2022, Next calibration: 15.09.2023 Calibrated by ELCAL to the national standards maintained at Swiss Federal Office of Metrology. SCS 0002
- FX100 Audio Analyzer, Serial No. 10408
   Last Calibration: 11.10.2022, Next Calibration: 11.10.2023
   Manufacturer calibration based on Agilent 34410, Serial No. MY47014254,
   Last Calibration: 26.05.2022, Next Calibration: 26.05.2023
   which is calibrated by ELCAL to national standards maintained at Swiss Federal Office of Metrology. SCS 002

<sup>&</sup>lt;sup>1</sup> The specified tolerance +/-0.1 dB @ 1V = +/- 1.1%

<sup>&</sup>lt;sup>2</sup> The reported expanded uncertainty is based on a standard uncertainty multiplied by a coverage factor k=2, providing a level of confidence of approximately 95%. The uncertainty evaluation has been carried out in accordance with the regulations of the GUM.



# Certificate of Calibration

Description: Sound Level Calibrator

Manufacturer: RION Type No.: NC-75 Serial No .: 34724244

Submitted by:

Customer: Acuity Sustainability Consulting Limited

Address: Unit E, 12/F, Ford Glory Plaza,

> Nos. 37-39 Wing Hong Street, Cheung Sha Wan, Kowloon,

Hong Kong

Upon receipt for calibration, the instrument was found to be:
✓ Within  ☐ Outside
the allowable tolerance.
The test equipments used for calibration are traceable to National S

tandards via:

The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 27 July 2023

Date of calibration: 3 August 2023

Date of NEXT calibration: 2 August 2024

Calibrated by:

Calibration Technician

Certified by: Mr. Ng Yan Wa Laboratory Manager

Date of issue: 3 August 2023

Certificate No.: APJ23-049-CC004

Page 1 of 2

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong Tel: (852) 2668 3423 Fax:(852) 2668 6946 



#### 1. Calibration Precautions:

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

# 2. Calibration Specifications:

Calibration check

# 3. Calibration Conditions:

Air Temperature:	22.6 °C
Air Pressure:	1006 hP
Relative Humidity:	52.9 %

#### 4. Calibration Equipment:

Test Equipment	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV220061	HOKLAS
Sound Level Meter	RION NA-28	30721812	AV220120	HOKLAS

# 5. Calibration Results

### 5.1 Sound Pressure Level

Nominal value	Accept lower level dB	Accept upper level	Measured value
dB		dB	dB
94.0	93.6	94.4	94.0

Note:


The values given in this certification only related to the values measured at the time of the calibration.



Page 2 of 2

Certificate No.: APJ23-049-CC004

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong Tel: (852) 2668 3423 Fax:(852) 2668 6946





#### Hong Kong Accreditation Service 香港認可處

# **Certificate of Accreditation** 認可證書

This is to certify that 特此證明

#### ACUMEN LABORATORY AND TESTING LIMITED

浩科檢測中心有限公司

Flat/Rm D, 12/F, Ford Glory Plaza, Nos. 37-39 Wing Hong Street, Cheung Sha Wan, Kowloon, Hong Kong

香港九龍長沙灣永康街37-39號福源廣場12樓D室

is accredited by the Hong Kong Accreditation Service (HKAS) to ISO/IEC 17025:2017 for performing specific laboratory activities as listed in the scope of accreditation within the test category of 獲香港認可處根據ISO/IEC 17025:2017認可 進行戰於認可範圍內下這測試類別中的指定實驗所活動

# **Environmental Testing**

環境測試

This accreditation to ISO/IEC 17025:2017 demonstrates technical competence for a defined scope and the implementation of a management system relevant to laboratory operation (see joint IAF-ILAC-ISO Communique).

此項 ISO/IEC 17025:2017 的認可資格證明此實驗所具備指定範疇內所須的技術能力並 實施一套與實驗所運作相關的管理關系 (見國際認可結婚、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of HKAS is affixed hereto by the authority of the HKAS Executive 現經香港認可處執行機關授權在此蓋上香港認可處的印章

SHUM Wai-leung, Executive Administrator

執行幹事 沈偉良

Issue Date: 15 November 2021

簽發日期:二零二一年十一月十五日

Registration Number : HOKLAS 241

Date of First Registration: 16 July 2014 首次註冊日期:二零一四年七月十六日

This certificate is issued subject to the terms and conditions laid down by HICAS 本體書級照香港認可盡訂立的條款及媒件發出

L002316



Hong Kong Accreditation Service 香港認可處

# **Certificate of Accreditation**

認可證書

This is to certify that 特此證明

# ALS TECHNICHEM (HK) PTY LIMITED

11/F, Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong 香港新界葵涌永業街1-3號忠信針織中心11樓

is accredited by the Hong Kong Accreditation Service (HKAS) to ISO/IEC 17025:2017 for performing specific laboratory activities as listed in the scope of accreditation within the test category of 獲香港認可處根據ISO/IEC 17025:2017認可 進行戰於認可範圍內下透測試類別中的指定實驗所活動

#### **Environmental Testing**

環境測試

This accreditation to ISO/IEC 17025:2017 demonstrates technical competence for a defined scope and the implementation of a management system relevant to laboratory operation (see joint IAF-ILAC-ISO Communiqué).

此項 ISO/IEC 17025:2017 的認可資格證明此實驗所具備指定範疇內所須的技術能力並 實施一套與實驗所運作相關的管理體系 (見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of HKAS is affixed hereto by the authority of the HKAS Executive 現經香港認可處執行機關授權在此蓋上香港認可處的印章

SHUM Wai-leung, Executive Administrator

執行幹事 沈偉良

Issue Date : 28 February 2020

**簽發日期:二零二零年二月二十八日** 

Registration Number : HOKLAS 066

註冊號碼:


Date of First Registration: 15 September 1995 首次註冊日期:一九九五年九月十五日


This certificate is issued subject to the terms and conditions laid down by HKAS 本證書按照香港即可處訂立的條款及條件發出

L001934

Contract No. HY/2014/20
Environmental Monitoring & Auditing

Appendix K
Location Plan of Noise and Air Quality
Monitoring Station

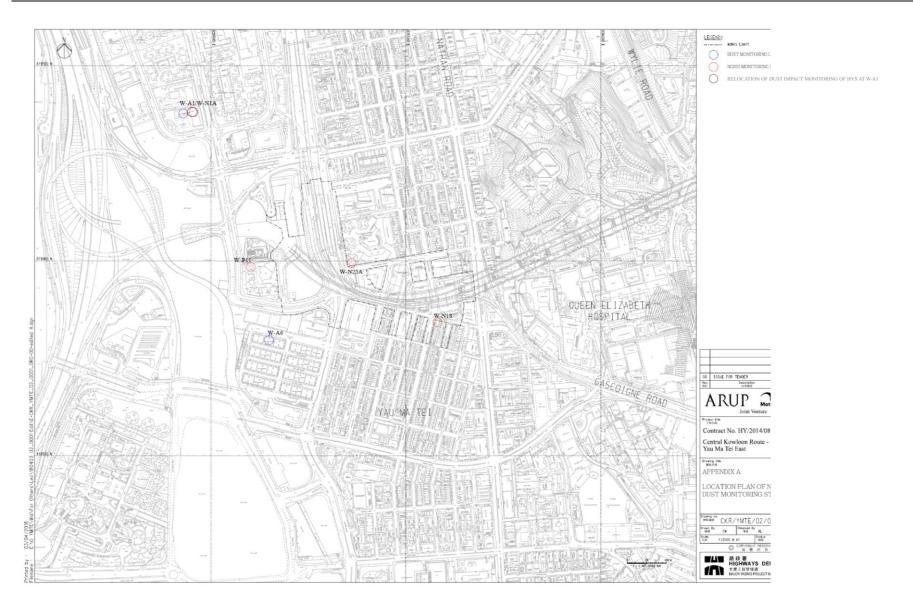



Location: Yau Ma Tei Catholic Primary School (Hoi Wang Road) (W-A1)

Monitoring date: 4, 9, 15, 21 and 27 December 2023

Parameter: TSP 1-hour
Other Factors Nearby traffic

		1-hour TSP (μg/m³)									
Date	Weather	Start Time	1 <sup>st</sup> Hour (μg/m³)	2 <sup>nd</sup> Hour (μg/m³)	3 <sup>rd</sup> Hour (μg/m³)						
04/12/2023	Fine	11:42	61	66	68						
09/12/2023	Fine	11:48	55	63	59						
15/12/2023	Fine	12:08	65	63	67						
21/12/2023	Fine	11:45	68	60	55						
27/12/2023	Fine	11:41	61	66	69						
Mini	mum: 55 μg/m	3		Maximum: 69 μg/m <sup>3</sup>							

Location: Man Cheong Building (W-A6)

Monitoring date: 4, 9, 15, 21 and 27 December 2023

Parameter: TSP 1-hour
Other Factors Nearby traffic

		1-hour TSP (μg/m³)										
Date	Weather Start Tim		1 <sup>st</sup> Hour (μg/m³)	2 <sup>nd</sup> Hour (μg/m³)	3 <sup>rd</sup> Hour (μg/m³)							
04/12/2023	Fine	09:09	68	56	56							
09/12/2023	Fine	09:10	66	62	54							
15/12/2023	Fine	11:34	59	70	65							
21/12/2023	Fine	09:16	63	54	55							
27/12/2023	Fine	09:13	59	70	65							
	Minimum: 54	μg/m³		Maximum: 70 μg/m <sup>3</sup>								

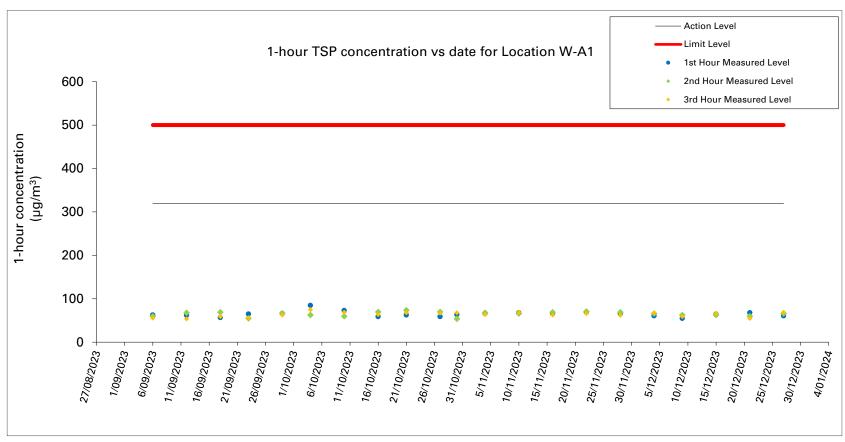


Figure 1: Graphical Illustration of Measured 1-hour TSP (μg/m³) Levels at W-A1

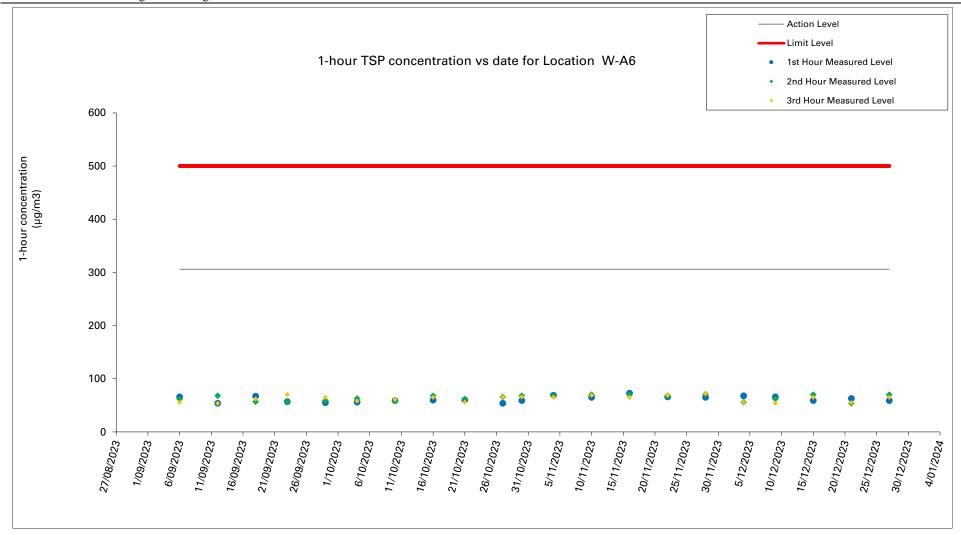


Figure 2: Graphical Illustration of Measured 1-hour TSP (μg/m³) Levels at W-A6

Location: Yau Ma Tei Catholic Primary School (Hoi Wang Road) (W-A1)

Monitoring date: 4, 9, 15, 21 and 27 December 2023

Parameter: TSP 24-hour
Other Factors Nearby traffic

Date of Calibration:	1-Dec-23	Slope =	41.2821
Calibration due date:	16-Dec-23	Intercept =	-5.0228
Date of Calibration:	14-Dec-23	Slope =	31.3097
Calibration due date:	29-Dec-23	Intercept =	-4.3254

Start Date	Weather	Elapse Time		Elapse Time   Chart Reading		Avg Air Temp	Avg Atmospheric Pressure	Flow Rate	Standard Air Volume	Filter Weight (g)		Particulate weight	Corr.		
	Condition	Initial	Final	Actual (min)	Min	Max	Avg	(°C)	(hPa)	(m³/min)	( <b>m</b> <sup>3</sup> )	Initial	Final	(g)	$(\mu g/m^3)$
4/12/2023	Fine	77996.7	78020.7	1440.0	47	48	47.5	21.8	1016.4	1.28	1846	2.6530	2.8636	0.2106	114
9/12/2023	Fine	78020.7	78044.7	1440.0	46	46	46.0	23.4	1014.2	1.24	1786	2.6701	2.8234	0.1533	86
15/11/2023	Fine	78044.7	78068.7	1440.0	47	47	47.0	22.9	1018.4	1.27	1829	2.6933	2.7679	0.0746	41
21/12/2023	Fine	78068.7	78092.7	1440.0	46	47	46.5	10.7	1028.6	1.68	2424	2.6506	2.7692	0.1186	49
27/12/2023	Fine	78092.7	78116.7	1440.0	45	45	45.0	21.2	1023.2	1.60	2302	2.6628	2.8909	0.2281	99
										Maximum:	114	μg/m <sup>3</sup>	Minimum:	41	μg/m <sup>3</sup>

Location: Man Cheong Building (W-A6)

Monitoring date: 4, 9, 15, 21 and 28 December 2023

Parameter: TSP 24-hour
Other Factors Nearby traffic

Date of Calibration:	1-Dec-23	Slope =	39.1205
Calibration due date:	16-Dec-23	Intercept =	-3.8835
Date of Calibration:	14-Dec-23	Slope =	28.0041
Calibration due date:	29-Dec-23	Intercept =	1.9274

Start Date	Weather Condition	Elapse Time			Chart Reading		Avg Air Temp Atmospheric Pressure		Flow Rate Standard Air Volume		Filter Weight (g)		Particulate weight	Conc.	
	Condition	Initial	Final	Actual (min)	Min	Max	Avg	(°C)	(hPa)	(m³/min)	( <b>m</b> <sup>3</sup> )	Initial	Final	(g)	(μg/m <sup>3</sup> )
4/12/2023	Fine	10411.9	10435.9	1440.00	42	42	42.0	21.8	1016.4	1.18	1702	2.6617	2.8654	0.2037	120
9/12/2023	Fine	10435.9	10459.9	1440.00	42	41	41.5	23.4	1014.2	1.16	1676	2.6623	2.8000	0.1377	82
15/11/2023	Fine	10459.9	10483.9	1440.00	42	42	42.0	22.9	1018.4	1.18	1702	2.6796	2.7675	0.0879	52
21/12/2023	Fine	10483.9	10507.9	1440.00	41	41	41.0	10.7	1028.6	1.45	2094	2.6461	2.8504	0.2043	98
28/12/2023	Fine	10507.9	10531.9	1440.00	41	41	41.0	19.8	1021.7	1.42	2046	2.6673	2.805	0.1377	67
		-	-			·				Maximum:	120	μg/m <sup>3</sup>	Minimum:	52	μg/m <sup>3</sup>

Remarks: Due to equipment malfunction, 24-hr TSP monitoring at W-A6 on 27 December 2023 has been postponed to 28 December 2023.

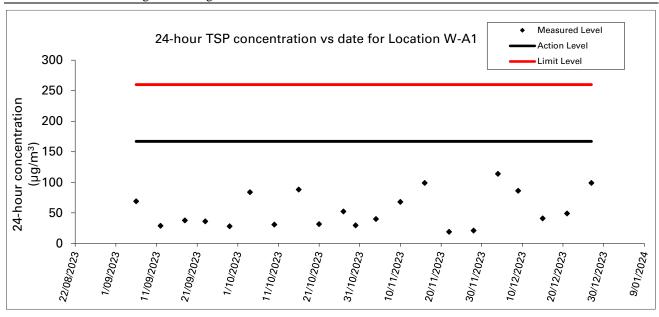


Figure 3: Graphical Illustration of Measured 24-hour TSP (μg/m³) Levels at W-A1



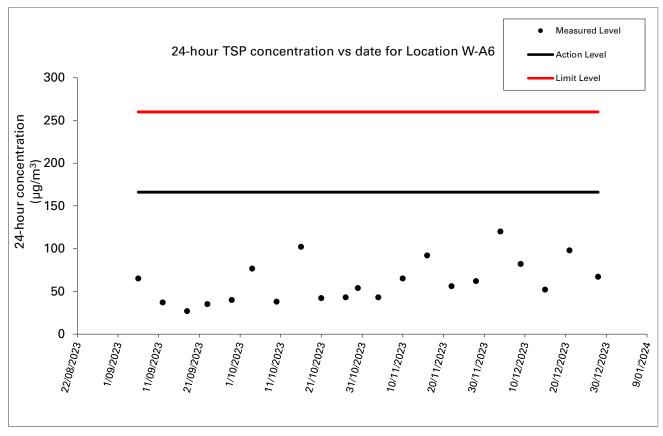


Figure 4: Graphical Illustration of Measured 24-hour TSP ( $\mu g/m^3$ ) Levels at W-A6

# Wind direction data for 4, 5, 9, 10, 15, 16, 21, 22, 27 and 28 December 2023




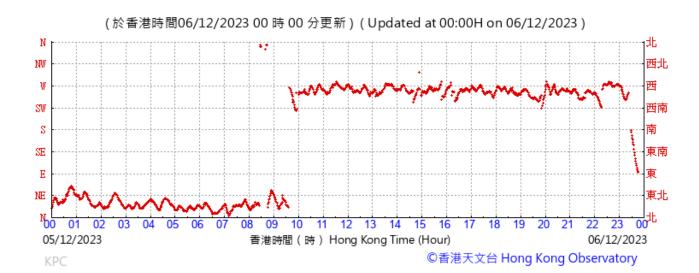


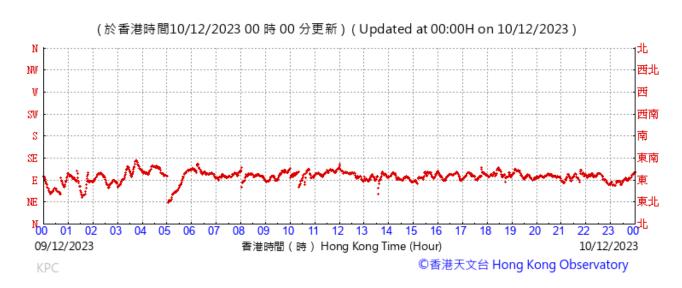








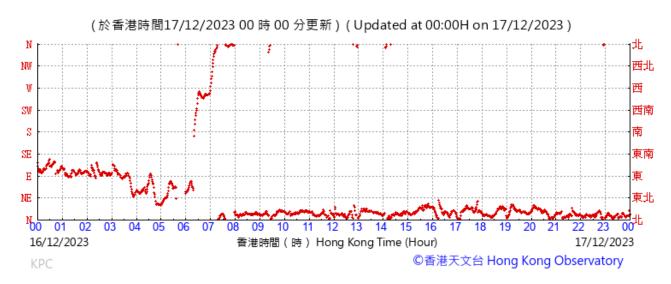

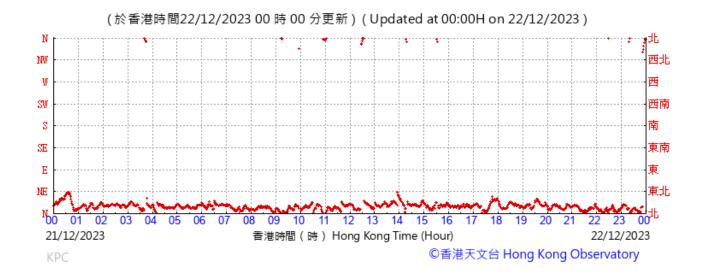

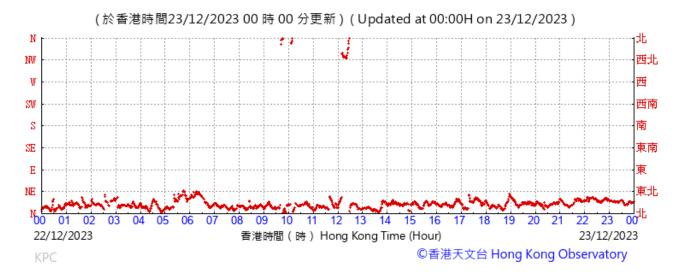

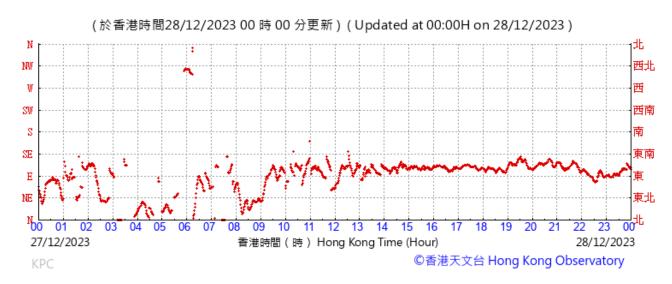

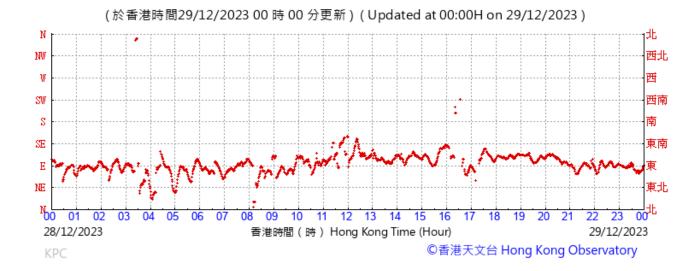

### Wind speed data for 4, 5, 9, 10, 15, 16, 21, 22, 27 and 28 December 2023













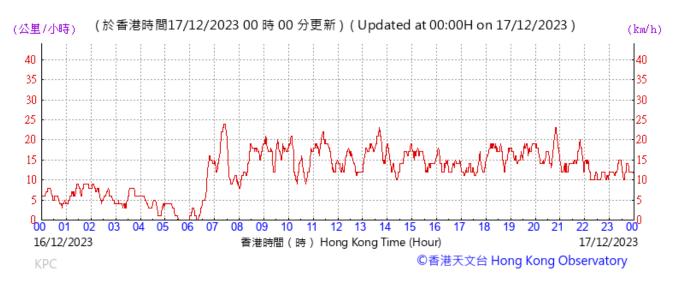





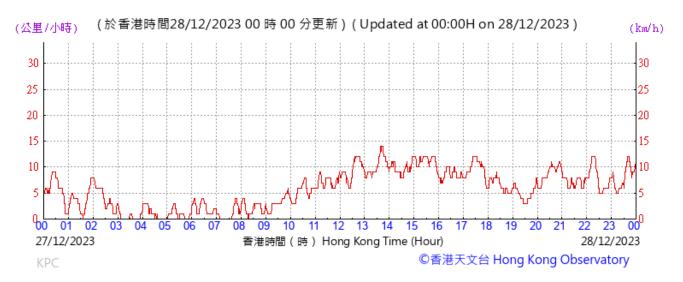



Contract No. HY/2014/20
Environmental Monitoring & Auditing

Appendix M Monitoring Data (Noise) Location: Yau Ma Tei Catholic Primary School (Hoi Wang Road) (W-N1A)

Monitoring date: 4, 9, 15, 21 and 27 December 2023

 $\begin{array}{ll} \text{Parameter:} & L_{\text{eq}}, L_{10}, L_{90} \\ \text{Other Factors} & \text{Nearby traffic} \end{array}$ 

# Noise Monitoring data:

Date	Weather	Start Time - End Time	$L_{ m eq}$	$L_{10}$	L <sub>90</sub>	Wind speed (m/s)	Limit level
04/12/2023	Fine	11:40 - 12:10	66.1	72.0	60.4	1.9	70.0
09/12/2023	Fine	11:46 - 12:16	66.2	72.5	59.4	3.9	70.0
15/12/2023	Fine	12:10 - 12:40	61.7	64.0	58.9	2.5	70.0
21/12/2023	Fine	11:42 - 12:12	66.7	69.7	60.4	4.2	70.0
27/12/2023	Fine	11:48 - 12:18	65.8	72.1	61.2	3.6	70.0

Remark: 1. No examination was scheduled at Yau Ma Tei Catholic Primary School during the reporting month. The limit level of W-N1A would be 70 dB(A).

# Contract No. HY/2014/20 Environmental Monitoring & Auditing

Location: Hydan Place (W-N18)

Monitoring date: 4, 9, 15, 21 and 27 December 2023

 $\begin{array}{ll} \mbox{Parameter}: & L_{eq}, L_{10}, L_{90} \\ \mbox{Other Factors} & \mbox{Nearby traffic} \end{array}$ 

# Noise Monitoring data:

Date Weather	Weather	Start Time	- End Time	$L_{\rm eq}$	$L_{10}$	L <sub>90</sub>	Wind speed	Limit level
2 4.0	,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,		2.1.0		_10	,,,	(m/s)	
04/12/2023	Fine	09:24	- 09:54	70.4	74.7	66.2	1.1	75.0
09/12/2023	Fine	09:29	- 09:59	70.9	74.7	65.9	2.5	75.0
15/12/2023	Fine	9:27	- 9:57	69.5	71.9	65.3	1.9	75.0
21/12/2023	Fine	09:28	- 09:58	68.4	72.1	65.2	3.5	75.0
27/12/2023	Fine	09:32	- 10:02	69.4	72.6	64.3	1.1	75.0

Location: Prosperous Garden Block 1 (W-N25A)

Monitoring date: 4, 9, 15, 21 and 27 December 2023

 $\begin{array}{ll} \mbox{Parameter}: & L_{\mbox{\scriptsize eq},} L_{10}, L_{90} \\ \mbox{Other Factors} & \mbox{Nearby traffic} \end{array}$ 

## Noise Monitoring data:

Date Weather		Start Time - End Time		$L_{ m eq}$ $L_{ m 10}$		$L_{90}$	Wind speed	Limit level
Bute	vv cather	Start Time - End Time		<b>L</b> eq	1210	1290	(m/s)	Emmt iever
04/12/2023	Fine	10:06	- 10:36	68.9	71.4	64.8	0.7	75.0
09/12/2023	Fine	10:11	- 10:41	68.7	72.7	65.1	2.8	75.0
15/12/2023	Fine	10:17	- 10:47	68.8	71.8	64.4	3.1	75.0
21/12/2023	Fine	10:08	- 10:38	67.0	72.6	58.9	3.5	75.0
27/12/2023	Fine	10:13	- 10:43	65.1	72.3	60.8	1.7	75.0

#### Contract No. HY/2014/20 Environmental Monitoring & Auditing

Location: The Coronation Tower 1 (W-P11)

Monitoring date: 4, 9, 15, 21 and 27 December 2023

 $\begin{array}{ll} \mbox{Parameter}: & L_{\mbox{\scriptsize eq}}, L_{10}, L_{90} \\ \mbox{Other Factors} & \mbox{Nearby traffic} \end{array}$ 

## Noise Monitoring data:

Date	Weather	Start Time	- End Time	$L_{\rm eq}$	$L_{10}$	L <sub>90</sub>	Wind speed (m/s)	Limit level
04/12/2023	Fine	10:45	- 11:15	65.4	71.4	60.5	1.4	75.0
09/12/2023	Fine	10:51	- 11:15	68.3	70.4	65.5	2.8	75.0
15/12/2023	Fine	13:15	- 13:45	67.1	70.0	64.4	3.1	75.0
21/12/2023	Fine	10:52	- 13:30	68.9	71.0	65.3	3.5	75.0
27/12/2023	Fine	10:56	- 11:26	66.3	73.0	59.3	1.9	75.0

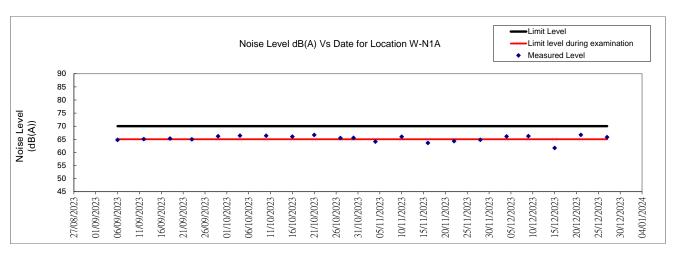


Figure 1: Graphical Illustration of Measured Noise Levels at W-N1A

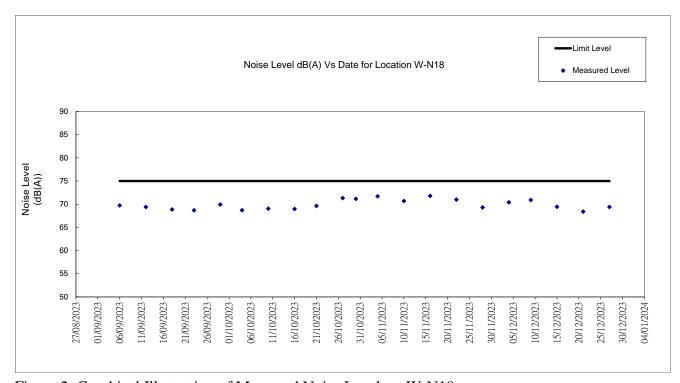


Figure 2: Graphical Illustration of Measured Noise Levels at W-N18

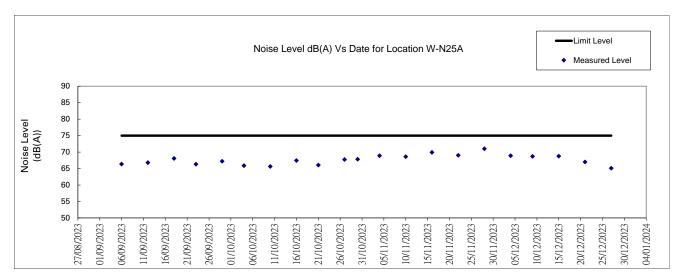


Figure 3: Graphical Illustration of Measured Noise Levels at W-N25A

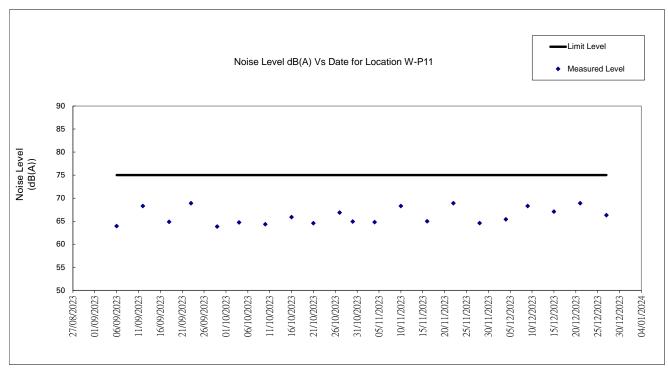


Figure 4: Graphical Illustration of Measured Noise Levels at W-P11

Contract No. HY/2014/20
Environmental Monitoring & Auditing

Appendix N Waste Flow Table Environmental Monitoring & Auditing

**Monthly Summary Waste Flow Table** 

Name of Department: **Highways Department** Contract No. / Works Order No.: <u>HY/2014/20</u>

Monthly Summary Waste Flow Table for December 2023

[to be submitted not later than the 15<sup>th</sup> day of each month following reporting month] (All quantities shall be rounded off to 2 decimal place.)

	Actual Quantities of <u>Inert</u> Construction Waste Generated Monthly					
Month	(a)=(b)+(c)+(d)+I+ (f)+ (g)+ (h)+ (i)+ (j)+ (k)  Total Quantity Generated	(b) Hard Rock and Large Broken Concrete	I Reused in the Contract	(d) Reused in other Projects	I Disposed of as Public Fill	(f) Imported Fill
	(in 'tonnes)	(in 'tonnes)	(in 'tonnes)	(in 'tonnes)	(in 'tonnes)	(in 'tonnes)
Jan-23	3810.16	0.00	0.00	0.00	2814.24	876.02
Feb-23	11085.29	0.00	0.00	0.00	10559.85	375.09
Mar-23	15268.28	0.00	0.00	0.00	15150.39	0.00
Apr-23	38951.51	0.00	27490.00	46.53	11263.49	47.22
May-23	8585.67	0.00	0.00	57.54	8312.41	0.00
Jun-23	9197.99	0.00	0.00	0.00	9040.92	0.00
Sub-total	86898.89	0.00	27490.00	104.07	57141.30	1298.33
Jul-23	5775.46	0.00	0.00	0.00	5671.16	0.00
Aug-23	6222.37	0.00	0.00	0.00	5593.53	377.52
Sep-23	6527.40	0.00	0.00	0.00	5781.97	648.96
Oct-23	9521.34	0.00	0.00	0.00	8471.80	851.66
Nov-23	7194.25	0.00	0.00	0.00	6412.49	587.26
Dec-23	4592.19	0.00	0.00	0.00	3918.79	476.79
Total	126731.90	0.00	27490.00	104.07	92991.04	4240.52
2018	15.65	0.00	0.00	0.00	0.00	0.00
2019	71691.85	0.00	5534.00	8066.88	57313.64	415.55
2020	168891.36	0.00	15437.30	84381.54	68187.83	180.00
2021	213790.30	0.00	16567.28	79780.37	114965.52	1002.03
2022	140806.50	0.00	22476.00	20553.85	51490.05	44771.11
Accumulated Total	721927.56	0.00	87504.58	192886.71	384948.08	50609.20

		Actual Quantities of Non-inert Construction Waste Generated Monthly							
Month	М	(g) Metals		(h) Paper/ cardboard packaging		(i) Plastics		(j) cal Waste	(k) Others, e.g. General Refuse disposed at Landfill
	(in '	000kg)	(in '0	00kg)	(in '00	00kg)	(in '(	000kg)	(in 'tonnes)
	generated	recycled	generated	recycled	generated	recycled	generated	recycled	generated
Jan-23	0.00	47.32	0.00	0.03	0.00	0.35	0.00	0.00	72.20
Feb-23	0.00	44.14	0.00	0.00	0.00	0.00	0.00	0.00	106.21
Mar-23	0.00	33.56	0.00	0.05	0.00	0.35	0.00	0.00	83.93
Apr-23	0.00	19.48	0.00	0.00	0.00	0.00	0.00	0.00	84.79
May-23	0.00	139.98	0.00	0.06	0.00	0.30	0.00	0.00	75.38
Jun-23	0.00	77.94	0.00	0.00	0.00	0.005	0.00	0.00	79.12
Sub-total	0.00	362.42	0.00	0.14	0.00	1.005	0.00	0.00	501.63
Jul-23	0.00	0.00	0.00	0.07	0.00	1.268	0.00	0.00	102.96
Aug-23	0.00	152.79	0.00	0.00	0.00	0.00	0.00	0.00	98.53
Sep-23	0.00	8.30	0.00	0.013	0.00	0.00	0.00	0.00	88.16
Oct-23	0.00	99.70	0.00	0.00	0.00	1.58	0.00	0.00	96.60
Nov-23	0.00	35.67	0.00	0.095	0.00	0.56	0.00	0.00	158.17
Dec-23	0.00	57.60	0.00	0.012	0.00	0.042	0.00	0.00	138.96
Total	0.00	716.48	0.00	0.33	0.00	4.46	0.00	0.00	1185.01
2018	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	15.65
2019	0.00	106.04	0.00	0.20	0.00	1.47	2.11	0.00	251.96
2020	359.10	0.00	0.35	0.00	3.16	0.00	0.88	0.00	341.20
2021	945.79	0.00	0.20	0.00	3.34	0.00	0.00	0.00	525.77
2022	615.75	159.28	0.75	0.08	2.12	1.49	0.00	0.00	736.02
Accumulated Total	1920.64	981.80	1.30	0.61	8.62	7.42	2.99	0.00	3055.61



Appendix O
Statistics on Complaint, Notifications of
Summons and Successful Prosecutions

Statistical Summary of Exceedances

Air Quality					
Reporting Period	Action Level	Limit Level			
1 – 31 December 2023	0	0			
	Noise				
Reporting Period	Action Level	Limit Level			
1 – 31 December 2023	0	0			

Statistical Summary of Environmental Complaints

Donouting Donied	Environmental Complaint Statistics					
Reporting Period	Frequency	Cumulative	Complaint Nature			
1 – 31 December 2023	3	17	Noise nuisance			

Statistical Summary of Environmental Non-compliance


Donauting David	Environmental Non-compliance Statistics					
Reporting Period	Frequency	Cumulative	Details			
1 – 31 December 2023	0	0	N/A			

Statistical Summary of Environmental Summons


Donarting Daried	Environmental Summons Statistics				
Reporting Period	Frequency	Cumulative	Details		
1 – 31 December 2023	0	0	N/A		

Statistical Summary of Environmental Prosecution

Donauting David	Environmental Prosecution Statistics					
Reporting Period	Frequency	Cumulative	Details			
1 – 31 December 2023	0	0	N/A			



		Impa	ct Monitoring Schedule for Y	MTW		
	Jan-24					
Sun	Mon			Thu		Sat
	1		3	4	5	6
		Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A				
7	8	9	10	11	12	13
	Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A					Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A
14	15	16	17	18		20
					Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A	
21	22	23	24	25	26	27
				Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A		
28	29	30	31			
			Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A			




## **Interim Report on Environmental Complaint**

Project	Central Kowloon Route, Yau Ma Tei West Section
Complaint Code	EC015-CKRYMTW20231207-001
Complaint description	The complainant was received on 12 Dec 2023, about the construction noise from the site area <sup>1</sup> near Charming Garden on 07 Dec 2023 from 0100 to 0149.
Parameter	Construction Noise
Investigation finding	The complaint was received on 12 Dec 2023 and the complainant was concerned about the construction noise from the site area near Charming Garden on 07 Dec 2023 from 0100 to 0149.
	For construction works undertaken within restricted hours, the Contractor applied for valid Construction Noise Permits (CNP) (Permit No: GW-RE1529-23) which was granted from EPD, effective from 07 Dec 2023 to 9 Feb 2024 with coverage of the construction site at the concerned area <sup>1</sup> . As noted by the contractor, underground utility diversion was performed from 0100 to 0200 on 07 Dec 2023. PME used included 1 excavator. The aforementioned PME was classified in PME Group D and was allowed to be operated in the Working Zone during 0100-0530 on any day not being a general holiday between Monday and Friday. The excavator used was with Quality Powered Mechanical Equipment Label showing Sound Power Level not greater than 105dB(A). CNP conditions had been strictly followed when operating PME during restricted hours. No violation and non-compliance of CNP was observed or recorded. The Contractor had followed the requirements as stipulated in CNP.
	Considering the fulfillment of stipulated requirements by the Contractor for EM&A manual and the granted CNP, it is concluded that there was no non-compliance of the Project regarding noise quality impact from construction site.
Actions taken / to be taken	The Contractor had followed EM&A Manual, granted CNP and the CNMMP strictly to implement mitigation measures in order to minimize nuisance to the public.
	<ul> <li>In view of public concerns, the following additional remedial measures are taken:</li> <li>Carry out site inspection to ensure all PMEs are well-maintained and in proper function to avoid excessive noise;</li> <li>Provide training to workers of using PME carefully to minimize noise; and</li> <li>Reschedule the operation time of the noisy equipment to less sensitive hours if possible.</li> </ul>
Remarks	1. Working Zone of CNP GW-RE1529-23
(Shown in next page)	

Prepared by ET (Acuity Sustainability Consulting Limited)	Kako Ho	Ho
Reviewed by ETL (Acuity Sustainability Consulting Limited)	Kevin Li	K
Verified by IEC (ERM-Hong Kong, Limited)	Mandy To	Mandej2.
Date	18 Decem	ber 2023

Remark 1: Working Zone of CNP GW-RE1529-23

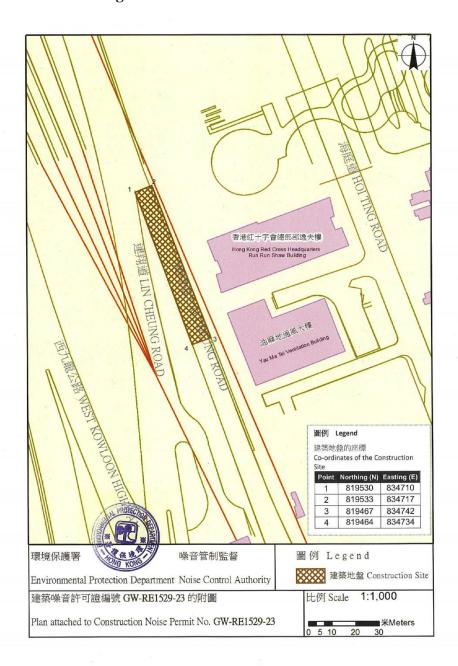


## **Interim Report on Environmental Complaint**

Project	Central Kowloon Route, Yau Ma Tei West Section
Complaint Code	EC0016-CKRYMTW20231214-001
Complaint description	The complainant made a complaint on 14 Dec 2023, about the construction noise from the site area <sup>1</sup> near Olympian City 2 on 14 Dec 2023 at 0100.
Parameter	Construction Noise
Investigation finding	The complaint was received on 14 Dec 2023, concerned about the construction noise from the site area near Olympian City 2 on 14 Dec 2023 at 0100.
	For construction works undertaken within restricted hours, the Contractor applied for valid Construction Noise Permits (CNP) (Permit No: GW-RE1529-23) which was granted from EPD, effective from 07 Dec 2023 to 9 Feb 2024 with coverage of the construction site at the concerned area <sup>1</sup> . As noted by the contractor, underground utility diversion was performed from 0100 to 0200 on 14 Dec 2023. PME used included 1 excavator. The aforementioned PME was classified in PME Group D and was allowed to be operated in the Working Zone during 0100-0530 on any day not being a general holiday between Monday and Friday. The excavator used was with Quality Powered Mechanical Equipment Label showing Sound Power Level not greater than 105dB(A). CNP conditions had been strictly followed when operating PME during restricted hours. No violation and non-compliance of CNP was observed or recorded. The Contractor had followed the requirements as stipulated in CNP.
	Considering the fulfillment of stipulated requirements by the Contractor for EM&A manual and the granted CNP, it is concluded that there was no non-compliance of the Project regarding noise quality impact from construction site.
Actions taken / to be taken	The Contractor had followed EM&A Manual, granted CNP and the CNMMP strictly to implement mitigation measures in order to minimize nuisance to the public.
	<ul> <li>In view of public concerns, the following additional remedial measures are taken:</li> <li>Carry out site inspection to ensure all PMEs are well-maintained and in proper function to avoid excessive noise;</li> <li>Provide training to workers of using PME carefully to minimize noise; and</li> <li>Reschedule the operation time of the noisy equipment to less sensitive hours if possible.</li> </ul>
Remarks	1. Working Zone of CNP GW-RE1529-23
(Shown in next page)	

Prepared by ET (Acuity Sustainability Consulting Limited)	Kako Ho	Ho
Reviewed by ETL (Acuity Sustainability Consulting Limited)	Kevin Li	K
Verified by IEC (ERM-Hong Kong, Limited)	Mandy To	Mandy 2.
Date	15 Decem	ber 2023

Remark 1: Working Zone of CNP GW-RE1529-23

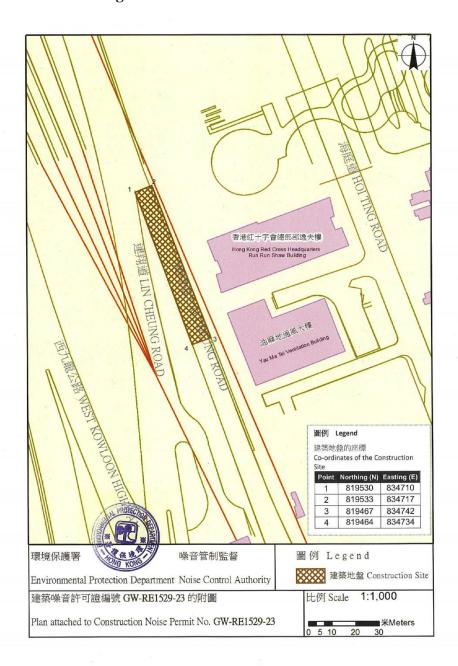


## **Interim Report on Environmental Complaint**

Project	Central Kowloon Route, Yau Ma Tei West Section
Complaint Code	EC017_CKRYMTW20231214_002
Complaint description	The complaint was received on 20 Dec 2023, about the construction noise from the site area near West Kowloon and Olympic Station on 14 Dec 2023 at midnight.
Parameter	Construction Noise
Investigation finding	The complaint was received on 20 Dec 2023 and the complainant was concerned about the construction noise from the site area near West Kowloon and Olympic Station on 14 Dec 2023 at midnight.
	For construction works undertaken within restricted hours, the Contractor applied for valid Construction Noise Permits (CNP) (Permit No: GW-RE1529-23) which was granted from EPD, effective from 07 Dec 2023 to 9 Feb 2024 with coverage of the construction site at the concerned area <sup>1</sup> . As noted by the contractor, road surfacing opening was performed from 0100 to 0200 on 14 Dec 2023. PME used included 1 electric hand-held breaker and 1 excavator. The aforementioned PME were classified in PME Group B and Group D respectively and were allowed to be operated in the Working Zone during 0100-0530 on any day not being a general holiday between Monday and Friday. Only hand-held breaker or excavator was operated at a time. The hand-held breaker used was with Noise Emission Label showing Sound Power Level not greater than 103 dB(A). The hand-held breaker was inside noise enclosure during the operation. CNP conditions had been strictly followed when operating PME during restricted hours. No violation and non-compliance of CNP was observed or recorded. The Contractor had followed the requirements as stipulated in CNP.
	Considering the fulfillment of stipulated requirements by the Contractor for EM&A manual and the granted CNP, it is concluded that there was no non-compliance of the Project regarding noise quality impact from construction site.
Actions taken / to be taken	The Contractor had followed EM&A Manual, granted CNP and the CNMMP strictly to implement mitigation measures in order to minimize nuisance to the public.
	<ul> <li>In view of public concerns, the following additional remedial measures are taken:</li> <li>Carry out site inspection to ensure all PMEs are well-maintained and in proper function to avoid excessive noise;</li> <li>Provide training to workers of using PME carefully to minimize noise; and</li> <li>Reschedule the operation time of the noisy equipment to less sensitive hours if possible.</li> </ul>
Remarks (Shown in next page)	1. Working Zone of CNP GW-RE1529-23

Prepared by ET (Acuity Sustainability Consulting Limited)	Kako Ho	Ho
Reviewed by ETL (Acuity Sustainability Consulting Limited)	Kevin Li	X:
Verified by IEC (ERM-Hong Kong, Limited)	Mandy To	Mandy2.
Date	27 Decem	ber 2023

Remark 1: Working Zone of CNP GW-RE1529-23

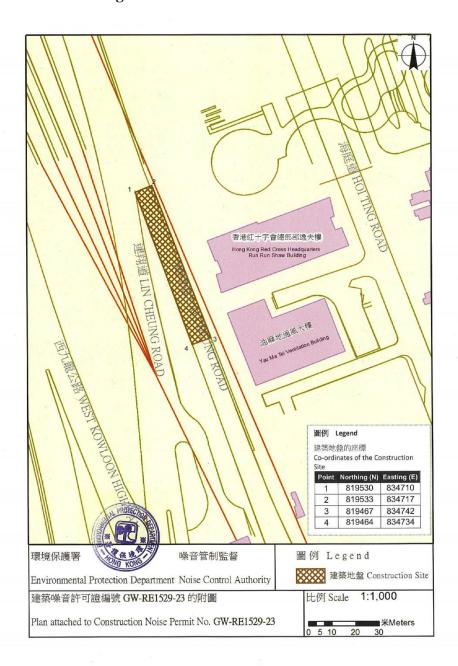

Central Kowloon Route
Buildings, Electrical and
Mechanical Works
Contract No. HY/2019/13
(Yau Ma Tei West Area)

#### **Gammon Construction Limited**

# Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works

Monthly EM&A Report No. 39 (December 2023)

Version 1.0

Date of Report: 3 January 2024

Certified By

(Environmental Team Leader:

Ms. Betty Choi)

#### REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties

#### CINOTECH CONSULTANTS LTD

Room 1710, Technology Park, 18 On Lai Street, Shatin, NT, Hong Kong Tel: (852) 2151 2083 Fax: (852) 3107 1388

Email: info@cinotech.com.hk





## Environmental Permit No. EP-457/2013/D

#### Central Kowloon Route

## **Independent Environmental Checker Verification**

Reference Document/Plan	
Document/Plan to be Certified/ Verified:	Monthly EM&A Report No.39
Date of Report:	3 January 2024 (Version 1.0)
Date received by IEC:	3 January 2024

Buildings, Electrical and Mechanical Works (HY/2019/13)

#### Reference EP Condition

**Works Contract:** 

**Environmental Permit Condition:** 3.4

Submission of Monthly EM&A Report of the Project

3.4 Four hard copies and one electronic copy of monthly EM&A Report shall be submitted to the Director within 2 weeks after the end of each reporting month throughout the entire construction period. The EM&A Reports shall include a summary of all non-compliance. The submissions shall be certified by the ET Leader and verified by the IEC as complying with the requirements as set out in the EM&A Manual before submission to the Director. Additional copies of the submission shall be provided to the Director upon request by the Director.

#### **IEC Verification**

Mondy 20.

Independent Environmental Checker

I hereby verify that the above referenced document/plan complies with the above referenced condition of EP-457/2013/D.

Ms Mandy To

Date: 5 January 2024

Our ref: 0436942\_IEC Verification Cert\_BEM\_Monthly EM&A Rpt No.39\_20240105.docx

## TABLE OF CONTENTS

		Page
EX	KECUTIVE SUMMARY	1
1	INTRODUCTION	3
Ba	ckground	3
	rpose of the Report	
	oject Organizations	
	Instruction Activities undertaken during the Reporting Month	
	mmary of EM&A Requirements	
Sta	atues of Environmental Licensing and Permitting	
2	AIR QUALITY	6
Mo	onitoring Requirements	6
Ob	servations	6
3	NOISE	6
Mo	onitoring Requirements	6
	oservations	
4	WASTE MANAGEMENT	7
Μα	onitoring Requirements	7
	sults and Observations	
5	LANDSCAPE AND VISUAL	8
Μα	onitoring Requirements	8
	sults and Observations	
6	ENVIRONMENTAL AUDIT	9
Sit	e Audits	9
	plementation Status of Environmental Mitigation Measures	
	plementation Status of Event and Action Plans	
Su	mmary of Complaint, Warning, Notification of any Summons and Successful P	rosecution10
	atus of Required Submission under Environmental Permit	
7	FUTURE KEY ISSUES	11
8	CONCLUSIONS AND RECOMMENDATIONS	12
<b>C</b> -		12

#### LIST OF TABLES

Table I	Summary of Complaint/Summons/Prosecution in the Reporting Month
Table 1.1	Key Project Contacts
Table 1.2	Summary of Environmental Licensing and Permit Status
Table 4.1	Quantities of Waste Generated from the Project
Table 6.1	Observations and Recommendations of Site Inspections
Table 6.2	Status of Required Submission under Environmental Permit

#### LIST OF FIGURES

Figure 1.1	Site Layout Plan
Figure 1.2	Project Organisation for Environmental Monitoring and Audit

## LIST OF APPENDICES

Appendix A	Construction Programme
Appendix B	Summary of Waste Generation and Disposal Records
Appendix C	Environmental Mitigation Implementation Schedule (EMIS)
Appendix D	Summaries of Environmental Complaint, Warning, Summon and Notification of
	Successful Prosecution

#### **EXECUTIVE SUMMARY**

#### Introduction

- 1. This is the 39<sup>th</sup> Monthly Environmental Monitoring and Audit (EM&A) Report prepared by the Environmental Team (ET), Cinotech Consultants Ltd., for Contract No. HY/2019/13 "Central Kowloon Route Buildings, Electrical and Mechanical Works". This report summarized the monitoring results and audit findings of the EM&A programme under the issued EP No. EP-457/2013/D, and in accordance with the EM&A programme in Yau Ma Tei West Area during the reporting period from 1<sup>st</sup> December 2023 31<sup>st</sup> December 2023.
- 2. The major site activities undertaken in Yau Ma Tei Area in the reporting month included:
  - Super-structure works.
  - ABWF works
  - E&M installation

#### **Environmental Monitoring Works**

- 3. Environmental monitoring for the Project was performed in accordance with the EM&A Manual and the monitoring results were checked and reviewed. Joint weekly site inspections with the representative of ET, Engineer Representative and the Contractor for Contract No. HY/2019/13 were conducted on 5, 13, 19, 27 December 2023, whereas joint site inspection with the representative of IEC was conducted on 13 December 2023. The implementation of the environmental mitigation measures, Event and Action Plans and environmental complaint handling procedures were also checked.
- 4. A summary of the non-compliance (exceedance) during the reporting month (December 2023) and the investigation results and/or follow-up actions is provided below:

#### Air Quality Monitoring

- No Action/Limit Level exceedance for 1-hour TSP was recorded.
- No Action/Limit Level exceedance for 24-hour TSP was recorded.

#### Landscape and Visual Monitoring

• No non-conformity for landscape and visual was recorded.

#### Complaint Handling, Prosecution and Public Engagement

5. Summary of complaint/summons/prosecution in the reporting month is tabulated in **Table I**.

Table I Summary of Complaint/Summons/Prosecution in the Reporting Month

Event	<b>Event Details</b>		Follow-up/ Remedial	Status/ Remarks
Event	Number	<b>Brief Description</b>	Actions	
Complaints Received	0	-	-	-
Notification of Summons and Prosecutions Received	0	-	-	-

#### **Reporting Changes**

6. There were no reporting changes during the reporting month.

#### **Future Key Issues**

- 7. The key works or activities will be anticipated in the coming two months are as follows:
  - Super-structure works.
  - ABWF works
  - E&M installation

#### 1 INTRODUCTION

#### **Background**

- 1.1 Central Kowloon Route (CKR) is a 4.7km long dual 3-lane trunk road across Central Kowloon linking Yau Ma Tei Interchange in West Kowloon and the road network at Kai Tak Development and Kowloon Bay in East Kowloon. The underground tunnel section will be about 3.9km long. In particular, an underground tunnel of about 370m long in Kowloon Bay to the north of To Kwa Wan Typhoon Shelter will be constructed.
- 1.2 The Environmental Impact Assessment Report for Central Kowloon Route Design and Construction (Register No.: AEIAR-171/2013) was approved under the Environmental Impact Assessment Ordinance (EIAO) on 11 July 2013. An Environmental Permit (EP No.: EP-457/2013) was issued on 9 August 2013. Variations of Environmental Permit (VEP) was subsequently applied and an EP (EP No. EP-457/2013/C) was issued on 16 January 2017. The latest EP (EP No. EP-457/2013/D) was issued by Environmental Protection Department (EPD) on 15 June 2021.
- 1.3 The construction of the CKR had been divided into different sections. This Contract No. HY/2019/13 Central Kowloon Route Buildings, Electrical and Mechanical Works ("The Project") will include the architectural, civil and structural construction works of Yau Ma Tei Ventilation Building (YVB), Ho Man Tin Ventilation Building (HVB), Kai Tak Ventilation Building (KVB) and Central Kowloon Route Administration Building (ADB) for the CKR. The landscaping and electrical and mechanical (E&M) works within the building sites will be involved as well.
- 1.4 Cinotech Consultants Limited was assigned as the Environmental Team (ET) to undertake the EM&A works for the Project. The construction of this Contract was commenced on 12th October 2020.

#### **Purpose of the Report**

1.5 This is the 39<sup>th</sup> Monthly EM&A Report which summarises the impact monitoring results and audit findings for the EM&A programme in Yau Ma Tei West Area during the reporting period from 1<sup>st</sup> December 2023 – 31<sup>st</sup> December 2023. The Yau Ma Tei West Area site layout plan for the Project is shown in **Figure 1.1**.

#### **Project Organizations**

- 1.6 Different Parties with different levels of involvement in the project organization include:
  - Project Proponent Highways Department (HyD)
  - Engineer Representative (ER) Arup Mott MacDonald Joint Venture (AMMJV)
  - Environmental Team (ET) Cinotech Consultants Limited (Cinotech)
  - Independent Environmental Checker (IEC) Environmental Resources Management Hong Kong Limited (ERM)
  - Contractor Gammon Construction Limited (GCL)

1.7 The key contacts of the Project are shown in **Table 1.1**.

**Table 1.1 Key Project Contacts** 

Party	Role	Contact Person	Phone No.
AMMJV	Engineer Representative	Mr. Tommy Wong	3695 0419
Cinotech	Environmental Team	Ms. Betty Choi	2151 2072
ERM	Independent Environmental Checker	Ms. Mandy To	2271 3113
GCL	Contractor	Mr. Sampson Lo	9752 9118

1.8 The Organizational Structure for Environmental Management is shown in **Figure 1.2**.

#### Construction Activities undertaken during the Reporting Month

- 1.9 The construction programme is presented in **Appendix A**.
- 1.10 The major site activities undertaken in the reporting month included:
  - Super-structure works.
  - ABWF works
  - E&M installation

#### **Summary of EM&A Requirements**

- 1.11 The EM&A programme requires air quality monitoring, landscape and visual monitoring and environmental site audit. The EM&A requirements for each parameter are described in the following sections, including:
  - Environmental requirements and mitigation measures, as recommended in the EM&A Manual under the EP.
- 1.12 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 6 of this report.

## Statues of Environmental Licensing and Permitting

1.13 All permits/licenses obtained for the Project are summarized in **Table 1.2**.

Table 1.2 Summary of Environmental Licensing and Permit Status

	Valid		
Permit / License No.	From	То	Status
Environmental Permit (EP)			
EP-457/2013/D	15 Jun 2021	N/A	Valid
Notification of Construction World	ks under Air Pollution	n Control Ordinance	(APCO)
457325	19 Jun 2020	End of Project	Valid
Billing Account for Construction	Waste Disposal		
7037679	26 Jun 2020	N/A	Valid
Registration of Chemical Waste P	roducer – YVB		
5117-253-G2347-55	25 Aug 2020	N/A	Valid
Wastewater Discharge Licence - Y	MT	<u> </u>	
WT00036898-2020	25 Nov 2020	30 Nov 2025	Valid
Construction Noise Permit (YVB	Site - General Works	[Grouting, Piling]))	
GW-RE1191-23	5 Oct 2023	4 Mar 2024	Valid

#### 2 AIR QUALITY

#### **Monitoring Requirements**

2.1 As all of the air quality (1-hour TSP and 24-hour TSP) monitoring works in Yau Ma Tei West Area are currently covered under the Contract No. HY/2014/20 (Central Kowloon Route - Yau Ma Tei West), the corresponding monitoring parameters, equipment, methodology, results and established Action and Limit Levels could be referred to Section 3 of the EM&A report for Contract No. HY/2014/20 during this reporting month.

#### **Observations**

- 2.2 No Action/Limit Level exceedance was recorded for all 1-hour TSP and 24-hour TSP monitoring in the reporting month.
- 2.3 Site audits were carried out on a weekly basis to monitor and audit the timely implementation of air quality mitigation measures within the site boundaries of this Project. The summary of site audits is shown in **Table 6.1** of this report.

#### 3 NOISE

#### **Monitoring Requirements**

3.1 As all of the construction noise monitoring works in Yau Ma Tei West Area are currently covered under the Contract No. HY/2014/20 (Central Kowloon Route - Yau Ma Tei West), the corresponding monitoring parameters, equipment, methodology, results and established Action and Limit Levels could be referred to Section 3 of the EM&A report for Contract No. HY/2014/20 during this reporting month.

#### **Observations**

- 3.2 No Action/Limit Level exceedance was recorded for all construction noise monitoring in the reporting month.
- 3.3 Site audits were carried out on a weekly basis to monitor and audit the timely implementation of construction noise mitigation measures within the site boundaries of this Project. The summary of site audits is shown in **Table 6.1** of this report.

#### 4 WASTE MANAGEMENT

#### **Monitoring Requirements**

4.1 Waste generated from this Project includes inert construction and demolition (C&D) materials and non-inert C&D materials. Inert C&D waste includes soil, broken rock, broken concrete and building debris, while non-inert C&D materials are made up of C&D waste which cannot be reused or recycled and has to be disposed of at the designated landfill sites.

#### **Results and Observations**

4.2 The quantities of different types of waste generated in the reporting month are summarised in **Table 4.1**. Details of the amount of wastes generated by the major site activities of this Project during the reporting month is shown in **Appendix B**.

Table 4.1 Quantities of Waste Generated from the Project

Quantity							
Inert C&D Materials Non-inert C&D Materials							
Reporting	Total	Disposed as	Others, e.g.	Metals	Paper/cardboard	Plastics	Chemical
Period	Quantity	Public Fill	general	(in	Packaging	(in	waste (in
	Generated	(in '000m <sup>3</sup> )	refuse (in	'000kg)	(in '000kg)	'000kg)	'000kg)
	(in '000m <sup>3</sup> )		'000m <sup>3</sup> )	,	, , , , ,	,	J.
Dec 2023	0	0	0.248	0	0	0	0

4.3 Site audits were carried out on a weekly basis to monitor and audit to ensure that proper storage, transportation, and disposal practices of waste materials generated during construction activities, such as construction and demolition (C&D) materials and general refuse are being implemented. The summary of site audits is shown in **Table 6.1** of this report. The implementation status of the waste/chemical management measures in the reporting period are summarized in **Appendix** C.

#### 5 LANDSCAPE AND VISUAL

#### **Monitoring Requirements**

5.1 According to the EM&A Manual, site audits would be undertaken during the construction phase of the Project to check that the proposed landscape and visual mitigation measures are properly implemented and maintained as per their intended objectives. Site inspections of the implementation of landscape and visual mitigation measures would be undertaken at least once every two weeks during the construction period.

#### **Results and Observations**

- 5.2 Bi-weekly inspection of the implementation of landscape and visual mitigation measures within the site boundaries of this Project was conducted on 13 & 27 December 2023. The implementation status of the landscape and visual mitigation measures in the reporting period are summarized in **Appendix C**. The summary of observations and recommendations made for landscape and visual mitigation measures during site audits are shown in **Table 6.1** of this report.
- 5.3 No non-compliance of the landscape and visual impact was recorded in the reporting month.

#### **6** ENVIRONMENTAL AUDIT

#### **Site Audits**

- 6.1 Site audits were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site.
- 6.2 Site audits for Contract No. HY/2019/13 were conducted on 5, 13, 19, 27 December 2023 in the reporting month. Joint site inspection with the representative of IEC was conducted on 13 December 2023. No non-compliance was observed during the site audit.

#### **Implementation Status of Environmental Mitigation Measures**

- 6.3 According to Environmental Permit, the approved EIA Report (Register No.: AEIAR-171/2013), and the EM&A Manual of the Project, the mitigation measures detailed in the documents are recommended to be implemented during the construction phase. An Environmental Mitigation Implementation Schedule (EMIS) is provided in **Appendix C**.
- 6.4 The ET weekly site inspections were carried out during the reporting month and the observations and follow-up actions in Yau Ma Tei West Area are summarized in **Table 6.1**.

**Table 6.1 Observations and Recommendations of Site Inspections** 

Parameters	Date	Observations	Follow-up Actions
Water Quality	N/A	No environmental deficiency was identified in the reporting period.	N/A
Air Quality	19 December	Stock of more than 20 bags of cement should be covered.	Stock of cement has been covered.
Noise	N/A	No environmental deficiency was identified in the reporting period.	N/A
Waste / Chemical Management	N/A	No environmental deficiency was identified in the reporting period.	N/A
Land Contamination	N/A	No environmental deficiency was identified in the reporting period.	N/A
Landscape and Visual	N/A	No environmental deficiency was identified in the reporting period.	N/A
Permits /Licences	N/A	No environmental deficiency was identified in the reporting period.	N/A

#### **Implementation Status of Event and Action Plans**

6.5 The Event and Action Plans for air quality and construction noise could be referred to Appendices D and E of the EM&A report in Contract No. HY/2014/20 respectively.

#### Air Quality Monitoring

- No Action/Limit Level exceedance for 1-hour TSP was recorded.
- No Action/Limit Level exceedance for 24-hour TSP was recorded.

#### Construction Noise Monitoring

- No documented complaint on construction noise was received; no Action Level exceedance for day time construction noise monitoring was recorded.
- No Limit Level exceedance for day time construction noise monitoring was recorded in the reporting month.

#### Landscape and Visual Monitoring

• No non-conformity for landscape and visual was recorded.

## Summary of Complaint, Warning, Notification of any Summons and Successful Prosecution

6.6 No environmental complaints, warning, notifications of summons and successful prosecutions were received in the reporting month. The summary of environmental complaint, warning, summon and notification of successful prosecution for the Project is presented in **Appendix D** 

#### Status of Required Submission under Environmental Permit

6.7 Status of required submission under EP-457/2013/D during the reporting period are summarized in **Table 6.2**.

Table 6.2 Status of Required Submission under Environmental Permit

EP Condition (EP-457/2013/D)	Submission	Submission Date
Condition 3.4	Monthly EM&A Report (November 2023)	14 December 2023

#### 7 FUTURE KEY ISSUES

- 7.1 Major site activities undertaken for the coming two months include:
  - Super-structure works.
  - ABWF works
  - E&M installation
- 7.2 Key environmental issues in the coming two months include:
  - Stockpile accumulation on-site;
  - Water spraying for dust generating activities and on haul road;
  - Wastewater and runoff discharge from site;
  - Coverage of open manholes to avoid dirty runoff to drainage system;
  - Noise from operation of the equipment, especially for excavation works and machinery onsite;
  - Accumulation of general refuse and construction waste on-site;
  - Proper storage of construction materials on-site; and
  - Storage of chemicals/fuel and chemical waste/waste oil on-site.

#### 8 CONCLUSIONS AND RECOMMENDATIONS

#### **Conclusions**

8.1 This is the 39<sup>th</sup> Monthly EM&A Report which presents the EM&A works undertaken in Yau Ma Tei West Area during the reporting month from 1<sup>st</sup> December 2023 – 31<sup>st</sup> December 2023 in accordance with the EM&A Manual and the requirements under the EP.

#### Air Quality Monitoring

8.2 No Action/Limit Level exceedance was recorded for all 1-hour and 24-hour TSP monitoring in the reporting month.

#### Construction Noise Monitoring

8.3 No Action/Limit Level exceedance was recorded for all noise monitoring in the reporting month. HY/2014/20

#### Landscape and visual

8.4 No non-compliance was recorded in the reporting month.


#### Site Audit


8.5 4 ET joint weekly environmental site inspections were conducted in the reporting month. Joint weekly site inspections with the representative of ET, Engineer Representative and the Contractor were conducted on 5, 13, 19, 27 December 2023, whereas joint site inspection with the representative of IEC was conducted on 13 December 2023. All environmental deficiencies observed during site inspections were rectified by the Contractor.

#### Complaint, Notification of Summons and Successful Prosecution

8.6 No environmental complaint and no notifications of summons and successful prosecutions were received in the reporting month.

**FIGURES** 

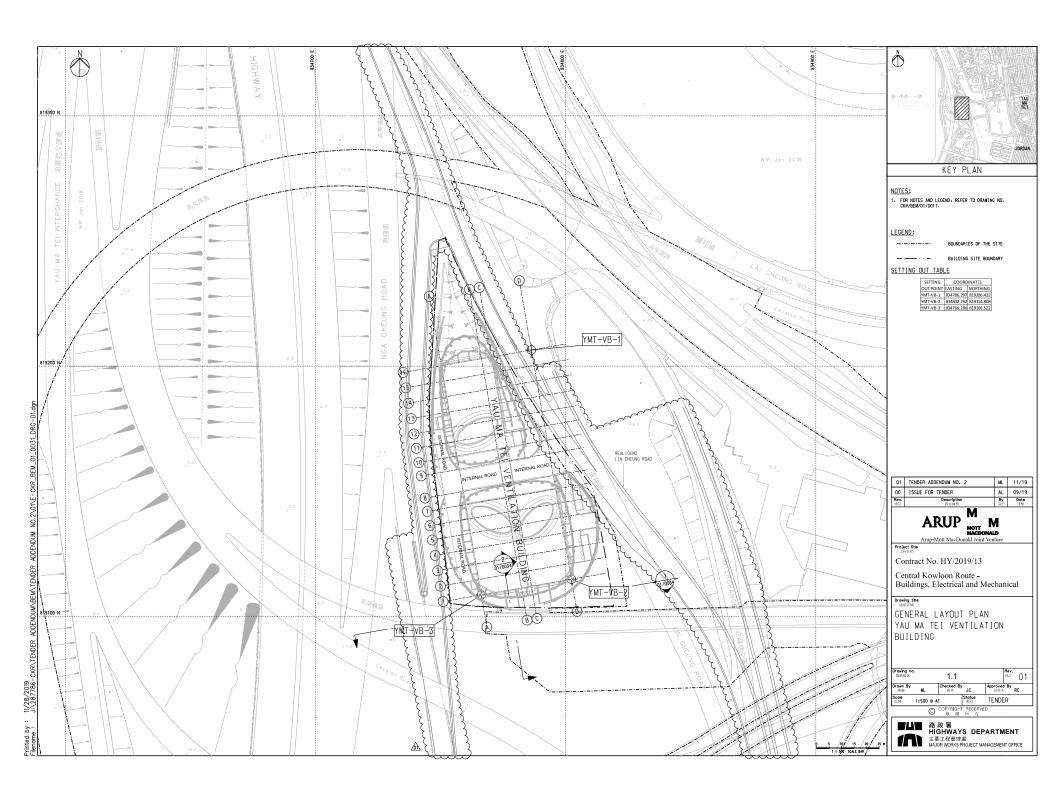


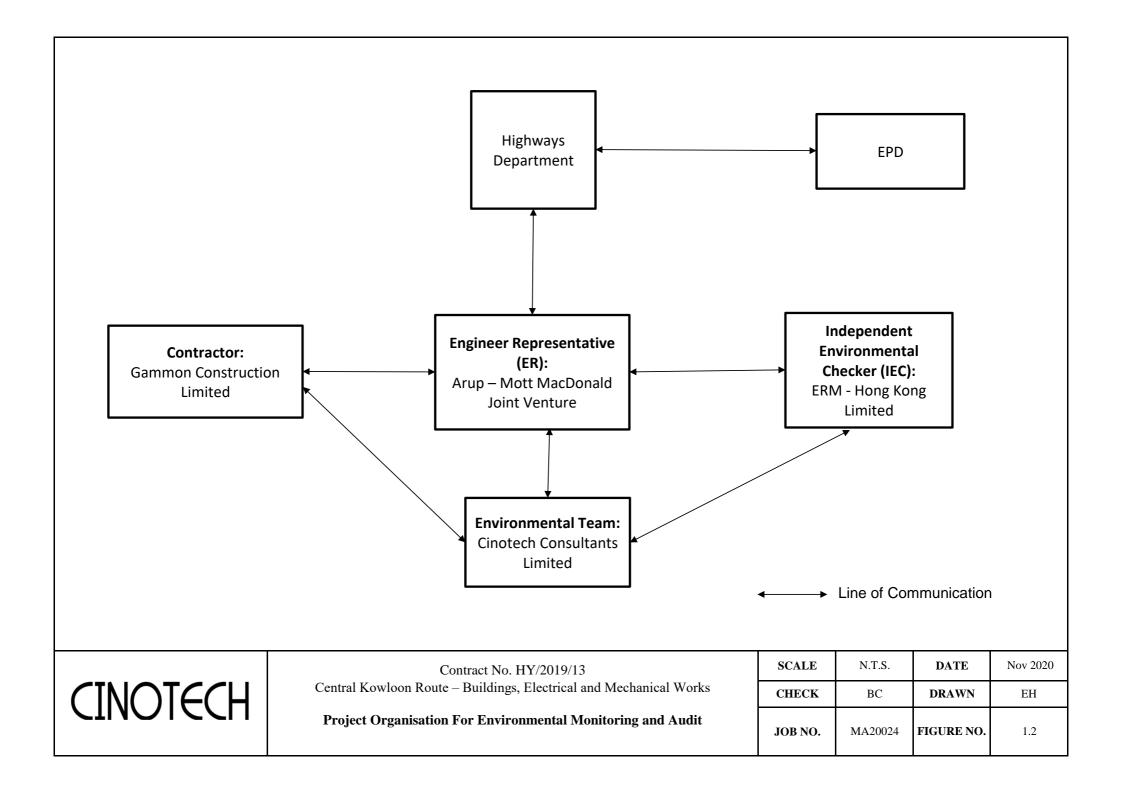

# APPENDIX A CONSTRUCTION PROGRAMME

# Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works Summary Programme



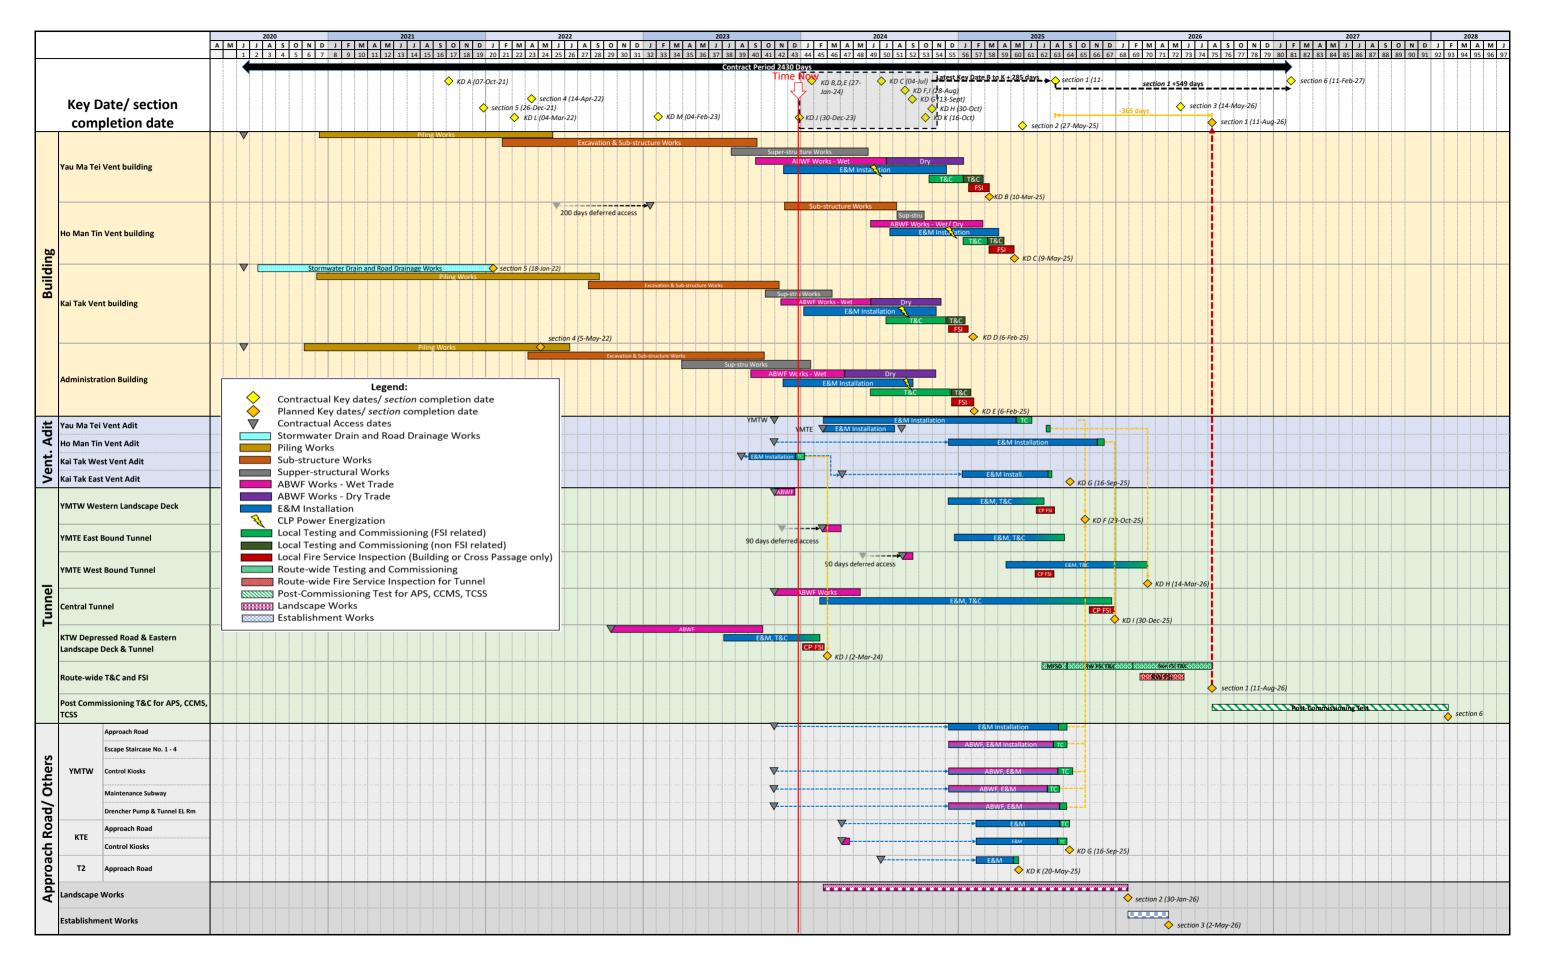

APPENDIX B SUMMARY OF WASTE GENERATION AND DISPOSAL RECORDS

#### **Monthly Summary Waste Flow Table**

[PS Clauses 25.24(11)S & 25.34(16)(a)]

Annex 4 to Appendix C

Name of Department: HyD Contract No.: HY/2019/13

Central Kowloon Route - Buildings, Electrical and Mechanical Works

Yau Ma Tei Site Area

Monthly Summary Waste Flow Table for 2023 (year)

	inertally statistically statistical restriction readers and the statistical restriction re											
		Actual Quanti	tes of Inert C&D	Materials Genera	nted Monthly			Actual	Quantites of C&	D Waste Generat	ed Monthly	
	<b>Total Quantity</b>	Hard Rock and	Reused in the	Reused in	Disposed as	Imported Fill	Metals	Paper /	Plastics	Chemical	Marine	Others, e.g.
	Generated	Large Broken	Contract	other Projects	Public Fill	(see Note 5)		cardboard	(see Note 3)	Waste	Sediment	general refuse
		Concrete	(see Note 5)	(see Note 5)	(see Note 5)			packaging		(see Note 5)	(see Note 7)	(see Note 5)
		(see Note 5)										
Month	(in '000m3)	(in '000m3)	(in '000m3)	(in '000m3)	(in '000m3)	(in '000m3)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m3)	(in '000m3)
Jan	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.076
Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.169
Mar	2.292	0.000	0.000	0.000	2.292	0.000	0.000	0.000	0.000	0.000	0.000	0.127
Apr	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.174
May	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.225
Jun	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.214
Sub-Total	2.292	0.000	0.000	0.000	2.292	0.000	0.000	0.000	0.000	0.000	0.000	0.984
Jul	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.274
Aug	0.049	0.000	0.000	0.000	0.049	0.000	0.000	0.000	0.000	0.000	0.000	0.443
Sep	0.049	0.000	0.000	0.000	0.049	0.000	0.000	0.000	0.000	0.000	0.000	0.522
Oct	0.141	0.000	0.000	0.000	0.141	0.000	0.000	0.000	0.000	0.000	0.000	0.310
Nov	0.152	0.000	0.000	0.000	0.152	0.000	0.000	0.000	0.000	0.000	0.000	0.395
Dec	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.248
Total (2023)	2.683	0.000	0.000	0.000	2.683	0.000	0.000	0.000	0.000	0.000	0.000	3.176
Total (whole)	87.232	0.000	0.000	57.554	29.678	0.000	0.000	0.000	0.000	0.000	0.000	3.629

Note:

- (1) The performance targets are given in PS Clause 25.24
- (2) The waste flow table shall also include C&D materails that are specified in the Contract to be imported for use at the Sites.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials, and water barriers
- (4)

The summary table shall be submitted to the Project Manager monthly together with the Waste Flow Table for review and monitoring in accordance with the PS Clause 25.24

(5) Density values and Bulk Factors adopted:

Hard Rock and Large Broken Concrete: 2.4 T/m3 (in-situ) Bulk Factor: 1.25

 Soil / Fill:
 2.0 T/m3 (in-situ)
 Bulk Factor:
 1.1

 Marine Sediment:
 1.7 T/m3 (in-situ)
 Bulk Factor:
 1.3

General Refuse: 400 kg/m3 Chemical Waste (mainly used lubricant): 900 kg/m3

Tree Trunk / Tree Stump: 850 kg/m3 (in-situ) Bulk Factor: 1.1

- (6) The reported and forecast volume figures are in "bulk" volume, with Bulk Factor applied as per Note (5)
- (7) This figure refers to marine sediment disposed via dumping at sea. Treated Sediment for Reuse on-site will be categorized into "Reused in the Contract"

APPENDIX C ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE (EMIS)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
	n Dust Impact	les de la companya de	ls er i i e	T ~		I	1	
S4.3.10	D1	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	- APCO - To control the dust impact to meet HKAQO and TM-EIA criteria	۸
S4.3.10	D2	Mitigation measures in form of regular watering under a good site practice should be adopted. Watering once per hour on exposed worksites and haul road should be conducted to achieve dust removal efficiencies of 91.7%. While the above watering frequencies are to be followed, the extent of watering may vary depending on actual site conditions but should be sufficient to maintain an equivalent intensity of no less than 1.3 L/m2 to achieve the dust removal efficiency.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	- APCO - To control the dust impact to meet HKAQO and TM-EIA criteria	^
S4.3.10	D3	Proper watering at exposed spoil should be undertaken throughout the construction phase.	Minimize dust impact at the	Contractor	All construction sites	Construction stage	- APCO - To control the dust	۸
		Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading.	nearby sensitive receivers				impact to meet HKAQO and TM-EIA criteria	۸
		Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads.						۸
		A stockpile of dusty material should not be extended beyond the pedestrian barriers, fencing or traffic cones.						۸
		The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle.						۸
		Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.						۸

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
		When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided and properly maintained as far as practicable along the site boundary with provision for public crossing. Good						۸
		site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period.						
		The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials.						۸
		Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously.						۸
		Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet						۸
		Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding.						N/A
		Any skip hoist for material transport should be totally enclosed by impervious sheeting.						N/A
		Every stock of more than 20 bags of cement or dry-pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides						ale
		Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed.						N/A
		Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system.						N/A

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
		Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabilizer within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.						N/A
S4.3.10	D6	Implement regular dust monitoring under EM&A programme during the construction stage.	Monitoring of dust impact	Contractor	Selected rep. dust monitoring station	Construction stage	- TM-EIA	۸
Construction	n Noise (Airbo	. /						
S5.4.1	N1	Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme.	Control construction airborne noise	Contractor	All construction sites	Construction stage	- Annex 5, TM-EIAO	^
		Machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.						^
		Plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs.						۸
		Silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works.						۸
		Mobile plant should be sited as far away from NSRs as possible and practicable.						^
		Material stockpiles, mobile container site office and other structures should be effectively utilized, where practicable, to screen noise from on-site construction activities.						N/A
S5.4.1	N2	Install temporary hoarding located on the site boundaries between noisy construction activities and NSRs. The conditions of hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level zone of NSRs through partial screening	Contractor	All construction sites	Construction stage	- Annex 5, TM-EIAO	۸

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
S5.4.1	N3	Install movable noise barriers (typical design is wooden framed barrier with a small-cantilevered on a skid footing with 25mm thick internal sound absorptive lining), acoustic mat or full enclosure, screen the noisy plants including air compressors, generators and handheld breakers, etc.	Sreen the noisy plant items to be used at all construction sites	Contractor	All construction sites where practicable	Construction stage	- Annex 5, TM-EIAO	N/A
S5.4.1	N4	Use 'Quiet plants'	Reduce the noise levels of plant items	Contractor	All construction sites where practicable	Construction stage	- Annex 5, TM-EIAO	۸
S5.4.1	N5	Loading/ unloading activities should be carried out inside the full enclosure of mucking out points.	Reduce the noise levels of loading/ unloading activities	Contractor	Mucking out locations	Construction stage	- Annex 5, TM-EIAO	۸
S5.4.1	N6	Sequencing operation of construction plants where practicable.	Operate sequentially within the same work site to reduce the construction airborne noise	Contractor	All construction sites where practicable	Construction stage	- Annex 5, TM-EIAO	^
S5.4.1	N7	Implement a noise monitoring programme under EM&A programme.	Monitor the construction noise levels at the selected representative locations	Contractor	Selected rep. noise monitoring station	Construction stage	- TM-EIAO	^
Water Quali	ity (Construction	on Phase)						
S6.9.1.1	W1	Construction Runoff At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the contractor prior to the commencement of construction.	To minimize water quality impact from the construction site runoff and general construction activities	Contractor	All construction sites where practicable	Construction stage	- Water Pollution Control Ordinance - ProPECC PN 1/94 - TM-EIAO - TM-DSS	^

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
		The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/ sediment trap. The sediment/ silt traps should be incorporated in the permanent drainage channels to enhance deposition rates.						۸
		The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt/ sand traps should be 5 minutes under maximum flow conditions. Sizes may vary depending upon the flow rate, but for a flow rate of 0.1 m3/s a sedimentation basin of 30 m3 would be required and for a flow rate of 0.5 m3/s the basin would be 150 m3. The detailed design of the sand/ silt traps shall be undertaken by the contractor prior to the commencement of construction.						۸
		All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. Exposed slope surfaces should be covered by tarpaulin or other means.						N/A
		The overall slope of the site should be kept to a minimum to reduce the erosive potential of surface water flows, and all traffic areas and access roads protected by coarse stone ballast. An additional advantage accruing from the use of crushed stone is the positive traction gained during prolonged periods of inclement weather and the reduction of surface sheet flows.						N/A
		All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas.						۸
		Measures should be taken to minimize the ingress of site drainage into excavations. If the excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.						^

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
		Open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50m3 should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.						۸
		Manholes should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.						۸
		Precautions be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes.						۸
		All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and site wheel washing facilities should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel wash bay to the public road should be paved with sufficient backfall toward the wheel wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.						^
		Oil interceptors should be provided in the drainage system downstream of any oil/ fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain.						۸
		Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts.						^

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
		All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby.						^
		Adopt best management practices.						۸
		All earth works should be conducted sequentially to limit the amount of construction runoff generated from exposed areas during the wet season (April to September) as far as practicable.						۸
S6.9.1.2	W2	Tunneling Works and Underground Works Cut-&-cover tunneling work should be conducted sequentially to limit the amount of construction runoff generated from exposed areas during the wet season (April to September) as far as practicable.	To minimize construction water quality impact from tunneling works	Contractor	All tunneling portion	Construction stage	- Water Pollution Control Ordinance - ProPECC PN 1/94 - TM-EIAO	N/A
		Uncontaminated discharge should pass through sedimentation tanks prior to off-site discharge.					- TM-DSS	۸
		The wastewater with a high concentration of SS should be treated (e.g. by sedimentation tanks with sufficient retention time) before discharge. Oil interceptors would also be required to remove the oil, lubricants and grease from the wastewater.						N/A
		Direct discharge of the bentonite slurry (as a result of D-wall) is not allowed. It should be reconditioned and reused wherever practicable. Temporary storage locations (typically a properly closed warehouse) should be provided on site for any unused bentonite that needs to be transported away after all the related construction activities area completed. The requirements in ProPECC PN 1/94 should be adhered to in the handling and disposal of bentonite slurries.						N/A

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
S6.9.1.3	W3	Sewage Effluent Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.	To minimize water quality from sewage effluent	Contractor	All construction sites where practicable	Construction stage	- Water Pollution Control Ordinance - TM-DSS	۸
S6.9.1.5	W4	Groundwater from Potential Contaminated Area:  No direct discharge of groundwater from contaminated areas should be adopted.  A discharge license under the WPCO through the Regional Office of EPD for groundwater discharge should be applied. Prior to the excavation works within these potentially contaminated areas, the groundwater quality should be reviewed during the process of discharge license application. The compliance to the Technical Memorandum on Standards for Effluents Discharged into Drainage on Sewerage Systems, Inland and Coastal Waters (TM-DSS) and the existence of prohibited substance should be confirmed. If the review results indicated that the groundwater to be generated from the excavation works would be contaminated, the contaminated groundwater should be either properly treated in compliance with the requirements of the TM-DSS or properly recharged into the ground.	To minimize groundwater quality impact from contaminated area	Contractor	Excavation areas where contamination is found		- Water Pollution Control Ordinance - TM-EIAO - TM-DSS	^

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
		If wastewater treatment is deployed, the wastewater treatment unit shall deploy suitable treatment process (e.g. oil interceptor / activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (e.g. TPH) to undetectable range. All treated effluent from wastewater treatment plant shall meet the requirements as stated in TM-DSS and should be discharged into the foul sewers.						۸
		If groundwater recharging wells are deployed, recharging wells should be installed as appropriate for recharging the contaminated groundwater back into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in the Section 2.3 of TM-DSS. The baseline groundwater quality shall be determined prior to the selection of the recharge wells, and submit a working plan (including the laboratory analytical results showing the quality of groundwater at the proposed recharge location(s) as well as the pollutant levels of groundwater to be recharged) to EPD for agreement. Pollution levels of groundwater to be recharged shall not be higher than pollutant levels of ambient groundwater at the recharge well. Prior to recharge, any prohibited substances such as TPH products should be removed as necessary by installing the petrol interceptor.						N/A
S6.9.1.6	W6	Accidental Spillage All the tanks, containers, storage area should be bunded and the locations should be locked as far as possible from the sensitive watercourse and stormwater drains.  The Contractor should register as a chemical waste producer if chemical	To minimize water quality impact from accidental spillage	Contractor	All construction site where practicable	Construction stage	- Water Pollution Control Ordinance - ProPECC PN 1/94 - TM-EIAO - TM-DSS	٨
		wastes would be generated. Storage of chemical waste arising from the construction activities should be stored with suitable labels and warnings.  Disposal of chemical wastes should be conducted in compliance with the requirements as stated in the Waste Disposal (Chemical Waste) (General) Regulation.						٨

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
S7.4.1	WM1	On-site sorting of C&D material	Separation of	Contractor	All construction	Construction	· DEVB (W) No. 6/2010	^
		Geological assessment should be carried out by competent persons on site during excavation to identify materials which are not suitable to use as aggregate in structural concrete (e.g. volcanic rock, Aplite dyke rock, etc.). Volcanic rock and Aplite dyke rock should be separated at the source sites as far as practicable and stored at designated stockpile area preventing them from delivering to crushing facilities. The crushing plant operator should also be reminded to set up measures to prevent unsuitable rock from ending up at concrete batching plants and be turned into concrete for structural use. Details regarding control measures at source site and crushing facilities should be submitted by the Contractor for the Engineer to review and agree. In addition, site records should also be kept for the types of rock materials excavated and the traceability of delivery will be ensured with the implementation of Trip Ticket System and enforced by site supervisory staff as stipulated under DEVB TC(W) No. 6/2010 for tracking of the correct delivery to the rock crushing facilities for processing into aggregates. Alternative disposal option for the reuse of volcanic rock and Aplite Dyke rock, etc. should be explored.	unsuitable rock from ending up at concrete batching plants and be turned into concrete for structural use	Contractor	sites	stage		
\$7.5.1	WM2	Construction and Demolition Material  Maintain temporary stockpiles and reuse excavated fill material for backfilling and reinstatement.	Good site practice to minimize the waste generation and recycle the	Contractor	All construction sites	Construction stage	· Land (Miscellaneous Provisions) Ordinance · Waste Disposal Ordinance	۸
		Carry out on-site sorting.	C&D materials as				· ETWB TCW No.	^
		Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate	far as practicable so as to reduce the amount for final				19/2005	۸
		Adopt 'selective demolition' technique to demolish the existing structures and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible.	disposal					N/A
		Implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified.						^
		Implement an enhanced Waste Management Plan similar to ETWBTC (Works) No. 19/2005 – "Environmental Management on Construction Sites" to encourage on-site sorting of C&D materials and to minimize their generation during the course of construction.						۸

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
\$7.5.1	WM3	C&D Waste  Standard formwork or pre-fabrication should be used as far as practicable in order to minimize the arising of C&D materials. The use of more durable formwork or plastic facing for the construction works should be considered. Use of wooden hoardings should not be used, as in other projects. Metal hoarding should be used to enhance the possibility of recycling. The purchasing of construction materials will be carefully planned in order to avoid over ordering and wastage.  The Contractor should recycle as much of the C&D materials as possible onsite. Public fill and C&D waste should be segregated and stored in different	Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction stage	Land (Miscellaneous Provisions) Ordinance     Waste Disposal Ordinance     ETWB TCW No. 19/2005	N/A
		containers or skips to enhance reuse or recycling of materials and their proper disposal. Where practicable, concrete and masonry can be crushed and used as fill. Steel reinforcement bar can be used by scrap steel mills. Different areas of the sites should be considered for such segregation and storage.						
S7.5.1		Excavated Contaminated Soils  Details of the mitigation measures on handling of the contaminated soil shall be referred to Section on Land Contamination below.	The contaminated soil will be excavated for onsite reuse	Contractor	РВН4	t of	· Practice Guide (PG) for Investigation and Remediation of Contaminated Land · GN/GM for land contamination	۸
S7.5.1	WM5	Land-based and Marine-based Sediment All construction plant and equipment shall be designed and maintained to minimize the risk of silt, sediments, contaminants or other pollutants being released into the water column or deposited in the locations other than designated location.	To control pollution due to marine sediment	Contractor	Along CKR alignment	Construction stage	· ETWB TCW No. 34/2002	A N/A
		All vessels shall be sized such that adequate draft is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash.						N/A

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
		Before moving the vessels which are used for transporting dredged material, excess material shall be cleaned from the decks and exposed fittings of vessels and the excess materials shall never be dumped into the sea except at the approved locations.						N/A
		Adequate freeboard shall be maintained on barges to ensure that decks are not washed by wave action.						N/A
		The Contractors shall monitor all vessels transporting material to ensure that no dumping outside the approved location takes place. The Contractor shall keep and produce logs and other records to demonstrate compliance and that journeys are consistent with designated locations and copies of such records shall be submitted to the engineers.						N/A
		The Contractors shall comply with the conditions in the dumping licence.						٨
		All bottom dumping vessels (Hopper barges) shall be fitted with tight fittings seals to their bottom openings to prevent leakage of material.						N/A
		The material shall be placed into the disposal pit by bottom dumping.						N/A
		Contaminated marine mud shall be transported by spit barge of not less than 750m3 capacity and capable of rapid opening and discharge at the disposal site.						N/A
		Discharge shall be undertaken rapidly and the hoppers shall be closed immediately. Material adhering to the sides of the hopper shall not be washed out of the hopper and the hopper shall remain closed until the barge returns to the disposal site.						N/A
		For Type 3 special disposal treatment, sealing of contaminant with geosynthetic containment before dropping designated mud pit would be a possible arrangement. A geosynthetic containment method is a method whereby the sediments are sealed in geosynthetic containers and, the containers would be dropped into the designated contaminated mud pit where they would be covered by further mud disposal and later by the mud pit capping at the disposal site, thereby fulfilling the requirements for fully confined mud disposal.						N/A

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
S7.5.1	WM6	Chemical Waste Chemical Waste that is produced, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, should be handled in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.	Control the chemical waste and ensure proper storage, handling and disposal	Contractor	All construction sites	Construction stage	Waste Disposal (Chemical Waste) (General) Regulation     Code of Practice on the Packaging, Labelling and Storage of Chemical	۸
		Containers used for the storage of chemical wastes should be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed, have a capacity of less than 450 L unless the specification has been approved by EPD, and display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the regulation.					Waste	^
		The storage area for chemical wastes should be clearly labelled and used solely for the storage of chemical waste, enclosed on at least 3 sides, have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20% of the total volume of waste stored in that area, whichever is the greatest, have adequate ventilation, covered to prevent rainfall entering, and arranged so that incompatible materials are adequately separated.	ne storage of chemical waste, enclosed on at least 3 sides, have an le floor and bunding of sufficient capacity to accommodate 110% me of the largest container or 20% of the total volume of waste at area, whichever is the greatest, have adequate ventilation, prevent rainfall entering, and arranged so that incompatible				^	
		Disposal of chemical waste should be via a licensed waste collector, be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Centre which also offers a chemical waste collection service and can supply the necessary storage containers, or be to a reuser of the waste, under approval from EPD.						۸
S7.5.1	WM7	General refuse generated on-site should be stored in enclosed bins or compaction units separately from construction and chemical wastes.	Minimize production of the general refuse and avoid odour, pest	Contractor	All construction sites	Construction stage	· Waste Disposal Ordinance	۸
		A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law.	and litter impacts					^
		Aluminum cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. Separate labelled bins for their deposit should be provided if feasible.						۸

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status	
		Office wastes can be reduced through the recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme should be considered by the Contractor.						^	
Land Contai	mination								
S8.9 & Appendix 8.4	LC2	Excavation of the Contaminated Soil Prior to commencement of the excavation works at the contamination zone, the zone should be clearly marked out on site and the surface levels recorded. Excavation of contaminated material should be undertaken using dedicated earth-moving plant.  The excavated contaminated soils would be stockpiled at designated area on	e, soil will be excavated for on-	soil will be excavated for onsite reuse	soil will be d. excavated for onsite reuse  commencement tof I construction works within the	Contractor PBH4	ll be ted for on-	Practice Guide (PG) for Investigation and Remediation of Contaminated Land - Guidance Notes for Contaminated Land	N/A
		site and covered by sheet to prevent dispersion of contamination during stockpiling.				contaminated area	Assessment and Remediation Guidance Manual for Jse of Risk-Based		
		The Contractor should pay attention to the selection of suitable groundwater lowering schemes and discharge points if the groundwater table is higher than the contaminated soils during excavation. The Contractor should also obtain a valid Water Pollution Control Ordinance (WPCO) discharge licence from EPD where applicable.					Remediation Goals (RBRGs) for Contaminated Land Management	N/A	
Hazard to Li									
S9.18	Н8	The driver and his assistant should be physically healthy, experienced and have good safe driving records. The driver should hold a proper driving licence for the approved transport truck. Dedicated training programme and regular road safety briefing sessions/ workshops should be provided to enhance their safe driving attitude and practice. Smoking should be strictly prohibited.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	/	^	
S9.18	Н9	Emergency response plans in case of road accident should be prepared and implemented. The driver and his assistant should be familiar with the emergency procedures including evacuation, and proper communication/ fire-fighting equipment should be provided to the driver and his assistant.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	/	۸	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
Landscape a	nd Visual							
S10.10.1 Table 10.11	LV3	Good Site Management Large temporary stockpiles of excavated material shall be covered with unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance.	Minimize visual impact	Contractor	Within Project site	Construction Phase	/	^
		Construction plant and building material shall be orderly and carefully stored in order to create a neat and tidy visual appearance.						۸
S10.10.1 Table 10.11	LV4	Screen Hoarding Decorative screen hoarding should be erected to screen the public from the construction area. It should be designed to be compatible with the existing urban context.	Minimize visual impact	Contractor	Within Project site	Construction Phase	/	۸
S10.10.1 Table 10.11	LV5	Lighting Control during Construction All lighting in the construction site shall be carefully controlled to minimize light pollution and night-time glare to nearby residencies and GIC. The Contractor shall consider other security measures, which shall minimize the visual impacts.	Minimize visual impact	Contractor	Within Project site	Construction Phase	/	۸
S10.10.1 Table 10.11	LV6	Erosion Control The potential for soil erosion shall be reduced by minimizing the extent of vegetation disturbance on site and by providing a protective cover over newly exposed soil.	Minimize landscape impact	Contractor	Within Project site	Construction Phase	/	۸

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
S10.10.1 Table 10.11		Tree Protection & Preservation  Carefully protected during construction. Tree protection measures will be detailed at the Tree Removal Application stage and plans submitted to the relevant Government Department for approval in due course in accordance with ETWB TC no. 3/2006.		Contractor	Within Project site		· 'Guidelines for Tree Risk Management and Assessment Arrangement on an Area Basis and on a Tree Basis', Greening, Landscape and Tree Management (GLTM) Section, DEVB · Latest recommended horticultural practices from GLTM Section,	N/A
S10.10.1 Table 10.11	LV8	Tree Transplantation For trees unavoidably affected by the Project that have to be removed, where practical transplantation will be chosen as the top priority method of removal. If this is not possible or practical compensatory planting will be provided for trees unavoidably felled (See LV10). For trees unavoidably affected by the Project works that are transplanted, transplantation must be carried out in accordance with ETWB TCW 2/2004 and 3/2006.		Contractor	Within Project site and designated off- site locations		· ETWB TCW 3/2006 · Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DEVB · ETWB TCW 2/2004	N/A
S10.10.1 Table 10.11	LV9	Compensatory Planting For trees unavoidably affected by the Project that have to be removed, where practical transportation will be chosen as the top priority method of removal but if this is not possible or practical compensatory planting will be provided for trees unavoidably felled. All felled trees shall be compensated for by planting trees to the satisfaction of relevant Government projects. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006.	, A	Contractor	Within Project site		ETWB TCW 3/2006     Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DEVB     ETWB TCW 2/2004	N/A

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
S10.10.1 Table 10.11	LV10	Screen Planting Tall screen/buffer trees, shrubs and climbers should be planted, in so far as is possible, to soften and screen proposed structures such as roads and central strip, vertical edges and buildings and to enhance streetscape greening effect where appropriate. Indiscriminate use of trees for screening must be avoided and the principle of 'right tree for the right place' must be followed. This detail will be provided at the Detailed Design stage. This measure may additionally form part of the compensatory planting and will improve and create a pleasant pedestrian environment.	Minimize visual impact and also enhance landscape	Contractor	Within Project site		· Guidelines on Greening of Noise Barriers, issued April 2012, GLTMS, DevB · ETWB TCW 2/2004	N/A
S10.10.1 Table 10.11	LV11	Green Roof Roof greening will be established on ventilation and administration buildings to reduce exposure to untreated concrete surfaces and particularly mitigate visual impact to VSRs at high levels.	Minimize landscape and visual impact	Contractor	Within Project site	Construction Phase	/	N/A
S10.10.1 Table 10.11	LV12	Reinstatement All works areas, excavated areas and disturbed areas for tunnel construction and temporary road diversion or any other proposed works shall be reinstated to former conditions or better, with reasonable landscape treatment and to the satisfaction of the relevant Government departments. (Specific mitigation for disturbance to public open space is detailed separately under LV14)		Contractor	Within Project site	Construction Phase	/	N/A
S10.10.1 Table 10.11	LV13	Reprovising of Public Open Space All areas of public open space affected by the Project will be reprovisioned either at the same location following the completion of temporary works, or at a separate site, as agreed with relevant Government departments. Open space should be re-provisioned in an enhanced manner.	Minimize landscape impact	Contractor	Within Project site	Phase	Open space should be re-provided in an enhanced manner.	N/A
Cultural He	ritage Impact (	Construction Phase)						
S11.4.4	СНІ	The contractor should be alerted during the construction on the possibility of locating archaeological remains and as a precautionary measure, AMO shall be informed immediately in case of discovery of antiquities or supposed antiquities in the subject sites.	To preserve any cultural heritage items which may be removed and damaged by the excavation	Contractor	During construction works for cut and cover tunnels	During the Construction Phase	· AMOs requirements	N/A

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementati on Stage	Requirements and/ or standards to be achieved	Implementation Status
EM&A Proj								
S13.2	EM1	An Independent Environmental Checker needs to be employed as per the EM&A Manual	Control EM&A Performance	Highways Department	All construction sites	Construction stage	· EIAO Guidance Note No. 4/2010 · TM-EIAO	^
S13.2-13.4	EM2	An Environmental Team needs to be employed as per the EM&A Manual.	Perform environmental monitoring & auditing	Highways Department/ Contractor	All construction sites	Construction stage	· EIAO Guidance Note No. 4/2010 · TM-EIAO	۸
		Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures;	- uuug					^
		An environmental impact monitoring needs to be implemented by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with.						۸

Remarks: EN	Remarks: EM&A Programme under EP-457/2013/D						
^	Compliance of mitigation measure;						
N/A N/A(1)	Not applicable at this stage; Not observed;						
*	Recommendation was made during site audit but improved/retified by the contractor;						
#	Recommendation was made during site audit but not yet improved/retified by the contractor;						
X	Non-compliance of mitigation measure;						
•	Non-compliance but rectified by the contractor.						

APPENDIX D SUMMARIES OF ENVIRONMENTAL COMPLAINT, WARNING, SUMMON AND NOTIFICATION OF SUCCESSFUL PROSECUTION

## Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works

### Appendix D - Summary of Environmental Complaint, Warning, Summon and Notification of Successful Prosecution

**Reporting Month:** Dec 2023

Log Ref.	Location	Received Date	Details of Complaint/ warning/ summon and prosecution	Investigation/ Mitigation Action	Status
N/A	N/A	N/A	N/A	N/A	N/A

Remarks: No environmental complaint, warning/summon and prosecution was received in the reporting period.

Statistical Summary of Environmental Complaints, Notifications of Summons and Successful Prosecutions

Reporting Period	Frequency	Details		
		Environmental Complaint Statistics		
	0	0	N/A	
Dec 2023	F	Environmental Non-compliance Statistic		
Dec 2023	0	0	N/A	
	Envir	ronmental Summon and Prosecution Statis	tic	
	0	0	N/A	

MA20024\App D 1
