
Vol. 4 of 5

EP-457/2013/D Central Kowloon Route Yau Ma Tei West Contract No. HY/2014/20 &

Buildings, Electrical and Mechanical Works Contract No. HY/2019/13 (Yau Ma Tei West area) July 2024

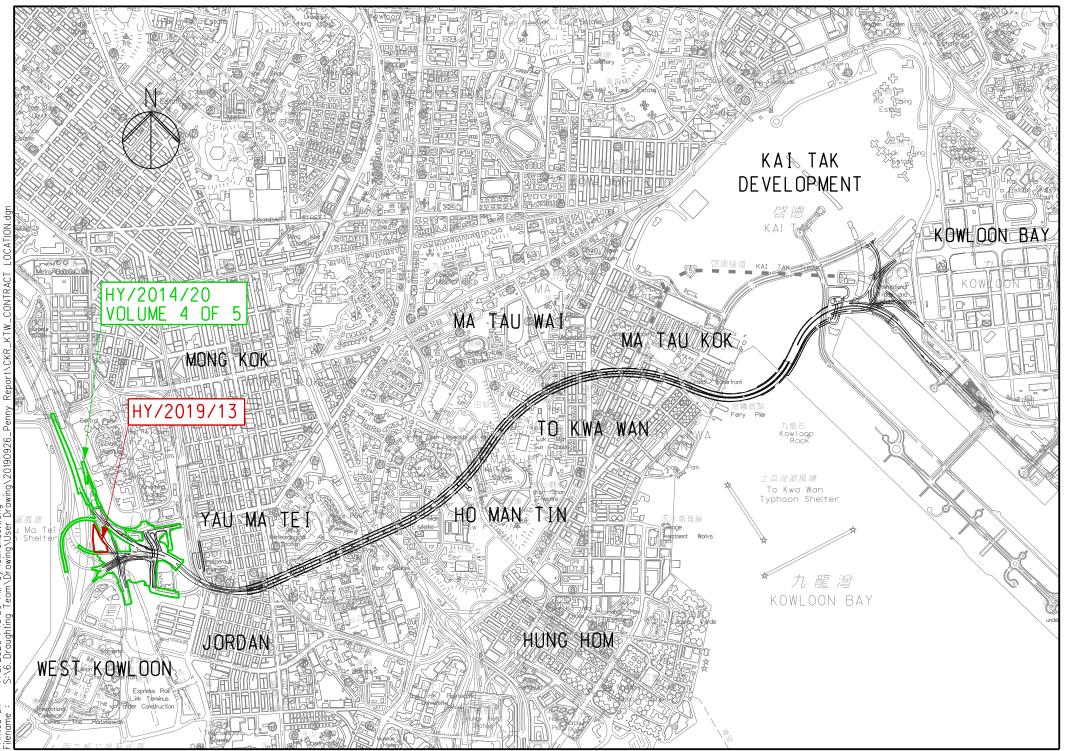

7/8/2020 1:43:56 PM by lawrence.wong 5:\6. Draughting Team\Drawing\User Dra Printed

Central Kowloon Route Yau Ma Tei West Contract No. HY/2014/20





Environmental Permit No. EP-457/2013/D

Central Kowloon Route

Independent Environmental Checker Verification

Works Contract:	Yau Ma Tei West (HY/2014/20)	
Reference Document/Plan		
Document/ Plan to be Certified / Verified:	Monthly EM&A Report No.66 (July 2024)	
Date of Report:	9 August 2024 (Rev. 1)	
Date received by IEC:	9 August 2024	

Reference EP Condition

Environmental Permit Condition:

Submission of Monthly EM&A Report of the Project

3.4 Four hard copies and one electronic copy of monthly EM&A Report shall be submitted to the Director within 2 weeks after the end of each reporting month throughout the entire construction period. The EM&A Reports shall include a summary of all non-compliance. The submissions shall be certified by the ET Leader and verified by the IEC as complying with the requirements as set out in the EM&A Manual before submission to the Director. Additional copies of the submission shall be provided to the Director upon request by the Director.

3.4

IEC Verification

I hereby verify that the above referenced document/plan complies with the above referenced condition of EP-457/2013/D.

Mondy 20.

Ms Mandy To Independent Environmental Checker

Date:

9 August 2024

Our ref: 0436942_IEC Verification Cert_YMTW_Monthly EM&A Rpt No.66.docx





Build King – SK ecoplant Joint Venture

Central Kowloon Route Contract HY/2014/20

Section of Yau Ma Tei West Section

Monthly EM&A Report No. 66

(Period from 1 to 31 July 2024)

Rev. 1

(9 August 2024)

	Name	Signature
Prepared by	Kako H.L. Ho (Assistant Environmental Consultant)	Ho
Checked & Reviewed by	Y.H. LAW (Senior Environmental Consultant)	yAdai
Approved & Certified by	Kevin W. M. Li (Environmental Team Leader)	K.

TABLE OF CONTENTS

EXECUTIVE SUMMARY

1.	BASIC PROJECT INFORMATION	.6
2.	ENVIRONMENTAL STATUS	.9
3.	MONITORING RESULTS	11
4.	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS	19
5.	EM&A SITE INSPECTION	21
6.	FUTURE KEY ISSUES	22
7.	CONCLUSION AND RECOMMENDATIONS	23

2

LIST OF APPENDICES

- A. Alignment and Works Area for the Contract No. HY/2014/20
- B. Construction Programme
- C. Project Organization Chart
- D. Dust Event-Action Plan (EAP)
- E. Noise Event-Action Plan (EAP)
- F. Environmental Mitigation Implementation Schedule (EMIS)
- G. Monitoring Schedules of the Reporting Month
- H. Calibration Certificate (Air Monitoring)
- I. Calibration Certificate (Noise)
- J. The Certification of Laboratory with HOKLAS Accredited Analytical Tests
- K. Location Plan of Noise and Air Quality Monitoring Station
- L. Monitoring Data (Air Monitoring)
- M. Monitoring Data (Noise)
- N. Waste Flow Table
- O. Statistics on Complaint, Notifications of Summons and Successful Prosecutions
- P. Monitoring Schedule of the Coming Month
- Q. Interim Report for the Complaint

EXECUTIVE SUMMARY

- A.1 Build King SK ecoplant Joint Venture ("Contractor") commenced the construction works of Highway Department (HyD) Central Kowloon Route Contract No. HY/2014/20 – Section of Yau Ma Tei West ("The Project") on 12 February 2019. This is the 66th monthly Environmental Monitoring and Audit (EM&A) report presenting the EM&A works carried out during the period from 1 July 2024 to 31 July 2024.
- A.2 A summary of the construction works reported by Main Contractor for the Project during the reporting month is listed below.

Construction Activities undertaken

- Noise Barrier C02, C03 & S01 (along Lin Cheung Road) at Portion 1E
- Slip Road A (Reinforced Concrete works for Noise Barrier C06 & V09) at Portion 1E
- Parapet Wall at Bridge B, B2, C, C2 and D at Portion 1B
- Parapet Wall at Abutment Wall Slip Road E & Installation of NB-C01 & V03 in Portion 1B
- Slip Road E in Portion 1A
- Slip Road E and F Widening Works (Variation Order)
- Recovery Area Roadworks at Portion 1B
- Landscaped construction at Segment 1 & 2 in Portion 1B
- Roadworks at Segment 1 to 4 at Portion 1B
- Fire Separation Wall FSW-1 at Segment 3 & 4 in Portion 1B
- Fire Separation Wall FSW-1 at Segment 1 & 2 in Portion 1B
- Abutment Wall at Emergency Access Road (West Side) in Portion 1D
- Escape Route Staircase No. 4 at Portion 1F
- Roadworks at Segment 10 to 12 in Portion 1F
- Fire Separation Wall FSW-2 at Segment 10 to 12 in Portion 1F
- Façade Wall at Segment 10 to 12 in Portion 1F
- Reinforced Concrete Works for Escape Route 1 and 2 in Portion 1F
- Upstand Wall and Column construction at Segment 5 (West Side) in Portion 1D
- Landscaped Deck construction at Segment 5A in Portion 1D
- Segments 8 and 9 Pile Cap, Upstand Wall & Column (West Side) including Hoi Wang Road Plant Room at Portion 1D
- A.3 A summary of regular construction noise and construction dust monitoring activities in this reporting period is listed below:

Regular construction noise monitoring during normal working hours

W-N1A, W-P11, W-N18, W-N25A	6 times
Construction dust (24-hour TSP) monitoring	
W-A1	6 times
W-A6	6 times
Construction dust (1-hour TSP) monitoring	
W-A1, W-A6	18 times

A.4 Bi-weekly inspection of the implementation of landscape and visual mitigation measures was conducted on 11 and 25 July 2024. Details of the audit findings and implementation

status are presented in Section 5.

- A.5 Joint weekly site inspections were conducted by representatives of the Contractor, Engineer and Contractor's ET on 4, 11, 18 and 25 July 2024. A joint site inspection with IEC was undertaken on 25 July 2024. Details of the audit findings and implementation status are presented in Section 5.
- A.6 Details of waste management are presented in Section 3.
- A.7 One Action Level of construction noise was triggered during the reporting month as documented complaints were received. No exceedance of Limit Level of construction noise was recorded in the reporting month. No exceedance of the Action and Limit Level of 24-hour TSP and 1-hour TSP was recorded in the reporting month.
- A.8 A total of one environmental complaint was received in the reporting month. After investigation with Contractor, precautionary measures had been proposed to the Contractor by ET. The interim reports for the complaints are shown in Appendix Q.
- A.9 No notification of summon or prosecution was received in this reporting period.
- A.10 A summary of the construction activities provided by Main Contractor in the next reporting month is listed below:

Construction Activities to be undertaken

- Along Lin Cheung Road remaining road works at Portion 1E
- Noise Barrier C02 Road Works in progress at Portion 1E
- Slip Road A backfilling, footing & wall construction for NB-C06 & V09 at Portion 1E
- Parapet Wall at Bridge B, B2, C, C2, D, E & F at Portion 1B, 1G
- Road Widening Works at Slip Road E & F in Portion 1A & 1B
- Slip Road E & F Road Works including Noise Barrier Installation (NB C01 at Slip Road E) in Portion 1A & 1B
- Fire Separation Wall FSW-1 at Segment 1 & 2 in Portion 1B
- Fire Separation Wall FSW-3 and FSW-4 at Bridge C2 in Portion 1D
- Abutment Wall at Emergency Access Road (West Side) in Portion 1D
- Roadworks at Segment 1, 2, 3, 4, 7, 10, 11 & 12A in Portion 1B & 1F
- Fire Separation Wall FSW-2 at Segment 10 to 12 in Portion 1F
- Façade Wall at Segment 10 to 12 in Portion 1F
- Reinforced Concrete works for Escape Route Staircase No. 1 to 2 at Portion 1F and 10
- Upstand Wall and Column construction at Segment 5 (West Side) in Portion 1D
- Landscaped Deck construction at Segment 5A in Portion 1D
- Reinforced Concrete works (Column) at Segment 8 & 9 and Washout Chamber in Portion 1D
- Portal installation for Landscaped Deck construction at Segment 5b, 8b & 9 in Portion 1D
- ABWF and E&M at HWR Plant Room Building in Portion 1D

1. BASIC PROJECT INFORMATION

- 1.1. Central Kowloon Route (CKR) is a 4.7 km long dual 3-lane trunk road in Central Kowloon linking Yau Ma Tei Interchange in West Kowloon with the road network on Kai Tak Development and Kowloon Bay in East Kowloon.
- 1.2. The Central Kowloon Route Design and Construction Environmental Impact Assessment Report (Register No.: AEIAR-171/2013) was approved with conditions by the Environmental Protection Department (EPD) on 11 July 2013. An Environmental Permit (EP 457/2013) was issued on 9 December 2013. Variations of EP (VEP) was subsequently applied for and the latest EP (EP-457/2013/D) was issued by EPD on 15 June 2021.
- 1.3. The construction of the CKR had been divided into different sections. This Contract No. HY/2014/20 Section of Yau Ma Tei West (YMTW) covers part of the construction activities located at Yau Ma Tei under the EP which includes:
 - Section of Yau Ma Tei West
 - i. Construction of an approximately 250m long Depressed Road at the western tunnel portal of CKR;
 - Construction of a Landscaped Deck structure above the western tunnel portal and Hoi Wang Road, including the associated civil engineering provisions and coordination with CKR-RMW contractor in respect of the remaining works for the Landscaped Deck;
 - iii. Construction of an underground Ventilation Adit connecting the tunnel ventilation system with the Yau Ma Tei Ventilation Building;
 - iv. Construction of approach roads and slip roads, including bridges and other associated structures, connecting CKR with the existing road networks:
 - Bridge B
 - Bridge C
 - Bridge D
 - Bridge G
 - Road D Structure
 - Box Structure E
 - Diversion of a section of existing drainage box culvert of approximately 215m in length;
 - v. Design and construction of the noise mitigation measures at Slip Roads A, C2, D, E, G, Hoi Wang Road, Lai Cheung Road and Lin Cheung Road;
 - vi. Design and construction of Smoke Ventilation System including Smoke Ventilator System including Smoke Ventilator System, Linear Heat Detection System, Pneumatic Air Supply System, the associated plant rooms, control system and power supply system for part of the Landscaped Deck;
 - vii. Design and construction of the façade system of the Landscaped Deck;
 - viii. Design and construction of lifts at the Landscaped Deck;

- ix. Associated roadworks, footpath, drainage, sewerage, watermains, street lighting, traffic aids, landscaping, electrical and mechanical works, instrument monitoring works and utility diversion works;
- x. Construction of civil engineering provisions and coordination with future tunnel E&M and TCSS contractor for installation of tunnel E&M and TCSS equipment;

The alignment and works area for the Contract No. HY/2014/20 – are shown in Appendix A.

1.4. A summary of the major construction activities undertaken in this reporting period is shown in Table 1.1. The construction programme is presented in Appendix B.

Table 1.1 Summary of the construction activities reported by Main Contractor during the Reporting

Month.

Construction Activities undertaken

- Noise Barrier C02, C03 & S01 (along Lin Cheung Road) at Portion 1E
- Slip Road A (Reinforced Concrete works for Noise Barrier C06 & V09) at Portion 1E
- Parapet Wall at Bridge B, B2, C, C2 and D at Portion 1B
- Parapet Wall at Abutment Wall Slip Road E & Installation of NB-C01 & V03 in Portion 1B
- Slip Road E in Portion 1A
- Slip Road E and F Widening Works (Variation Order)
- Recovery Area Roadworks at Portion 1B
- Landscaped construction at Segment 1 & 2 in Portion 1B
- Roadworks at Segment 1 to 4 at Portion 1B
- Fire Separation Wall FSW-1 at Segment 3 & 4 in Portion 1B
- Fire Separation Wall FSW-1 at Segment 1 & 2 in Portion 1B
- Abutment Wall at Emergency Access Road (West Side) in Portion 1D
- Escape Route Staircase No. 4 at Portion 1F
- Roadworks at Segment 10 to 12 in Portion 1F
- Fire Separation Wall FSW-2 at Segment 10 to 12 in Portion 1F
- Façade Wall at Segment 10 to 12 in Portion 1F
- Reinforced Concrete Works for Escape Route 1 and 2 in Portion 1F
- Upstand Wall and Column construction at Segment 5 (West Side) in Portion 1D
- Landscaped Deck construction at Segment 5A in Portion 1D
- Segments 8 and 9 Pile Cap, Upstand Wall & Column (West Side) including Hoi Wang Road Plant Room at Portion 1D
- 1.5. The project organisational chart specifying management structure and contact details are shown in Appendix C.
- 1.6. A summary of the valid permits, licences, and /or notifications on environmental protection for this Project is presented in Table 1.2

 Table 1.2 Summary of the Status of Valid Environmental Licence

Permit/ Licences/	r	Period		
Notification			Status Remark	
/Reference No.	From	То	Status	i i i i i i i i i i i i i i i i i i i
Environmental Permit				
EP-457/2013/D	15 Jun 2021	End of Project	Valid	_
Wastewater Discharge Li		Life of Project	, und	
WT10002994-2024	30 May 2024	31 May 2029	Valid	
Notification of Constructi				tion Dust) Regulation
438845	31 Oct 2018	End of Project	Notified	-
Chemical Waste Produce	r Registration	5		
WPN5213-229-B2527-02	31 Oct 2018	End of Project	Valid	-
Billing Account for Dispo	sal of Constructi	on Waste		
7032430	2 Nov 2018	End of Project	Valid	-
Disposal of Special Was	ste at Landfills	Admission Tick	et	
Nil	-	-	-	-
Collection of Public Fill	at Public Fill			
TM38-HY/2014/20-06	2 Jul 2024	31 Dec 2024	Valid	-
Construction Noise Permi	it	·		
GW-RE0749-24	22 Jun 2024	18 Sep 2024	Valid	General Site Activities
GW-RE0647-24	4 Jun 2024	10 Aug 2024	Valid	Erection of Sign Gantry G18 at Yau Ma Tei Interchange
GW-RE0687-24	18 Jun 2024	10 Aug 2024	Valid	Sign Face Demolition/ Erection at Yau Ma Tei Interchange
GW-RE0771-24	28 Jun 2024	31 Aug 2024	Valid	Portal Frame Erection at Hoi Wang Road Southbound
GW-RE0798-24	9 Jul 2024	10 Aug 2024	Valid	Remaining Works for Construction of Noise Barrier at Lin Cheung Road
GW-RE0844-24	19 Jul 2024	14 Sep 2024	Valid	Road Marking Works for Re-alignment of Lai Cheung Road
GW-RE0845-24	19 Jul 2024	14 Sep 2024	Valid	Sign Gantry G1 Modification at West Kowloon Highway Slip Road (Stage 1 & 2)

2. ENVIRONMENTAL STATUS

2.1. Environmental permit (EP) conditions under the EIAO, submission status under the EP and implementation status of mitigation measures had been reviewed and implemented on schedule. The status of required submissions under the EP (EP-457/2013/D) as of the reporting period for the Project are summarised in Table 2.1.

Table 2.1 Summary of Status of Required Submission for EP-457/2013/D for the Project

EP Condition (EP-457/2013/D)	Submission	Submission date
Condition 3.4	Monthly EM&A Report (June 2024)	11 July 2024

2.2. Details of the major construction activities undertaken in this reporting period are shown in Table 2.2.

Table 2.2 Summary of the Construction Activities Undertaken during the Reporting Month.

Construction activities undertaken	Remarks on progress
• Noise Barrier C02, C03 & S01 (along Lin Cheung Road) at Portion 1E	•99% completion
• Slip Road A (Reinforced Concrete works for Noise Barrier C06 & V09) at Portion 1E	•60% completion
• Parapet Wall at Bridge B, B2, C, C2 and D at Portion 1B	•55% completion
• Parapet Wall at Abutment Wall Slip Road E & Installation of NB- C01 & V03 in Portion 1B	•95% completion
Slip Road E in Portion 1A	• 95% completion
• Slip Road E and F Widening Works (Variation Order)	• 50% completion
• Recovery Area – Roadwork in Portion 1B	• 35% completion
• Landscaped Construction at Segment 1 & 2 in Portion 1B	• Completed
• Roadworks at Segment 1 to 4 in Portion 1B	• 30% completion
• Fire Separation Wall FSW-1 at Segment 3 & 4 in Portion 1B	• Completed
• Fire Separation Wall FSW-1 at Segment 1 & 2 in Portion 1B	• 10% completion
• Abutment Wall at Emergency Access Road (West Side) in Portion 1D	• 18% completion
• Escape Route Staircase No. 4 at Portion 1F	• Completed
• Roadworks at Segment 10 to 12 in Portion 1F	• 99% completion
• Fire Separation Wall FSW-2 at Segment 10 to 12 in Portion 1F	• 60% completion
• Façade Wall at Segment 10 to 12 in Portion 1F	• 20% completion
• Reinforced Concrete Works for Escape Route 1 and 2 in Portion 1F	• 90% completion
• Upstand Wall and Column construction at Segment 5 (West Side) in Portion 1D	• 20% completion
• Landscaped Deck construction at Segment 5A in Portion 1D	• 80% completion
• Segments 8 and 9 Pile Cap, Upstand Wall and Column (West Side) including Hoi Wang Road Plant Room at Portion 1D	• 80% completion

2.3. The drawing showing the project layout and the location of the monitoring station and environmental sensitive receivers are attached in Appendix A and Appendix K. Co-ordinates of the monitoring location are shown in Table 2.3.

Monitoring Location	Location ID	Latitude	Longitude
Yau Ma Tei Catholic Primary School (Hoi Wang Road)*	W-A1/W-N1A	22.31345	114.16409
Man Cheong Building	W-A6	22.308185	114.166033
Hydan Place	W-N18	22.30858	114.170185
Prosperous Garden Block 1	W-N25A	22.309846	114.168072
The Coronation Tower 1	W-P11	22.309824	114.165616

Table 2.3 Summary of the location of the monitoring stations

Remark: *The High Volume Sampler (HVS) at dust impact monitoring location W-A1 had been relocated on 6 Sep 2022 due to installation work of PV panel at Yau Ma Tei Catholic Primary School. The relocation of HVS was approved by ER and agreed with IEC.

3. MONITORING RESULTS

3.1. Monitoring Parameters

Air Quality

- 3.1.1. The impact monitoring had been carried out in accordance with section 5.8 of the approved EM&A Manual to determine the 1-hour and 24-hour total suspended particulates (TSP) levels at the monitoring locations in the reporting month.
- 3.1.2. The sampling frequency of at least once in every 6 days, shall be strictly observed at the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least 3 times in every 6 days should be undertaken when the highest dust impact occurs.
- 3.1.3. General meteorological conditions (wind speed, direction and precipitation) and notes regarding any significant adjacent dust producing sources had also been recorded throughout the impact monitoring period.

Noise

- 3.1.4. Construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). L_{eq} (30min) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays.
- 3.1.5. For all other time periods, Leq (5min) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria.
- 3.1.6. As supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.
- 3.2. Monitoring Equipment

Air Quality

- 3.2.1. 1-hour TSP levels and 24-hour TSP had been measured with direct reading dust meter and High Volume Samplers respectively. It has been demonstrated its capability in achieving comparable results with high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50).
- 3.2.2. The 1-hour TSP meter was calibrated by the manufacturer prior to purchasing. Zero response of the instrument was checked before and after each monitoring event. Operation of the 1-hour TSP meter followed manufacturer's Operation and Service Manual. The 24-hour TSP meter was calibrated against firmware 80570-8100-V1.0.4, annually. Operation of the 24-hour TSP meter followed manufacturer's Operation and Service Manual. Valid calibration certificates of dust monitoring equipment are attached in Appendix H.
- 3.2.3. A summary of the equipment that was deployed for the 24- hour averaged monitoring is shown in Table 3.1. The TSP monitoring was conducted as per the schedule presented in Appendix G.

3.2.4. The equipment used for 1-hour TSP and 24-hour TSP measurement and calibration are summarised in Table 3.1

Monitoring Parameter	Monitoring Equipment	Serial Number	Date of Calibration
	LD-5R Digital Dust Indicator	761172	28 Nov 2023
1-hour TSP	LD-5R Digital Dust Indicator	992821	28 Nov 2023
1-nour 1SP	PC-3A(E) Digital Dust Indicator	JC-2002222	19 Mar 2024
	PC-3A(E) Digital Dust Indicator	JC-2002225	19 Mar 2024
24-hour TSP	TE-5170X High Volume	1084	28 Jun 2024 and
	Sampler		17 Jul 2024
	TE-5170X High Volume	1050	28 Jun 2024 and
	Sampler		17 Jul 2024
	TE-5025A Calibration Kit	3465	15 Jan 2024

Table 3.1 Construction Dust Monitoring Equipment

<u>Noise</u>

- 3.2.5. Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications has been used for carrying out the noise monitoring. The sound level meter has been checked using an acoustic calibrator. The wind speed and other metrological data has been recorded from Hong Kong Observatory- King's Park meteorological station, along with portable wind speed meter stand by as back up when the information are not available from HKO.
- 3.2.6. Acoustic calibrators and sound level meters using for the monitoring is within the valid period and were calibrated per year. Valid calibration certificate of noise monitoring equipment is attached in Appendix I.
- 3.2.7. The details of equipment using for monitoring are listed in Table 3.2, as below:

Monitoring Equipment	Serial Number	Date of Calibration
Nti XL2 Sound Level Meter	A2A-09696-E0	2 Mar 2024
Rion NC-75 Sound Level Calibrator	34724244	3 Aug 2023

 Table 3.2 Monitoring Equipment Used in Monitoring

3.3. Monitoring Methodology and QA/QC results

Air Quality

- 3.3.1. The 1-hour TSP monitor, portable dust meters (Sibata Digital Dust Indicator Model LD-5R and PC-3A(E) digital dust indicator) was used for the impact monitoring. The 1-hour TSP meters provides a real time 1-hour TSP measurement based on 90° light scattering. Three 1-hour TSP level were logged per every six days.
- 3.3.2. The 24-hour TSP monitor, High Volume Samplers (Tisch TE-5170X High Volume Air Sampler) were used for the impact monitoring. The 24-hour TSP monitoring consists of the following:

- The HVS was set at the monitoring location, with electricity supply connected and secured;
- HVS was calibrated before commencing the 1st measurement;
- The filter paper was weight and provided by HOKLAS lab (Acumen Laboratory and Testing Limited and ALS Technichem (HK) Pty Ltd) before and after the sampling. Certificate of HOKLAS accredited laboratory can be referred to Appendix J;
- The airflow over time during sampling process was recorded by the HVS.
- 3.3.3. HVSs was free-standing with no obstruction. The following criteria were considered in the installation of the HVS:
 - Appropriate support to secure the samples against gusty wind needed to be provided the monitoring station;
 - A minimum of 2m separation from walls, parapets and penthouses was required for rooftop samplers;
 - No furnace or incinerator flues was nearby;
 - Airflow around the sampler was unrestricted; and
 - Permission could be obtained to set up the samplers and gain access to the monitoring station.
- 3.3.4. Preparation of Filter Papers
 - Glass fiber filters were labelled and sufficient filters that were clean and without pinholes were selected;
 - ◆ All filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25°C and not varied by more than ±3°C; the relative humidity (RH)was 40%; and
 - Acumen Laboratory and Testing Limited and ALS Technichem (HK) Pty Limited, as HOKLAS accredited laboratory, implemented comprehensive quality assurance and quality control programmes on the filters.

3.3.5. Field Monitoring

- The power supply was checked to ensure that the HVS was working properly;
- The filter holder and area surrounding the filter were cleaned;
- The filter holder was removed by loosening the foul bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully;
- The filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter;
- The swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges;
- The shelter lid was closed and secured with an aluminum strip;
- The HVS was warmed- up for about 5 minutes to establish run- temperature conditions;
- A new flow rate record sheet was inserted into the flow recorder;
- ◆ The flow rates of the HVS was checked and adjusted to between 0.64-1.52m³min⁻¹, which was within the range specified in the EM&A Manual (i.e. 0.6- 1.7 m³min⁻¹);

- The programmable timer was set for a sampling period of 24 hours, and the starting time, weather condition and filter number were recorded;
- The initial elapsed time was recorded;
- At the end of sampling, the sampled filter was removed carefully and folded in half so that only surfaces with collected particulate matter were in contact;
- The filter paper was placed in a clean plastic envelope and sealed; all monitoring information was recorded on a standard data sheet and
- The filters were sent to (Acumen Laboratory and Testing Ltd and ALS Technichem (HK) Pty Ltd) for analysis.
- 3.3.6. Maintenance and Calibration
 - The HVS and their accessories were maintained in a good working condition. For example, motor brushes were replaced routinely and electrical wiring was checked to ensure a continuous power supply; and
 - ◆ The flow rate of each HVS with mass flow controller was calibrated using an orifice calibrator, Initial calibrations of the dust monitoring equipment were conducted upon installation and prior to commissioning. Five- point calibration was carried out for HVS using TE-5025 Calibration Kit. HVS is calibrated bimonthly. The calibration records for the HVS is given in Appendix H.
- 3.3.7. Wind Data Monitoring
 - The wind speed has been recorded from Hong Kong Observatory- King's Park meteorological station, along with portable wind speed meter stand by as back up when the information are not available from HKO.

<u>Noise</u>

- 3.3.8. All noise measurements by the meter were set to FAST response and on the A-weighted equivalent continuous sound pressure level (L_{eq}) in decibels dB(A). $L_{Aeq(30mins)}$ was used as the monitoring metric for the time period between 0700 –1900 hours on normal weekdays. The measured noise levels were logged every 5 minutes throughout the monitoring period.
- 3.3.9. Prior to the noise measurement, the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Checking was conducted before and after the monitoring. The calibration level before and after the noise measurement is agreed to within 1.0 dB(A).
- 3.3.10. Noise measurements should not be made in presence of fog, rain, wind with a steady speed exceeding 5 ms⁻¹ or wind with gusts exceeding 10 ms⁻¹. The wind speed was checked with a portable wind speed meter capable of measuring with speeds in ms⁻¹.
- 3.4. Monitoring Locations

Air Quality

3.4.1. During the site visit, both of the original proposed dust monitoring locations were rejected due to the condition at The Coronation was not favourable for monitoring and

the access was declined by the management office of Hong Kong Community College (HKCC) of PolyU. Two alternative air monitoring stations Yau Ma Tei Catholic Primary School (Hoi Wang Road) and Man Cheong Building had been proposed by ET and approved by IEC. 2 designated air monitoring locations were identified and agreed with IEC and EPD. Details of air monitoring stations are described in Table 3.3. The location plan of air quality monitoring stations is shown in Appendix K.

Air Quality Monitoring Station	Dust Monitoring Station
W-A1	Yau Ma Tei Catholic Primary School (Hoi Wang Road)
W-A6	Man Cheong Building

Table 3.3 Location of t	e Dust Moni	toring Stations
-------------------------	-------------	-----------------

<u>Noise</u>

3.4.2. During the site visit, one of the original proposed noise monitoring locations Tak Cheong Building was rejected by the president of the owner's corporation. Alternative noise monitoring station Hydan place had been proposed by ET and approved by IEC. 4 noise sensitive receivers designated noise monitoring locations were identified and agreed with IEC and EPD. The designated monitoring stations are identified and access was granted by the premises. The details of noise monitoring stations are described in Table 3.4 and the location plan of noise monitoring station is shown in Appendix K.

6				
Noise Monitoring Station	Identified Noise Monitoring Station	Type of Measurement		
W-N1A	Yau Ma Tei Catholic Primary School (Hoi Wang Road)	Façade		
W-N18	Hydan Place	Façade		
W-N25A	Prosperous Garden Block 1	Façade		
W-P11	The Coronation Tower 1	Façade		

Table 3.4 Noise Monitoring Stations

- 3.5. Monitoring date, time, frequency and duration
- 3.5.1. A summary of impact monitoring duration, sampling parameter and frequency is presented in Table 3.5.

Impact Monitoring	Duration	Sampling Parameter	Frequency
Dust	1-hour continuous measurement	1-hour TSP	3 times per six days
Dust	24-hour continuous sampling	24-hour TSP	Once per six days
Noise	30-minute continuous measurement	Leq 30 min, L10 and L90 as reference.	Once per week (0700-1900)

Table 3.5 Summary of Impact Monitoring Programme

3.6. Result Summary

Air Quality

3.6.1. According to our field observations, the major dust source identified at the designated air quality monitoring stations in the reporting month are summarised in Table 3.6.

Tuble 5.0 Observation at Dust Montoning Stations		
Monitoring Station	Major Dust Source	
W-A1	Nearby traffic	
W-A6	Nearby traffic	

Table 3.6 Observation at Dust Monitoring Stations

- 3.6.2. Air quality impact monitoring for the reporting month was carried out on 2, 6, 12, 18, 24 and 30 July 2024.
- 3.6.3. The results for 1-hour TSP and 24-hour TSP are summarized in Table 3.7 and Table 3.8. The measurement data and details of influencing factors such as weather conditions and site observation are presented in Appendix L.

Monitoring Location	Range(µg/m ³)	Action Level(µg/m3)	Limit Level(µg/m3)
W-A1	51 - 67	319	500
W-A6	54 - 69 306		500
Ta	ble 3.8 Summary of 24-ho	our TSP Monitoring Result	S
Monitoring Location	Range(µg/m ³)	Action Level(µg/m3)	Limit Level(µg/m3)
W-A1	30 - 149	167	260

166

260

21 - 91

Table 3.7 Summar	ry of 1-hour TSP	Monitoring Results
------------------	------------------	--------------------

<u>Noise</u>

W-A6

3.6.4. According to our field observations, the major noise source identified at the designated noise monitoring station in the reporting month are summarised in Table 3.9:

Table 3.9 Observation at Noise Monitoring Stations

Monitoring Station	Major Noise Source
W-N1A	Nearby traffic
W-N18	Nearby traffic
W-N25A	Nearby traffic
W-P11	Nearby traffic

- 3.6.1. The construction noise impact monitoring for the reporting month was carried out on 2, 6, 12, 18, 24 and 30 July 2024.
- 3.6.2. The result for noise monitoring is summarized in Table 3.10. The measurement data are shown in Appendix M.

Time	Monitoring			Range, dB(A))		
Period	location	Parameter	\mathbf{L}_{eq}	L ₁₀	L ₉₀	Action Level	Limit Level#
	W-N1A*		67.9 – 69.6	69.9 - 73.2	64.0 - 65.8		70dB(A) or 65 dB(A) during examination
Normal working hour	W-N18	T	66.6 – 69.6	71.4 - 73.2	60.5 - 68.0	When one documented	
from 0700- 1900	W-N25A	Leq 30min	68.5 - 70.8	71.6 - 75.3	58.8 - 68.1	complaint is received	75dB(A)#
	W-P11		64.7 – 65.6	68.1 – 69.1	61.9 - 63.2		

Table 3.10 Summary of Noise Monitoring Results

Remarks: 1. # If works are to be carried out during restricted hours, the conditions in the construction noise permit by the Noise Control Authority have to be followed.

2. *No examination was scheduled at Yau Ma Tei Catholic Primary School during the monitoring date. The limit level of W-N1A would be 70 dB(A).

Waste management

3.6.3. The waste generated from this Project includes inert C&D materials, and non-inert C&D materials. Non-inert C&D materials are made up of general refuse, vegetative wastes and recyclable wastes such as plastics and paper/cardboard packaging waste. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarised in Table 3.11. Details of cumulative waste management data are presented as a waste flow table in Appendix N.

			Q	uantity		
				Non-inert C&	D Materials	
Reporting period	Inert C&D Materials (in 'tonnes)	Chemical Waste (in'000 Kg)	Others, e.g. General Refuse disposed at	Rec	cycled materials	5
			Landfill (in 'tonnes)	Paper/card board (in '000 Kg)	Plastics (in '000 Kg)	Metals (in '000 Kg)
July 2024	2236.87	0.00	97.84	0.00	0.51	44.06

Table 3.11 Quant	ities of waste gener	ated from the Project
------------------	----------------------	-----------------------

4. SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS

4.1. The Environmental Complaint Handling Procedure is shown in below Table 4.1:

Table 4.1 Environmental Complaint Handling Procedure			
Complaint Received via Project Hotline	Complaint Received via 1823 or from other government departments		
Contractor notify ER, ET and IEC	ER notify Contractor, ET and IEC		
• •	o the complaint database. Contractor, ER and ET to gation of complaint		
If complaint is considered not valid	If complaint is found valid		
ET or ER to reply the complainant if necessary	Contractor to identify and implement remedial measures in consultation with the IEC, ET and ER.		
The ER, ET and IEC to review the effective of the Contractor's remedial measures and updated situation; ET to undertake addite monitoring and audit to verify the situation necessary, and oversee that circumstances let to the complaint do not recur. ER to con- further inspection as necessary.			
complaint investigation and follow-up actions st measures and additional monitoring identified	tractor to prepare interim report on the status of the ipulated above, including the details of the remedial or already taken, for submission to EPD within the igned by the EPD		
The FT to record the details of the complaint res	ults of the investigation, subsequent actions taken to		
address the complaint and updated situation inc	cluding the effectiveness of the remedial measures,		
supported by regular and additional monitoring results in the monthly EM&A reports			

Table 4.1 Environmental Complaint Handling Procedure

- 4.2. Should non-compliance of the criteria occur, action in accordance with the Event and Action Plan in Appendix D and Appendix E shall be carried out.
- 4.3. One Action Level of construction noise was triggered during the reporting month as documented complaints were received. No exceedance of Limit Level of construction noise was recorded in the reporting month. No exceedance of the Action and Limit Level of 24-hour TSP and 1-hour TSP was recorded in the reporting month.
- 4.4. A total of one environmental complaint was received in the reporting month. After investigation with Contractor, precautionary measures had been proposed to the Contractor by ET. The interim reports for the complaints are shown in Appendix Q.
- 4.5. No non-compliance was reported in the reporting month.
- 4.6. Statistics on complaints, notifications of summons and successful prosecutions are summarized in Appendix O.

5. EM&A SITE INSPECTION

- 5.1. Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting period, four (4) site inspections were carried out on 4, 11, 18 and 25 July 2024, along with bi-weekly inspection of the implementation of landscape and visual mitigation measures conducted on 11 and 25 July 2024.
- 5.2. A joint site inspection with IEC were undertaken on 25 July 2024. Minor deficiency was observed during weekly site inspection. Key observations during the site inspections are summarized in Table 5.1.

Date	Environmental Observations	Follow-up Status
4 July 2024	1. Drip tray should be provided under chemical container at Plant Room.	1. Chemical container has been removed.
11 July 2024	1. Drip tray should be provided for chemical containers at Portion 17.	1. Chemical containers have been provided with drip tray.
18 July 2024	1. Drip tray should be provided for chemical containers at Road D.	1. Chemical containers have been provided with drip tray.
25 July 2024	1. Drip tray should be provided for chemical container at Portal Entrance.	1. Chemical container have been provided with drip tray.

Table 5.1 Site Observations

- 5.3. The Contractor had rectified all observation identified during environmental site inspections in the reporting period.
- 5.4. According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents are implemented as much as practical during the reporting period. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in Appendix F.

6. **FUTURE KEY ISSUES**

6.1. Work to be undertaken in the next reporting month are:


Construction Activities to be undertaken

- Along Lin Cheung Road remaining road works at Portion 1E
- Noise Barrier C02 Road Works in progress at Portion 1E
- Slip Road A backfilling, footing & wall construction for NB-C06 & V09 at Portion 1E
- Parapet Wall at Bridge B, B2, C, C2, D, E & F at Portion 1B, 1G
- Road Widening Works at Slip Road E & F in Portion 1A & 1B
- Slip Road E & F Road Works including Noise Barrier Installation (NB C01 at Slip Road E) in Portion 1A & 1B
- Fire Separation Wall FSW-1 at Segment 1 & 2 in Portion 1B
- Fire Separation Wall FSW-3 and FSW-4 at Bridge C2 in Portion 1D
- Abutment Wall at Emergency Access Road (West Side) in Portion 1D
- Roadworks at Segment 1, 2, 3, 4, 7, 10, 11 & 12A in Portion 1B & 1F
- Fire Separation Wall FSW-2 at Segment 10 to 12 in Portion 1F
- Façade Wall at Segment 10 to 12 in Portion 1F
- Reinforced Concrete works for Escape Route Staircase No. 1 to 2 at Portion 1F and 10
- Upstand Wall and Column construction at Segment 5 (West Side) in Portion 1D
- Landscaped Deck construction at Segment 5A in Portion 1D
- Reinforced Concrete works (Column) at Segment 8 & 9 and Washout Chamber in Portion 1D
- Portal installation for Landscaped Deck construction at Segment 5b, 8b & 9 in Portion 1D
- ABWF and E&M at HWR Plant Room Building in Portion 1D
- 6.2. Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise and waste management.
- 6.3. The tentative schedule of regular construction noise monitoring, 1-hour TSP and 24-hour TSP monitoring in the next reporting period is presented in Appendix P.
- 6.4. The construction programme for the Project for the next reporting month is presented in Appendix B.

7. CONCLUSION AND RECOMMENDATIONS

- 7.1. This 66th monthly EM&A Report presents the EM&A works undertaken during the period from 1 July 2024 to 31 July 2024 in accordance with the EM&A Manual and the requirement under EP- 457/2013/D.
- 7.2. Air quality (including 1-hour TSP and 24-hour TSP) and noise impact monitoring were carried out in the reporting period.
- 7.3. Weekly environmental site inspections were conducted during the reporting period. A joint site inspection with IEC were carried out on 25 July 2024. Minor deficiency was observed during site inspection and was rectified within the specified deadlines. The environmental performance of the Project was therefore considered satisfactory.
- 7.4. One Action Level of construction noise was triggered during the reporting month as documented complaints were received. No exceedance of Limit Level of construction noise was recorded in the reporting month. No exceedance of the Action and Limit Level of 24-hour TSP and 1-hour TSP was recorded in the reporting month.
- 7.5. A total of one environmental complaint was received in the reporting month. After investigation with Contractor, precautionary measures had been proposed to the Contractor by ET. The interim reports for the complaints are shown in Appendix Q.
- 7.6. No non-compliance was reported in the reporting month.
- 7.7. The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.


Appendix A Alignment and Works Area For the Contract No. HY/2014/20

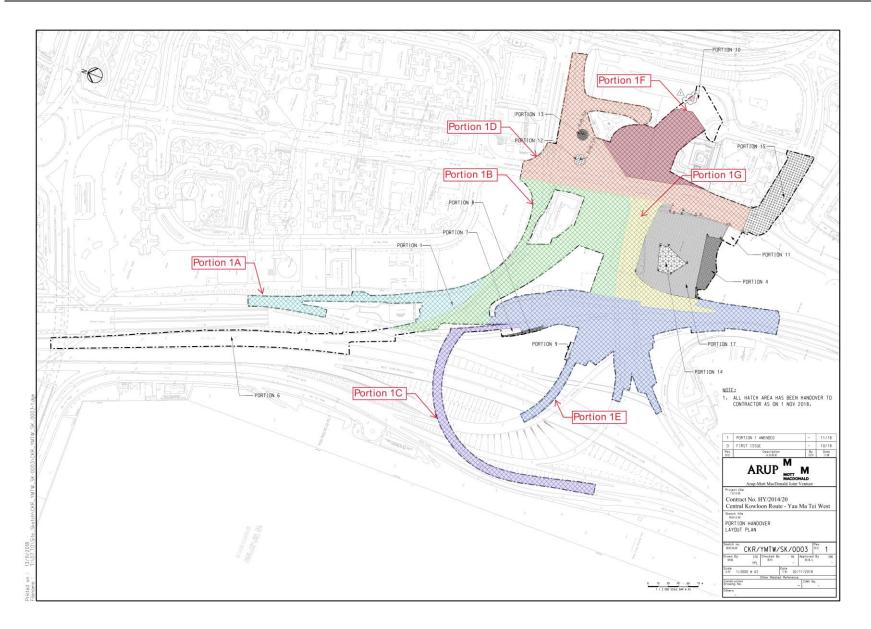

Appendix B Construction Programme

27.0 2736 2837 2000 2831 2831 2831 2831 2831 2831 2831 2831	01 Aboli A 01 Aboli A 01 Aboli A 19 Atar-19 A 11 Feb-19 A 11 Feb-19 A 11 Feb-19 A 11 Feb-19 A 11 Feb-19 A 11 Feb-19 A 17 Jon-19 A 27 Sep-19 A 19 Feb-24 A 01 Mar-24 A 28 Nov-24	23Apr-28 28Apr-26 28Apr-25 07Aby-29A 30Apr-25 30Apr-25 05Abr-25 05Abr-25 07Abr-25 05Abr-25 05-Abr-25 05-Dec-23A 10Apr-25 10Abr-24A								
2371 2331 2331 2331 2234 1971 1531 340 155 152 152 152 152 152	01-Am 18A 19-Mar-19A 11-Feb-19A 11-Feb-19A 11-Feb-19A 11-Feb-19A 17-Jun-19A 27-Sep-19A 19-Feb-24A 01-Mar-24A	28-Apr-25 07-Nov-20 A 30-Jun-25 30-Jun-25 05-Mar-25 07-Nov-24 05-Dec-23 A 10-Apr-25		••••••••••••••••••••••••••••••••••••••						
600 2331 2331 2214 1971 1531 340 215 5192 296 60 505 150	19-Mar-19 A 11-feb-19 A 11-feb-19 A 11-feb-19 A 11-feb-19 A 17-Jun-19 A 27-Sep-19 A 19-feb-24 A 19-feb-24 A 01-Mar-24 A	07-Nov-20 A 30-Jun-25 30-Jun-25 05-Mar-25 07-Nov-24 05-Dec-23 A 10-Apr-25								
600 2331 2331 2214 1971 1531 340 215 5192 296 60 505 150	19-Mar-19 A 11-feb-19 A 11-feb-19 A 11-feb-19 A 11-feb-19 A 17-Jun-19 A 27-Sep-19 A 19-feb-24 A 19-feb-24 A 01-Mar-24 A	07-Nov-20 A 30-Jun-25 30-Jun-25 05-Mar-25 07-Nov-24 05-Dec-23 A 10-Apr-25								
2331 2331 2331 2214 1971 1531 340 225 1920 96 50	11-Feb-19A 11-Feb-19A 11-Feb-19A 11-Feb-19A 11-Feb-19A 27-Sep-19A 19-Feb-24A 19-Feb-24A 01-Mar-24A	30-Jun-25 30-Jun-25 05-Mar-25 07-Nov-24 05-Dec-23 A 10-Apr-25								
2331 2214 1971 1531 340 125 2125 96 150	11-Feb-19A 11-Feb-19A 17-Jun-19A 27-Sep-19A 19-Feb-24A 19-Feb-24A 01-Mar-24A	30-Jun-25 30-Jun-25 05-Mar-25 07-Nov-24 05-Dec-23 A 10-Apr-25								
2331 2214 1971 1531 340 125 2125 96 150	11-Feb-19 A 11-Feb-19 A 17-Jun-19 A 27-Sep-19 A 19-Feb-24 A 19-Feb-24 A 01-Mar-24 A	30-Jun-25 05-Mar-25 07-Nov-24 05-Dec-23 A 10-Apr-25								
2214 1971 1531 340 125 192 96 150	11-Feb-19 A 17-Jun-19 A 27-Sep-19 A 19-Feb-24 A 19-Feb-24 A 01-Mar-24 A	05-Mar-25 07-Nov-24 05-Dec-23 A 10-Apr-25								
1531 340 125 192 96 150	27-Sep-19 A 19-Feb-24 A 19-Feb-24 A 01-Mar-24 A	05-Dec-23 A 10-Apr-25								
340 125 192 96 150	19-Feb-24 A 19-Feb-24 A 01-Mar-24 A	10-Apr-25	-							
125 192 96 150	19-Feb-24 A 01-Mar-24 A									
192 96 150	01-Mar-24 A	10-Jul-24 A						•		
96 150										
		23-Oct-24								
	09-Oct-24	26-Mar-25 10-Apr-25								
	09-Oct-24 25-Oct-19 A	10-Apr-25 18-Jan-25								
46	23-Nov-24	18-Jan-25								
1047										
1356	06-Dec-19 A	29-Oct-24	-							
996	09-Jul-22 A	15-Jan-25				· · · ·				
831	29-Mar-22 A	17-Jan-25								
1468	16-Nov-20 A	22-Nov-24								
2280	04-Apr-19 A	30-Jun-25								
									<u></u>	
324									· ·	
0	Z8-Apr-Z5									
	01.Mmi 18.A									
				_						
				•						
			·							
		24-Aug-24								
1876	11-Jan-19 A	25-Jan-24 A	l .			-				
2194	20-Dec-18 A	21-Dec-24	•							
1307	14-Apr-20 A	07-Sep-24								
				_		1 1 1				
206										
0	25-301-24									
	14-00-19.4									
			<u> </u>							
2237	21-Jan-19 A	09-Apr-25							<u> </u>	
1860	14-Jan-19 A	28-Apr-25	-							
1892	06-Dec-19 A	08-Feb-25	-					5		
0	18-Feb-25	18-Feb-25							•	
0		18-Feb-25							•	
	15-feb-19 A	22-Apr-22 A	-							
2082	06-May-19 A	15-Jan-25								
1626	06-May-19 A	28-Oct-24							-	
	11-May-19 A	28-Oct-24								
	06-May-19 A	28-Dec-22 A					-			
						•		-		
					·····					
								—		
141			+					•		
	1007 1356 996 813 1348 2200 433 334 0 0 2307 354 354 354 354 354 354 355 356 357 358 359 350 350 351 356 357 358 359 350 350 351 352 353 356 357 358 359 350 350 351 352 352 352 352 352 352 352 352 352 352	1007 25 ort 39.4 1556 66 box 39.4 181 26 box 32.4 181 26 box 32.4 181 22 box 32.4 463 20 box 32.4 183 20 box 32.4 463 20 box 32.4 463 20 box 32.4 183 20 box 32.4 483 20 box 32.4 183 20 box 32.4 184 20 box 32.4 185 20 box 32.4 186 12 box 128.4 199 20 box 128.4 199<	1007 25.05:9A 05.922A 1006 05.922A 154.872 1006 05.922A 154.872 1006 05.922A 154.872 1006 05.922A 154.872 1006 04.922A 154.872 1006 04.975A 30.8874 1016 05.982A 154.872 1020 04.9675A 30.8875A 1020 02.94755 12849 100 2244925 1284925 100 224925 1284925 101 121.0623A 121.0623A 1020 124925 1284925 1020 124925 1284925 1020 124925 1284925 1020 124912A 1249224 1020	1007 250-03-9A 05-592.A 1056 05-06-02 PA 250-03-9A 1056 05-06-02 PA 15 Jan 25 1018 20-06-02 PA 20-06-02 PA 1019 20-06-02 PA 20-06-02 PA 1020 0.06-02 PA 20-06-02 PA 1020 22-08-02 PA 20-06-02 PA 1020 0.26-02 PA 20-06-02 PA 1030 22-06-02 PA 22-06-02 PA 1030 22-06-02 PA 22-06-02 PA 1030 12-06-02 PA 22-06-02 PA 10307 12-06-02 PA 12-06-02 PA 10307 12-06-02 PA 12-06-02 PA 10307 12-06-02 PA 12-06-02 PA 10307 12-06-02 PA 12-0	1007 25 04:39.4 05 59.22.4 1996 05 bd.22.4 15 ban 25 1811 25 Mar 22.4 17 ban 25 1813 25 Mar 22.4 17 ban 25 1813 25 Mar 22.4 17 ban 25 1816 26 Mar 22.4 17 ban 25 1813 25 Mar 22.4 17 ban 25 1816 26 Mar 23.4 26 Mar 23.4 1920 0.4 mar 23.4 0.4 feb 25 1920 0.4 mar 23.4 0.4 feb 25 1920 0.6 mar 23.4 mar 23.4 0.4 feb 25 1920 0.6 mar 23.4 mar 23.4 0.4 feb 25 1920 0.6 mar 23.4 mar 23.4 0.4 feb 25 1920 26 Mar 23.4 23 feb 23.4 1920 26 Mar 23.4 23 feb 23.4 1920 12 Mar 13.4 12 Mar 24.4 1920 12 Mar 24	1007 22-0-0130A 005-0027A 1006 005-0027A 154m-25 1018 006-0027A 154m-25 1018 006-0027A 154m-25 1018 006-0027A 154m-25 1019 006-0027A 154m-25 1010 2240-23A 046m-25 1020 024-0273 244m-25 100 224m-23A 04m-25 100 224m-25 0 100 124m-15A 24m-25 1000 124m-15A 24m-25A 1001 124m-15A 25m-24A 1100 124m-15A <td>1007 250-039A 05-922A 1056 06-00-09A 250-034 1057 06-00-09A 154m-25 1018 2040-02A 154m-25 1019 06-00-09A 224m-24 1020 024m-25A 154m-25 1040 204m-27A 044m-25 1040 204m-27A 044m-25 1041 204m-27A 044m-25 1040 204m-27A 044m-25 1041 204m-27A 044m-25 1050 254m-27A 04m-25 1050 254m-27A 04m-25 1050 126m-15A 216m-26 <t< td=""><td>1000 20-0130A 05-692/A 1990 00-942/A 153-053 1811 20-04-92/A 153-053 1812 20-04-92/A 153-05 1813 20-04-92/A 153-05 1814 20-04-92/A 20-05-94 1815 20-04-92/A 20-05-94 1816 20-05-92/A 20-05-94 1817 20-06-95/A 20-05-95 1818 20-06-95/A 20-05-95/A 1817 20-06-95/A 20-05-95/A 1818 20-06-95/A 20-05-95/A 1819 20-06-95/A 20-05-95/A 1920 20-06-95/A 20-05-97/A 1921 20-06-95/A 20-05-97/A 1920 20-06-97/A 20-05-97/A 1920 20-06-97/A 20-05-97/A 1921 12-06-97/A 20-05-97/A 1920 20-06-97/A 20-05-97/A 1920 20-05-97/A 20-05-97/A 1920 20-05-97/A 20-05-97/A 1920</td><td>1900 350 334 0.592034 1960 050:034 250:034 1960 050:024 150:035 1960 050:024 250:034 1960 0.590:024 250:034 1960 0.590:024 250:034 1960 0.590:024 250:034 1960 0.590:024 250:025 1960 0.590:024 250:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960</td><td>100 200380 05-692A 100 05-023A 130-25 100 154-25 130-25 100 154-25A 130-25 100 154-25A 140-25 100 154-25A 150-26 100 154-25A 150-26 </td></t<></td>	1007 250-039A 05-922A 1056 06-00-09A 250-034 1057 06-00-09A 154m-25 1018 2040-02A 154m-25 1019 06-00-09A 224m-24 1020 024m-25A 154m-25 1040 204m-27A 044m-25 1040 204m-27A 044m-25 1041 204m-27A 044m-25 1040 204m-27A 044m-25 1041 204m-27A 044m-25 1050 254m-27A 04m-25 1050 254m-27A 04m-25 1050 126m-15A 216m-26 1050 126m-15A 216m-26 <t< td=""><td>1000 20-0130A 05-692/A 1990 00-942/A 153-053 1811 20-04-92/A 153-053 1812 20-04-92/A 153-05 1813 20-04-92/A 153-05 1814 20-04-92/A 20-05-94 1815 20-04-92/A 20-05-94 1816 20-05-92/A 20-05-94 1817 20-06-95/A 20-05-95 1818 20-06-95/A 20-05-95/A 1817 20-06-95/A 20-05-95/A 1818 20-06-95/A 20-05-95/A 1819 20-06-95/A 20-05-95/A 1920 20-06-95/A 20-05-97/A 1921 20-06-95/A 20-05-97/A 1920 20-06-97/A 20-05-97/A 1920 20-06-97/A 20-05-97/A 1921 12-06-97/A 20-05-97/A 1920 20-06-97/A 20-05-97/A 1920 20-05-97/A 20-05-97/A 1920 20-05-97/A 20-05-97/A 1920</td><td>1900 350 334 0.592034 1960 050:034 250:034 1960 050:024 150:035 1960 050:024 250:034 1960 0.590:024 250:034 1960 0.590:024 250:034 1960 0.590:024 250:034 1960 0.590:024 250:025 1960 0.590:024 250:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960</td><td>100 200380 05-692A 100 05-023A 130-25 100 154-25 130-25 100 154-25A 130-25 100 154-25A 140-25 100 154-25A 150-26 100 154-25A 150-26 </td></t<>	1000 20-0130A 05-692/A 1990 00-942/A 153-053 1811 20-04-92/A 153-053 1812 20-04-92/A 153-05 1813 20-04-92/A 153-05 1814 20-04-92/A 20-05-94 1815 20-04-92/A 20-05-94 1816 20-05-92/A 20-05-94 1817 20-06-95/A 20-05-95 1818 20-06-95/A 20-05-95/A 1817 20-06-95/A 20-05-95/A 1818 20-06-95/A 20-05-95/A 1819 20-06-95/A 20-05-95/A 1920 20-06-95/A 20-05-97/A 1921 20-06-95/A 20-05-97/A 1920 20-06-97/A 20-05-97/A 1920 20-06-97/A 20-05-97/A 1921 12-06-97/A 20-05-97/A 1920 20-06-97/A 20-05-97/A 1920 20-05-97/A 20-05-97/A 1920 20-05-97/A 20-05-97/A 1920	1900 350 334 0.592034 1960 050:034 250:034 1960 050:024 150:035 1960 050:024 250:034 1960 0.590:024 250:034 1960 0.590:024 250:034 1960 0.590:024 250:034 1960 0.590:024 250:025 1960 0.590:024 250:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960 250:025 100:025 1960	100 200380 05-692A 100 05-023A 130-25 100 154-25 130-25 100 154-25A 130-25 100 154-25A 140-25 100 154-25A 150-26 100 154-25A 150-26

Appendix C Project Organization Chart

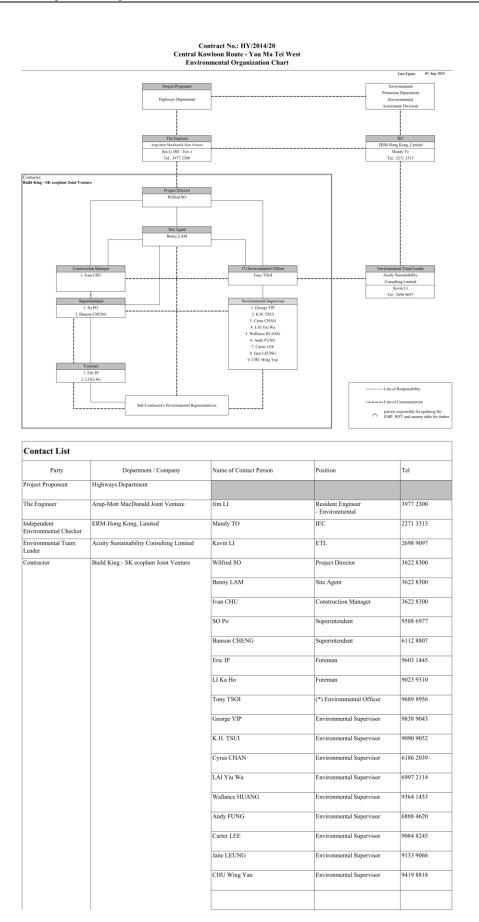

Appendix D Dust Event-Action Plan (EAP)

Contract No. HY/2014/20 Environmental Monitoring & Auditing

	ACTION							
EVENT	ET	IEC	ER	CONTRACTOR				
ACTION LEV	EL							
1.Exceedance for one sample	 Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and ER; Repeat measurement to confirm finding; Increase monitoring frequency to daily. 	 Check monitoring data submitted by ET; Check Contractor's working method. 	1. Notify Contractor.	 Rectify any unacceptable practice; Amend working methods if appropriate. 				
2.Exceedance for two or more consecutive samples	 Identify source; Inform IEC and ER; Advise the ER on the effectiveness of the proposed remedial measures; Repeat measurements to confirm findings; Increase monitoring frequency to daily; Discuss with IEC and Contractor on remedial actions required; If exceedance continues, arrange meeting with IEC and ER; If exceedance stops, cease additional monitoring. 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ET on the effectiveness of the proposed remedial measures; Supervise Implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented. 	 Submit proposals for remedial to ER within 3 working days of notification; Implement the agreed proposals; Amend proposal if appropriate. 				
LIMIT LEVEL			1					
1.Exceedance for one sample	 Identify source, investigate the causes of exceedance and propose remedial measures; Inform ER, Contractor and 	 Check monitoring data submitted by ET; Check Contractor's working method; 	 Confirm receipt of notification of failure in writing; Notify Contractor; 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC 				

Contract No. HY/2014/20 Environmental Monitoring & Auditing

EVENT	ACTION							
	ЕТ	IEC	ER	CONTRACTOR				
	 EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 	 Discuss with ET and Contractor on possible remedial measures; Advise the ER on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures. 	3. Ensure remedial measures properly implemented.	 within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate. 				
2.Exceedance for two or more consecutive samples	 Notify IEC, ER, Contractor and EPD; Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring. 	 Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the ER until the exceedance is abated. 				

Note:

ET – Environmental Team

ER – Engineer's Representative

Environmental

Checker

Independent

IEC

Acuity Sustainability Consulting Ltd.

Appendix E Noise Event-Action Plan (EAP)

EVENT		ACTIO	DN	
	ЕТ	IEC	ER	CONTRACTOR
Action Level	 Identify source, investigate the causes of exceedance and propose remedial measures; Notify IEC and Contractor; Report the results of investigation to the IEC, ER and Contractor; Discuss with the Contractor and formulate remedial measures; Increase monitoring frequency to check mitigation effectiveness. 	 Review the analysed results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the ER accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures are properly implemented 	 Submit noise mitigation proposals to IEC; Implement noise mitigation proposals.
Limit Level	 Identify source; Inform IEC, ER, EPD and Contractor; Repeat measurements to confirm findings; Increase monitoring frequency; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Inform IEC, ER and EPD the causes and actions taken for the exceedances; Assess effectiveness of Contractor's remedial actions 	 Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the ER until the exceedance is abated.

EVENT	ACTION								
	ET	IEC	ER	CONTRACTOR					
	and keep IEC, EPD and ER informed of the results;		abated.						
	8. If exceedance stops, cease additional monitoring.								

Note:

ET – Environmental Team

IEC – Independent Environmental Checker

ER – Engineer's Representative

Appendix F Environmental Mitigation Implementation Schedule (EMIS)

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		Со	nstruction Dust Im	pact				
\$4.3.10	D1	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	 APCO To control the dust impact To meet HKAQO and TM-EIA criteria 	Implemented
\$4.3.10	D2	 Mitigation measures in form of regular watering under a good site practice should be adopted. Watering once per hour on exposed worksites and haul road should be conducted to achieve dust removal efficiencies of 91.7%. While the above watering frequencies are to be followed, the extent of watering may vary depending on actual site conditions but should be sufficient to maintain an equivalent intensity of no less than 1.3 L/m² to achieve the dust removal efficiency. 	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	 APCO To control the dust impact To meet HKAQO and TM-EIA criteria 	• Implemented
\$4.3.10		 Proper watering at exposed spoil should be undertaken throughout the construction phase; Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading; Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads; A stockpile of dusty material should not be extended 	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	 APCO To control the dust impact To meet HKAQO and TM-EIA criteria 	 Implemented, deficiency rectified after reminder

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 beyond the pedestrian barriers, fencing or traffic cones; The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle. Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores; When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided and properly maintained as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period; The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials; Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously; Any area that involves demolition activities should be 						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
\$4.3.10	D6	 sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet; Any skip hoist for material transport should be totally enclosed by impervious sheeting; Every stock of more than 20 bags of cement or dry-pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides; Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabilizer within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies. 	Monitoring of	Contractor	Selected rep.	Construction stage	• TM-EIA	• Implemented
54.3.10	DP	Implement regular dust monitoring under EM&A programme during the construction stage.	Monitoring of dust impact	Contractor	Selected rep. dust monitoring station	Construction stage	• IM-EIA	Implemented
		Со	nstruction Noise (Airborne)				

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
S5.4.1	N1	 Implement the following good site practices: Only well-maintained plant should be operated onsite and plant should be serviced regularly during the construction programme; Machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; Plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs; Silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works; Mobile plant should be sited as far away from NSRs as possible and practicable; Material stockpiles, mobile container site office and other structures should be effectively utilized, where practicable, to screen noise from on-site construction activities. 	Control construction airborne noise	Contractor	All construction sites	Construction stage	• Annex 5, TM- EIAO	• Implemented
\$5.4.1	N2	Install temporary hoarding located on the site boundaries between noisy construction activities and NSRs. The conditions of hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level zone of NSRs through partial screening	Contractor	All construction sites	Construction stage	• Annex 5, TM- EIAO	Implemented
S5.4.1	N3	Install movable noise barriers (typical design is wooden framed barrier with a small-cantilevered on a skid footing with 25mm thick internal sound absorptive lining), acoustic mat or full enclosure,	Sreen the noisy plant items to be used at all	Contractor	All construction sites where practicable	Construction stage	• Annex 5, TM- EIAO	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		screen the noisy plants including air compressors, generators and handheld breakers, etc.	sites					
S5.4.1	N4	Use 'Quiet plant'	Reduce the noise levels of plant items	Contractor	All construction sites where practicable	Construction stage	• Annex 5, TM- EIAO	Implemented
S5.4.1	N5	Loading/ unloading activities should be carried out inside the full enclosure of mucking out points.	Reduce the noise levels of loading/ unloading activities	Contractor	Mucking out locations	Construction stage	• Annex 5, TM- EIAO	Implemented
S5.4.1	N6	Sequencing operation of construction plants where practicable.	Operate sequentially within the same work site to reduce the construction airborne noise	Contractor	All construction sites where practicable	Construction stage	• Annex 5, TM- EIAO	Implemented
S5.4.1	N7	Implement a noise monitoring programme under EM&A programme.	Monitor the construction noise levels at the selected representative locations	Contractor	Selected rep. noise monitoring station	Construction stage	• TM-EIAO	Implemented
		Water C	uality (Constructi	on Phase)				
\$6.9.1.1		In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN1/94), construction phase mitigation measures shall include	To minimize water quality impact from the construction site	Contractor	All construction sites where practicable	Construction stage	Water Pollution Control Ordinance	 Implemented, deficiency rectified after observation

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 the following: Construction Runoff At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the contractor prior to the commencement of construction; The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/ sediment trap. The sediment/ silt traps should be incorporated in the permanent drainage channels to enhance deposition rates; The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt/ sand traps should be 5 minutes under maximum flow conditions. Sizes may vary depending upon the flow rate, but for a flow rate of 0.1 m³/s a sedimentation basin of 30 m³ would be required and for a flow rate of 0.5 m³/s the 	runoff and general construction activities				ProPECC PN 1/94 TM-EIAO TM-DSS	

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 basin would be 150 m³. The detailed design of the sand/ silt traps shall be undertaken by the contractor prior to the commencement of construction; All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. Exposed slope surfaces should be covered by tarpaulin or other means; The overall slope of the site should be kept to a minimum to reduce the erosive potential of surface water flows, and all traffic areas and access roads protected by coarse stone ballast. An additional advantage accruing from the use of crushed stone is the positive traction gained during prolonged periods of inclement weather and the reduction of surface sheet flows; All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas; Measures should be taken to minimize the ingress of site drainage into excavations. If the excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or 						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 foundation excavations should be discharged into storm drains via silt removal facilities; Open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50m³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system; Manholes should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers; Precautions be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes; All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and site wheel washing facilities should be provided at every construction site exit where practicable. Washwater should have sand and silt settled out and removed at least on a weekly basis to ensure the 						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 continued efficiency of the process. The section of access road leading to, and exiting from, the wheel wash bay to the public road should be paved with sufficient backfall toward the wheel wash bay to prevent vehicle tracking of soil and silty water to public roads and drains; Oil interceptors should be provided in the drainage system downstream of any oil/ fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain; Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts; All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby; Adopt best management practices; All earth works should be conducted sequentially to limit the amount of construction runoff generated from exposed areas during the wet season (April to December) as far as practicable. 						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
\$6.9.1.2		 Tunneling Works and Underground Works Cut-&-cover tunneling work should be conducted sequentially to limit the amount of construction runoff generated from exposed areas during the wet season (April to December) as far as practicable. Uncontaminated discharge should pass through sedimentation tanks prior to off-site discharge; The wastewater with a high concentration of SS should be treated (e.g. by sedimentation tanks with sufficient retention time) before discharge. Oil interceptors would also be required to remove the oil, lubricants and grease from the wastewater; Direct discharge of the bentonite slurry (as a result of D-wall) is not allowed. It should be reconditioned and reused wherever practicable. Temporary storage locations (typically a properly closed warehouse) should be provided on site for any unused bentonite that needs to be transported away after all the related construction activities area completed. The requirements in ProPECC PN 1/94 should be adhered to in the handling and disposal of bentonite slurries. 	To minimize construction water quality impact from tunneling works	Contractor	All tunneling portion	Construction stage	 Water Pollution Control Ordinance ProPECC PN 1/94 TM-DSS TM-EIAO 	• N/A
\$6.9.1.3	W3	 Sewage Effluent Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide 	To minimize water quality from sewage effluent	Contractor	All construction sites where practicable	Construction stage	 Water Pollution Control Ordinance TM-DSS 	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.						
S6.9.1.5	W4	 Groundwater from Potential Contaminated Area: No direct discharge of groundwater from contaminated areas should be adopted. A discharge license under the WPCO through the Regional Office of EPD for groundwater discharge should be applied. Prior to the excavation works within these potentially contaminated areas, the groundwater quality should be reviewed during the process of discharge license application. The compliance to the Technical Memorandum on Standards for Effluents Discharged into Drainage on Sewerage Systems, Inland and Coastal Waters (TM-DSS) and the existence of prohibited substance should be confirmed. If the review results indicated that the groundwater to be generated from the excavation works would be contaminated, the contaminated groundwater should be either properly treated in compliance with the requirements of the TM-DSS or properly recharged into the ground. If wastewater treatment is deployed, the wastewater treatment unit shall deploy suitable treatment process (e.g. oil interceptor / activated carbon) to reduce the pollution level to an 	To minimize groundwater quality impact from contaminated area	Contractor	Excavation areas where contamination is found	Construction stage	 Water Pollution Control Ordinance TM-DSS TM-EIAO 	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 acceptable standard and remove any prohibited substances (e.g. TPH) to undetectable range. All treated effluent from wastewater treatment plant shall meet the requirements as stated in TM-DSS and should be discharged into the foul sewers. If groundwater recharging wells are deployed, recharging wells should be installed as appropriate for recharging the contaminated groundwater back into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in the Section 2.3 of TM-DSS. The baseline groundwater quality shall be determined prior to the selection of the recharge wells, and submit a working plan (including the laboratory analytical results showing the quality of groundwater at the proposed recharge location(s) as well as the pollutant levels of groundwater at the recharge well. Prior to recharge, any prohibited substances such as TPH products should be removed as necessary by installing the petrol interceptor. 						
\$6.9.1.6	W6	Accidental Spillage In order to prevent accidental spillage of chemicals, the following is recommended:	To minimize water quality impact from accidental	Contractor	All construction site where practicable	Construction stage	Water Pollution Control Ordinance	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 All the tanks, containers, storage area should be bunded and the locations should be locked as far as possible from the sensitive watercourse and stormwater drains; The Contractor should register as a chemical waste producer if chemical wastes would be generated. Storage of chemical waste arising from the construction activities should be stored with suitable labels and warnings. Disposal of chemical wastes should be conducted in compliance with the requirements as stated in the Waste Disposal (Chemical Waste) (General) Regulation. 	spillage				 ProPECC PN 1/94 TM-EIAO TM-DSS 	
		Waste Man	agement (Constru	iction Waste)				
S7.4.1	WM1	 On-site sorting of C&D material Geological assessment should be carried out by competent persons on site during excavation to identify materials which are not suitable to use as aggregate in structural concrete (e.g. volcanic rock, Aplite dyke rock, etc.). Volcanic rock and Aplite dyke rock should be separated at the source sites as far as practicable and stored at designated stockpile area preventing them from delivering to crushing facilities. The crushing plant operator should also be reminded to set up measures to prevent unsuitable rock from ending up at concrete batching plants and be turned into concrete for 	Separation of unsuitable rock from ending up at concrete batching plants and be turned into concrete for structural use	Contractor	All construction sites	Construction stage	• DEVB (W) No. 6/2010	• N/A

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		structural use. Details regarding control measures at source site and crushing facilities should be submitted by the Contractor for the Engineer to review and agree. In addition, site records should also be kept for the types of rock materials excavated and the traceability of delivery will be ensured with the implementation of Trip Ticket System and enforced by site supervisory staff as stipulated under DEVB TC(W) No. 6/2010 for tracking of the correct delivery to the rock crushing facilities for processing into aggregates. Alternative disposal option for the reuse of volcanic rock and Aplite Dyke rock, etc. should be explored.						
\$7.5.1	WM2	 Construction and Demolition Material Maintain temporary stockpiles and reuse excavated fill material for backfilling and reinstatement; Carry out on-site sorting; Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; Adopt 'selective demolition' technique to demolish the existing structures and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible; Implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified; and Implement an enhanced Waste Management Plan 	Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction stage	 Land (Miscellaneo us Provisions) Ordinance Waste Disposal Ordinance ETWB TCW No. 19/2005 	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		similar to ETWBTC (Works) No. 19/2005 – "Environmental Management on Construction Sites" to encourage on-site sorting of C&D materials and to minimize their generation during the course of construction.						
\$7.5.1	WM3	 <u>C&D Waste</u> Standard formwork or pre-fabrication should be used as far as practicable in order to minimize the arising of C&D materials. The use of more durable formwork or plastic facing for the construction works should be considered. Use of wooden hoardings should not be used, as in other projects. Metal hoarding should be used to enhance the possibility of recycling. The purchasing of construction materials will be carefully planned in order to avoid over ordering and wastage; The Contractor should recycle as much of the C&D materials as possible on-site. Public fill and C&D waste should be segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal. Where practicable, concrete and masonry can be crushed and used as fill. Steel reinforcement bar can be used by scrap steel mills. Different areas of the sites should be considered for such segregation and storage. 	Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction stage	 Land (Miscellaneo us Provisions) Ordinance Waste Disposal Ordinance ETWB TCW No. 19/2005 	• Implemented
\$7.5.1	WM5	<u>Land-based Sediment</u> • All construction plant and equipment shall be	To control pollution due to	Contractor	Along CKR alignment	Construction stage	 ETWB TCW No. 34/2002 	Implemented
		designed and maintained to minimize the risk of silt, sediments, contaminants or other pollutants	marine sediment					

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 being released into the water column or deposited in the locations other than designated location; All vessels shall be sized such that adequate draft is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; Before moving the vessels which are used for transporting dredged material, excess material shall be cleaned from the decks and exposed fittings of vessels and the excess materials shall never be dumped into the sea except at the approved locations; Adequate freeboard shall be maintained on barges to ensure that decks are not washed by wave action. The Contractors shall monitor all vessels transporting material to ensure that no dumping outside the approved location takes place. The Contractor shall keep and produce logs and other records to demonstrate compliance and that journeys are consistent with designated locations and copies of such records shall be submitted to the engineers; The Contractors shall comply with the conditions in the dumping licence. All bottom dumping vessels (Hopper barges) shall be fitted with tight fittings seals to their bottom openings to prevent leakage of material; The material shall be placed into the disposal pit by 						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 bottom dumping; Contaminated marine mud shall be transported by spit barge of not less than 750m3 capacity and capable of rapid opening and discharge at the disposal site; Discharge shall be undertaken rapidly and the hoppers shall be closed immediately. Material adhering to the sides of the hopper shall not be washed out of the hopper and the hopper shall remain closed until the barge returns to the disposal site. For Type 3 special disposal treatment, sealing of contaminant with geosynthetic containment before dropping designated mud pit would be a possible arrangement. A geosynthetic containment method is a method whereby the sediments are sealed in geosynthetic containers and, the containers would be dropped into the designated contaminated mud pit where they would be covered by further mud disposal and later by the mud pit capping at the disposal. 						
S7.5.1	WM6	 <u>Chemical Waste</u> Chemical waste that is produced, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, should be handled in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes; Containers used for the storage of chemical wastes 	Control the chemical waste and ensure proper storage, handling and disposal	Contractor	All construction sites	Construction stage	 Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on 	 Implemented, deficiency rectified after observation

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 should be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed, have a capacity of less than 450 L unless the specification has been approved by EPD, and display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the regulation; The storage area for chemical wastes should be clearly labelled and used solely for the storage of chemical waste, enclosed on at least 3 sides, have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20% of the total volume of waste stored in that area, whichever is the greatest, have adequate ventilation, covered to prevent rainfall entering, and arranged so that incompatible materials are adequately separated; Disposal of chemical waste should be via a licensed waste collector, be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Centre which also offers a chemical waste collection service and can supply the necessary storage containers, or be to a reuser of the waste, under approval from EPD. 					the Packaging, Labelling and Storage of Chemical Waste	
S7.5.1	WM7	 <u>General Refuse</u> General refuse generated on-site should be stored in enclosed bins or compaction units separately from construction and chemical wastes; A reputable waste collector should be employed by 	Minimize production of the general refuse and avoid odour, pest and	Contractor	All construction sites	Construction stage	Waste Disposal Ordinance	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law. Aluminum cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. Separate labelled bins for their deposit should be provided if feasible; Office wastes can be reduced through the recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme should be considered by the Contractor. 	litter impacts					
			Land Contamin	ation	•	·	·	
S8.9 & Appendix 8.4	LC2	 Excavation of the Contaminated Soil Prior to commencement of the excavation works at the contamination zone, the zone should be clearly marked out on site and the surface levels recorded. Excavation of contaminated material should be undertaken using dedicated earth-moving plant. The excavated contaminated soils would be stockpiled at designated area on site and covered by sheet to prevent dispersion of contamination during stockpiling. The Contractor should pay attention to the selection of suitable groundwater lowering schemes and discharge points if the groundwater table is higher than the contaminated soils during 	The contaminated soil will be excavated for on-site reuse	Contractor	PBH4	Prior to commencement of construction works within the contaminated area	 Practice Guide (PG) for Investigation and Remediation of Contaminate d Land Guidance Notes for Contaminate d Land Assessment 	• Implemented

EIA Ref.	EM&A Log Ref.	Recommo	ended Mitigatio	n Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
	LC3	 excavation. The Contractor should also obtain a valid Water Pollution Control Ordinance (WPCO) discharge licence from EPD where applicable. Following completion of the excavation to the 						and Remediation • Guidance Manual for Use of Risk-	Implemented	
Appendix 8.4		specified dept of the excar distributed ald shall be taker	h, at least one sa vation and fou ong the boundar	mple from the base r samples evenly y of the excavation assessment testing.					Based Remediation Goals (RBRGs) for Contaminate d Land	- implementeu
			Testing requirement PCBs of analysis below er excavation will	Acceptance Criteria RBRGs (Public Park) the RBRGs (Public be required.					Management	
		(i.e. noncomplia further excavatio increment vertica the location(s) of the acceptance of conducted for c excavation, samplic continue until all	ance of the ac on shall be car ally and/or horizon f the sample(s) w riteria. Further sa compliance testin ing and complia contaminated ma	e of contamination ceptance criteria), ried out in 0.5m ntally depending on vhich has exceeded mpling shall also be g. The process of nce testing should terials are removed and Contamination						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
Appendix 8.4	LC4	 A Remediation Report (RR) to demonstrate adequate clean-up shall be prepared and submitted to EPD for endorsement prior to the commencement of any construction/development works within the sites. No construction/development works shall be carried out prior to the endorsement of the RR by EPD. 		fa				Implemented
	n		Hazard to Li	1		1		
\$9.18	H8	The driver and his assistant should be physically healthy, experienced and have good safe driving records. The driver should hold a proper driving licence for the approved transport truck. Dedicated training programme and regular road safety briefing sessions/ workshops should be provided to enhance their safe driving attitude and practice. Smoking should be strictly prohibited.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A
S9.18	H9	Emergency response plans in case of road accident should be prepared and implemented. The driver and his assistant should be familiar with the emergency procedures including evacuation, and proper communication/ fire-fighting equipment should be provided to the driver and his assistant.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A
			Landscape & V	'isual				
S10.10.1 Table 10.11	LV3	 <u>Good Site Management</u> Large temporary stockpiles of excavated material shall be covered with unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance. 	Minimize visual impact	Contractor	Within Project site	Construction stage	-	Implemented


EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 Construction plant and building material shall be orderly and carefully stored in order to create a neat and tidy visual appearance. 						
S10.10.1 Table 10.11	LV4	 <u>Screen Hoarding</u> Decorative screen hoarding should be erected to screen the public from the construction area. It should be designed to be compatible with the existing urban context. 	Minimize visual impact	Contractor	Within Project site	Construction stage	-	Implemented
S10.10.1 Table 10.11	LV5	 Lighting Control during Construction All lighting in the construction site shall be carefully controlled to minimize light pollution and night-time glare to nearby residencies and GIC. The Contractor shall consider other security measures, which shall minimize the visual impacts. 	Minimize visual impact	Contractor	Within Project site	Construction stage	-	Implemented
S10.10.1 Table 10.11	LV6	 Erosion Control The potential for soil erosion shall be reduced by minimizing the extent of vegetation disturbance on site and by providing a protective cover over newly exposed soil. 	Minimize landscape impact	Contractor	Within Project site	Construction stage	-	• N/A
S10.10.1 Table 10.11	LV7	 <u>Tree Protection & Preservation</u> Carefully protected during construction. Tree protection measures will be detailed at the Tree Removal Application stage and plans submitted to the relevant Government Department for approval in due course in accordance with ETWB TC no. 3/2006. 	Minimize landscape and visual impact	Contractor	Within Project site	Construction stage	 'Guidelines for Tree Risk Management and Assessment Arrangement on an Area Basis and on a Tree Basis', Greening, 	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
S10.10.1 Table 10.11	LV8	 <u>Tree Transplantation</u> For trees unavoidably affected by the Project that have to be removed, where practical transplantation will be chosen as the top priority method of removal. If this is not possible or practical compensatory planting will be provided for trees unavoidably felled (See LV10). For trees unavoidably affected by the Project works that are transplanted, transplantation must be carried out in accordance with ETWB TCW 2/2004 and 3/2006. 	Minimize landscape and visual impact	Contractor	Within Project site and designated off-site locations	Prior to Construction stage	Landscape and Tree Management (GLTM) Section, DEVB Latest recommende d horticultural practices from GLTM Section, DEVB ETWB TCW 3/2006 Latest recommende d horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DEVB	• Implemented

S10.10.1 Table U/9 Compensatory Planting • For trees unavoidably affected by the Project that have to be removed, where practical transportation will be chosen as the top priority method of removal but if this is not possible or practical compensatory planting two to the satisfaction of relevant Government projects. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under FUMET 3/2006. Minimize visual impact and also enhance and scape Within Project site Construction stage • ETWB TCW 3/2006 • Implemented d Image: Shall be determined and agreed separately with Government during the Tree Felling Application process under FUMET 3/2006. Minimize visual enhance satification of relevant be construction works and therefore be part of the bigger wider planting plans. Onsite compensatory the planting in genered but if necessary, additional receptor sites outside the Works Area shall be agreed separately with Government during the Tree Felling Application process. ETWB TCW 2/2004 • Implemented amenty areas affected by the construction works and therefore be part of the bigger wider planting plans. Onsite compensatory tree planting in partice planting plans. Onsite compensatory based separately with Government during the Tree felling Application process. ETWB TCW 2/2004	EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
Table 10.11• For trees unavoidably affected by the Project that have to be removed, where practical transportation will be chosen as the top priority method of removal but if this is not possible or practical compensatory planting will be provided for trees unavoidably felled. All felled trees shall be compensated for by planting trees to the satisfaction of relevant Government projects. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006.site3/2006 enhance and method of relevant Government from Greening, LandscapeCompensatory tree planting planting plants, Onsite compensation planting into public open spaces and along roadside amently areas affected by the construction works and therefore be part of the bigger wider planting plans. Onsite compensation planting is preferred but if necessary, additional receptor sites outside the Works Area shall be agreed separately with Government during the Tree Felling Application process.site3/2006 Latest recommend d horticultural practices from Greening, LandscapeETWB and therefore be part of the bigger wider planting plans. Onsite compensation planting is preferred but if necessary, additional receptor sites outside the Works Area shall be agreed separately with Government during the Tree Felling Application process.site3/2006 horticultural practices horticultural practices but if necessary, additional receptor sites outside the Works Area shall be agreed separately with Government during the Tree Felling Application process.					2				
	Table	LV9	 For trees unavoidably affected by the Project that have to be removed, where practical transportation will be chosen as the top priority method of removal but if this is not possible or practical compensatory planting will be provided for trees unavoidably felled. All felled trees shall be compensated for by planting trees to the satisfaction of relevant Government projects. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006. Compensatory tree planting may be incorporated into public open spaces and along roadside amenity areas affected by the construction works and therefore be part of the bigger wider planting plans. Onsite compensation planting is preferred but if necessary, additional receptor sites outside the Works Area shall be agreed separately with Government during the Tree Felling Application process. 	impact and also enhance landscape			Construction stage	3/2006 • Latest recommende d horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DEVB • ETWB TCW	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
S11.4.4	CH1	The contractor should be alerted during the construction on the possibility of locating archaeological remains and as a precautionary measure, AMO shall be informed immediately in case of discovery of antiquities or supposed antiquities in the subject sites.	To preserve any cultural heritage items which may be removed and damaged by the excavation	Contractor	During construction works for cut and cover tunnels	Construction stage	AMOs requirements	• N/A
			EM&A Proje	ect				
S13.2	EM1	An Independent Environmental Checker needs to be employed as per the EM&A Manual	Control EM&A Performance	Highways Department	All construction sites	Construction stage	 EIAO Guidance Note No. 4/2010 TM-EIAO 	Implemented
513.2-13.4	EM2	 An Environmental Team needs to be employed as per the EM&A Manual; Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures; An environmental impact monitoring needs to be implemented by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with. 	Perform environmental monitoring & auditing	Highways Department/ Contractor	All construction sites	Construction stage	 EIAO Guidance Note No. 4/2010 TM-EIAO 	Implemented

Appendix G Monitoring Schedule of the Reporting Month

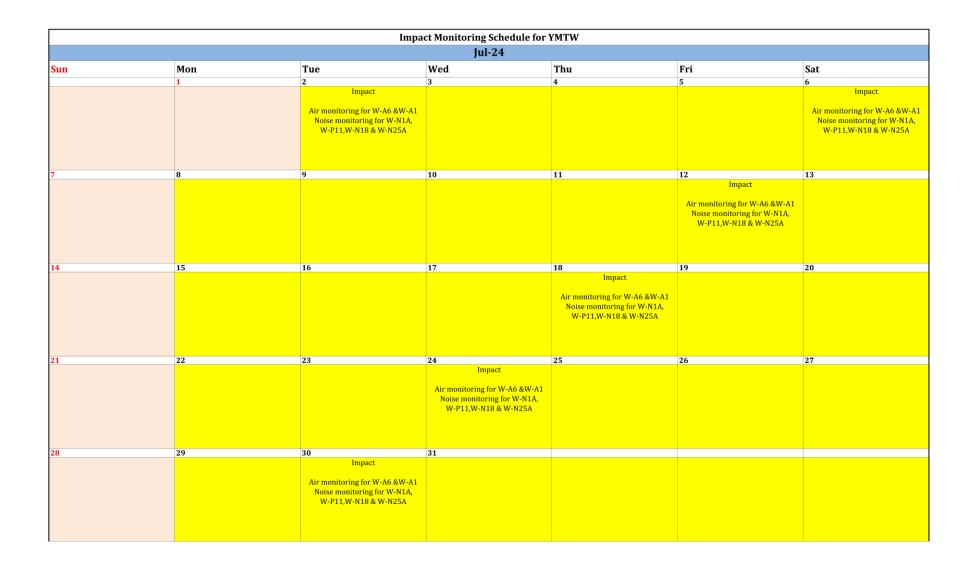

Appendix H Calibration Certificates (Air Monitoring)

Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Information of Calibrated Equipement

Verification Test Date:	28-Nov-23	to	30-Nov-23	Next Verification Test Date:	28-Nov-24
Unit-under-Test- Model No.:		Sibata LD-5R			
- Unit-under-Test Serial No.:		761172			
Our Report Refrence No.:	1	RPT-23-HVS-006	6		
- Calibration Location:	AM2,	location near	the Leachate Tre	atment Works within the NENTX Landfill	
-					-


	Standard Equipment Inform	nation
Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5025A
Equipment serial no.:	1106	4166
Last Calibration Date:	4-Nov-23	19-Jun-23
Next Calibration Date:	3-Jan-24	19-Jun-24

	Equipement Vertification Result										
Verification		Duration			Results from	Calibrated Equipement	Results from Standard Equipment				
Test No.	Date		End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration (μg/m³) y-axis				
1	28/11/2023	8789.68	8792.68	180.00	16234	90	96				
2	28/11/2023	8792.68	8795.68	180.00	15010	83	85				
3	28/11/2023	8795.68	8798.68	180.00	8526	47	49				
4	30/11/2023	8798.68	8801.68	180.00	10756	60	67				
5	30/11/2023	8801.68	8804.68	180.00	24867	138	145				
6	30/11/2023	8804.68	8807.68	180.00	9785	54	56				

 Linear Regression of y on x

 Slope, K factor:
 1.0443
 Intercept:
 0.6370
 *Correlation Coefficient, R:
 0.9978

 Verification Test Result:
 Strong Correlation, Results were accepted.
 * If the Correlation Coefficient, R: s<0.5. Checking and Re-verification are required.</td>



Operated By:

Andy Li Project Technician, Environmental

Date: 30-11-2023

Checked By:

Tandy Tse Senior Consultant, Environmenta


Date: 30-11-2023


Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Information of Calibrated Equipement								
Verification Test Date:	28-Nov-23	to	30-Nov-23	Next Verification Test Date:	28-Nov-24			
Unit-under-Test- Model No.:		Sibata LD-5R	1	-				
- Unit-under-Test Serial No.:		992821		-				
Our Report Refrence No.:	R	PT-23-HVS-00)72	-				
Calibration Location:	AM2,	location near	r the Leachate Tre	- eatment Works within the NENTX Landfill				
-					-			

	Standard Equipment Infor	mation
Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5025A
Equipment serial no.:	1106	4166
Last Calibration Date:	4-Nov-23	19-Jun-23
Next Calibration Date:	3-Jan-24	19-Jun-24

	Equipement Vertification Result										
Verification			Duration		Results from	a Calibrated Equipement	Results from Standard Equipment				
Test No.	Date	Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration (µg/m³) y-axis				
1	28/11/2023	8789.68	8792.68	180.00	15798	88	96				
2	28/11/2023	8792.68	8795.68	180.00	15038	84	85				
3	28/11/2023	8795.68	8798.68	180.00	8687	48	49				
4	30/11/2023	8798.68	8801.68	180.00	10732	60	67				
5	30/11/2023	8801.68	8804.68	180.00	24813	138	145				
6	30/11/2023	8804.68	8807.68	180.00	9156	51	56				





Operated By:

Andy Li Project Technician, Environmental

30-11-2023 Date:

Checked By:

L.fl Tandy Tse Senior Consultant, Environmental

Date: 30-11-2023


PC-3A(E) K-Factor Verification Test by Total Suspended Particulates HVS Test Report

	Information of Calibrated Equipement								
Verification Test Date:	19-Mar-24	to	24-Mar-24		Next Verification Test Date:	19-Mar-25			
Unit-under-Test- Model No.:		PC-3A(E)		-					
Unit-under-Test Serial No.:		JC-2002222		-					
Our Report Refrence No.:	P	RT-24-HVS-004	1	-					
Calibration Location:				Emax					

	Standard Equipment Informat	tion
Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5025A
Equipment serial no.:	1049	3465
Last Calibration Date:	19-Mar-24	15-Jan-24
Next Calibration Date:	2-Apr-24	15-Jan-25

	Equipement Vertification Result										
Verification		Duration			Results from	Calibrated Equipement	Results from Standard Equipment				
Test No.		Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration (μg/m³) y-axis				
1	19/03/2024	7953.66	7956.66	180.00	26946	150	162				
2	19/03/2024	7956.66	7959.66	180.00	26820	149	160				
3	19/03/2024	7959.66	7962.66	180.00	31140	173	182				
4	24/03/2024	7985.12	7988.12	180.00	7074	39	40				
5	24/03/2024	7988.12	7991.12	180.00	15786	88	92				
6	24/03/2024	7991.12	7994.12	180.00	12546	70	72				

Linear Regression of y on x



Operated By:

Andy Li Project Technician, Environmental

29-03-2024 Date:

Checked By:

Tandy Tse

Date: 29-03-2024


PC-3A(E) K-Factor Verification Test by Total Suspended Particulates HVS Test Report


Information of Calibrated Equipement										
Verification Test Date:	19-Mar-24	to	24-Mar-24		Next Verification Test Date:	19-Mar-25				
- Unit-under-Test- Model No.:		PC-3A(E)		-						
- Unit-under-Test Serial No.:		JC-2002225		_						
Our Report Refrence No.:	Р	RT-24-HVS-003	36	_						
Calibration Location:				Emax						
=						-				

	Standard Equipment Inform	nation
Verification Equipment Type:	Tisch TSP HVS	Tisch HVS Calibrator
Standard Equipment Model No.:	TE-5170X	TE-5025A
Equipment serial no.:	1049	3465
Last Calibration Date:	19-Mar-24	15-Jan-24
Next Calibration Date:	2-Apr-24	15-Jan-25

Equipement Vertification Result											
Verification Test No.	Date	Duration			Results from	Calibrated Equipement	Results from Standard Equipment				
		Start-time	End-time	Elapsed Time (in min)	Total Counts	Counts/ Minute x-axis	Dust Concentration (μg/m³) y-axis				
1	19/03/2024	7953.66	7956.66	180.00	26640	148	162				
2	19/03/2024	7956.66	7959.66	180.00	27360	152	160				
3	19/03/2024	7959.66	7962.66	180.00	31860	177	182				
4	24/03/2024	7985.12	7988.12	180.00	7200	40	40				
5	24/03/2024	7988.12	7991.12	180.00	15354	85	92				
6	24/03/2024	7991.12	7994.12	180.00	12834	71	72				

Linear Regression of y on x





Count/Minute

Operated By:

Checked By:

Andy Li Project Technician, Environmental

29-03-2024 Date:

412 (L) Tandy Tse Senior Consultant, Environmental

Date: 29-03-2024

								ALIBRATION
							Janu	ary 15, 202
nvir	onm	ent	al					
	Ce	rtifa	cate				rtion	
C-1 D-1		2021	Calibration					
Cal. Date:	January 15	, 2024	Roots	meter S/N:	438320	Ta:	294	°К
Operator:	Jim Tisch					Pa:	755.9	mm Hg
Calibration	Model #:	TE-5025A	Calib	prator S/N:	3465			
		Vol. Init	Vol. Final	ΔVol.	ΔTime	ΔΡ	ΔΗ	1
	Run	(m3)	(m3)	(m3)	(min)	(mm Hg)	(in H2O)	
	1	1	2	1	1.4350	3.3	2.00	-
	2	3	4	1	1.0180	6.4	4.00	
	3	5	6	1	0.9090	8.0	5.00	
	4	7	8	1	0.8670	8.9	5.50	-
						12.9	8.00	1
				ata Tabula	tion			
	Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right)}$)(<u>Tstd</u>)		Qa	$\sqrt{\Delta H(Ta/Pa)}$	
	(m3)	(x-axis)	(y-axi		Va	(x-axis)	(y-axis)	
	1.0037 0.9996	0.6995	1.420		0.9956	0.6938	0.8820	
	0.9975	1.0973	2.008		0.9915	0.9740	1.2473	
	0.9963	1.1491	2.354		0.9882	1.1398	1.3943	
	0.9909	1.3859	2.839	19	0.9829	1.3747	1.7639	
	OCTO	m=	2.069			m=	1.29570	
	QSTD	b= r=	-0.025		QA	b=	-0.01582	
		1-	0.555	33		r=	0.99999	
	No.1		10 . 11/2 . 1/2	Calculation				
		/std/ Δ Time	/Pstd)(Tstd/Ta)	$Va = \Delta Vol((Pa - \Delta P)/Pa)$			
	4314-	stu/anne	For subseque	ent flow rat	Qa= Va/ΔTime rate calculations:			
	Qstd=	1/m ((_AH(-	Pa Pstd (Tstd Ta)-b)			(Ta/Pa))-b)	
<u>'</u>	Standard	Conditions		, ,		11.	11	
Tstd:	298.15 •	К		Г		RECAL	IBRATION	
Pstd:		nm Hg		1				1000
ΔH: calibrato		er reading (in	H2O)				nual recalibratio egulations Part 5	
ΔP: rootsme	ter manome	ter reading (r					Reference Meth	
Ta: actual ab	solute temp		1-)				nded Particulate	
	rometric pre	essure (mm H	(g)				e, 9.2.17, page 3	
Pa: actual ba b: intercept				1	the	Atmospher	e, 9.2.17, page 3	10

Tisch Environmental, Inc. 145 South Miami Avenue

Village of Cleves, OH 45002

<u>www.tisch-env.com</u> TOLL FREE: (877)263-7610 FAX: (513)467-9009



I

aurecon

HIVOL SAMPLER CALIBRATION DATA SHEET (TSP)						
Site Information						
Location:	YMT Catholic Primary School	Site ID:	W-A6	Date:	28-Jun-2024	
Serial No:	1084	Model:	TE-5170X	Operator:	Andy Li	

	Ambien	t Conditi	on	
Actual Pressure during Calibration (P _a) (mm Hg):	756.7 Actual Temperature during Calibration (T _a) (deg K):			304.2
	Calibra	tion Orifi	се	
Model:	TE-5	5025A	Slope (m _c):	2.06920
Serial No.:	3465		Intercept (b _c):	-0.02547
Calibration Due Date:	15-Jan-25		Corr. Coeff:	0.99999

	Calibration Data							
Plate or	∆H₂O	Qa, X-Axis	I, CFM	IC, Y-Axis				
Test #	(in)	(m ³ /min)	(chart)	(corrected)				
18	10.80	1.581	59.0	58.27				
13	8.30	1.388	55.0	54.32				
10	6.10	1.191	48.0	47.41				
7	4.10	0.979	42.0	41.48				
5	3.20	0.866	39.0	38.52				

Sampler Calibtation Relationship (Qa on x-axis, IC on y-axis)

28.5008

b=

Calculations

13.7744

Corr. Coeff=____ 0.9974


 $Qa = 1/m_c*[Sqrt (\Delta H_2O*(P_a/P_{Std})*(T_{Std}/T_a))-b_c]$ $IC = I^*(Sqrt (P_a/P_{Std})^*(T_{Std}/T_a))$

Qa = actual flow rate IC = corrected chart response I = actual chart response m_c = calibrator slope b_c = calibrator intercept

m=___

m = sampler slope b = sampler intercept T_{Std} = 298 deg K P_{Std} = 760 mm Hg T_a = actual temperature during calibration (deg K)

 P_a = actual pressure during calibration (mm Hg)





aurecon

HIVOL SAMPLER CALIBRATION DATA SHEET (TSP)

Site Information							
Location:	Man Cheong Building	Site ID:	W-A6	Date:	28-Jun-2024		
Serial No:	1050	Model:	TE-5170X	Operator:	Andy Li		

Ambient Condition							
Actual Pressure during Calibration (P _a) (mm Hg):	756.7 Actual Temperature during Calibration (T _a) (deg K):		304.2				
Calibration Orifice							
Model:	TE-5	025A	Slope (m _c):	2.06920			
Serial No.:	3465		Intercept (b _c):	-0.02547			
Calibration Due Date:	15-Jan-25		Corr. Coeff:	0.99999			

		Calibration Data		
Plate or	∆H₂O	Qa, X-Axis	I, CFM	IC, Y-Axis
Test #	(in)	(m ³ /min)	(chart)	(corrected)
18	10.30	1.544	59.0	58.27
13	8.80	1.428	56.0	55.31
10	6.60	1.239	50.0	49.39
7	4.30	1.002	43.0	42.47
5	3.40	0.892	38.0	37.53

Sampler Calibtation Relationship (Qa on x-axis, IC on y-axis)

31.3219 m=__

b= 10.3461

Calculations


Corr. Coeff= 0.9976

 $Qa = 1/m_{c}^{*}[Sqrt (\Delta H_{2}O^{*}(P_{a}/P_{Std})^{*}(T_{Std}/T_{a}))-b_{c}]$ $IC = I^{*}(Sqrt (P_{a}/P_{Std})^{*}(T_{Std}/T_{a}))$

Qa = actual flow rate IC = corrected chart response I = actual chart response m_c = calibrator slope

b_c = calibrator intercept

m = sampler slope b = sampler intercept T_{Std} = 298 deg K P_{Std} = 760 mm Hg T_a = actual temperature during calibration (deg K) P_a = actual pressure during calibration (mm Hg)





aurecon

HIVOL SAMPLER CALIBRATION DATA SHEET (TSP)						
Site Information						
Location:	YMT Catholic Primary School	Site ID:	W-A6	Date:	17-Jul-2024	
Serial No:	1084	Model:	TE-5170X	Operator:	Andy Li	
Ambient Condition						

Ambient Condition							
Actual Pressure during Calibration (P _a) (mm Hg):	755.0	Actual Temperature during Calibration (T _a) (deg K):		303.3			
Calibration Orifice							
Model:	TE-5	025A	Slope (m _c):	2.06920			
Serial No.:	3465		Intercept (b _c):	-0.02547			
Calibration Due Date:	15-Jan-25		Corr. Coeff:	0.99999			

		Calibration Data		
Plate or	∆H₂O	Qa, X-Axis	I, CFM	IC, Y-Axis
Test #	(in)	(m ³ /min)	(chart)	(corrected)
18	10.50	1.560	62.0	61.26
13	8.60	1.413	58.0	57.31
10	7.10	1.285	55.0	54.34
7	4.50	1.025	46.0	45.45
5	3.50	0.906	41.0	40.51

Sampler Calibtation Relationship (Qa on x-axis, IC on y-axis)

m= 31.6134

b= 12.65

Calculations


12.6506

Corr. Coeff= 0.9959

 $\begin{aligned} &\mathsf{Qa} = 1/\mathsf{m_c}^*[\mathsf{Sqrt}\;(\Delta\mathsf{H}_2\mathsf{O}^*(\mathsf{P}_a/\mathsf{P}_{\mathsf{Std}})^*(\mathsf{T}_{\mathsf{Std}}/\mathsf{T}_a))\text{-}\;\mathsf{b_c}] \\ &\mathsf{IC} = \mathsf{I}^*(\mathsf{Sqrt}\;(\mathsf{P}_a/\mathsf{P}_{\mathsf{Std}})^*(\mathsf{T}_{\mathsf{Std}}/\mathsf{T}_a)) \end{aligned}$

 $\begin{array}{l} Qa = actual \ flow \ rate \\ IC = corrected \ chart \ response \\ I = actual \ chart \ response \\ m_c = calibrator \ slope \\ b_c = calibrator \ intercept \end{array}$

 $\label{eq:stars} \begin{array}{l} m = sampler slope \\ b = sampler intercept \\ T_{std} = 298 \mbox{ deg K} \\ P_{std} = 760 \mbox{ mm Hg} \\ T_a = actual temperature during calibration (deg K) \\ P_a = actual pressure during calibration (mm Hg) \end{array}$





aurecon

HIVOL SAMPLER CALIBRATION DATA SHEET (TSP)

	Site Information						
Location:	Man Cheong Building	Site ID:	W-A6	Date:	17-Jul-2024		
Serial No:	1050	Model:	TE-5170X	Operator:	Andy Li		

Ambient Condition							
Actual Pressure during Calibration (P _a) (mm Hg):	755.0	5.0 Actual Temperature during Calibration (T _a) (deg K):		303.3			
Calibration Orifice							
Model:	TE-S	5025A	Slope (m _c):	2.06920			
Serial No.:	3465		Intercept (b _c):	-0.02547			
Calibration Due Date:	15-Jan-25		Corr. Coeff:	0.99999			

		Calibration Data		
Plate or	∆H₂O	Qa, X-Axis	I, CFM	IC, Y-Axis
Test #	(in)	(m³/min)	(chart)	(corrected)
18	11.00	1.596	59.0	58.29
13	8.90	1.437	53.0	52.37
10	7.00	1.276	49.0	48.41
7	4.70	1.048	42.0	41.50
5	3.30	0.880	38.0	37.55

Sampler Calibtation Relationship (Qa on x-axis, IC on y-axis)

28.7108 m=__

11.8172 b=

Calculations


Corr. Coeff= 0.9976

 $Qa = 1/m_{c}^{*}[Sqrt (\Delta H_{2}O^{*}(P_{a}/P_{Std})^{*}(T_{Std}/T_{a}))-b_{c}]$ $IC = I^{*}(Sqrt (P_{a}/P_{Std})^{*}(T_{Std}/T_{a}))$

Qa = actual flow rate IC = corrected chart response I = actual chart response m_c = calibrator slope

b_c = calibrator intercept

m = sampler slope b = sampler intercept T_{Std} = 298 deg K P_{Std} = 760 mm Hg $\rm T_a$ = actual temperature during calibration (deg K) P_a = actual pressure during calibration (mm Hg)



Appendix I Calibration Certificates (Noise)

(A+A)*L Acoustics and Air Testing Laboratory Co. Ltd. 聲量】||| 聲學及空氣測試實驗室有限公司

Certificate of Calibration

for

Description:	Sound Level Meter
Manufacturer:	NTi Audio
Type No.:	XL2 (Serial No.: A2A-09696-E0)
Microphone:	ACO 7052 (Serial No.:73780)
Preamplifier:	NTi Audio MA220 (Serial No.:6282)

Submitted by:

Customer: Aurecon Hong Kong Limited Address: Unit 1608, 16/F, Tower B, . Manulife Financial Centre, 223-231 Wai Yip Street, Kwun Tong, Kowloon, Hong Kong.

Upon receipt for calibration, the instrument was found to be:

✓ Within (31.5Hz − 8kHz)
 □ Outside
 the allowable tolerance.

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 28 February 2024

Date of calibration: 02 March 2024

Date of NEXT calibration: 01 March 2025

Calibrated by: David Calibration Technician

Date of issue: 02 March 2024

Certificate No.: APJ23-146-CC003

Certified by:____

Mr. Ng Yan Wa Laboratory Manager

age 1 of 4

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong Tel: (852) 2668 3423 Fax:(852) 2668 6946 Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

Acoustics and Air Testing Laboratory Co. Ltd. 聲聲 及空氣測試實驗室有限公司 (A+A)*

Calibration Precaution: 1.

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point. -

2. **Calibration Conditions:**

Air Temperature:	22.9 °C
Air Pressure:	1005 hPa
Relative Humidity:	61.2 %

3. Calibration Equipment:

	Туре	Serial No.	Calibration Report Number	Traceable to	
Multifunction Calibrator	B&K 4226	2288467	AV220061	HOKLAS	

4. Calibration Results

Sound Pressure Level

Reference Sound Pressure Level

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq.	Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dBA	SPL	Fast	94	1000	94.1	±0.4

Linearity

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. W	eighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
				94		94.1	Ref
30-130	dBA	SPL	Fast	104	1000	104.1	±0.3
		_		114		114.1	±0.3

Time Weighting

Setting of Unit-under-test (UUT)			Appl	ied value	UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. W	eighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
20 120	A D A	SPL	Fast	04	1000	94.1	Ref
30-130 dBA	SPL	Slow	94	1000	94.1	±0.3	
rate No · Ai	0 172 1 44	CCOD			(and	NR TESTING LABORATOR	Page 2 of 4

Certificate No.: APJ23-146-CC003

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street , Fo Tan, Shatin, N.T., Hong Kong Tel: (852) 2668 3423 Fax:(852) 2668 6946 Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

(A+A)*L Acoustics and Air Testing Laboratory Co. Ltd. 聲聲及空氣測試實驗室有限公司

Frequency Response

Linear Response

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. We	eighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
					31.5	94.0	±2.0
					63	94.1	±1.5
			125	94.1	±1.5		
			250	94.1	±1.4		
30-130	dB	SPL	Fast	94	500	94.1	±1.4
					1000	94.1	Ref
				2000	94.4	±1.6	
				4000	95.2	±1.6	
			8000	94.5	+2.1; -3.1		

A-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. W	eighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
					31.5	54.6	-39.4 ±2.0
					63	67.9	-26.2 ±1.5
				125	78.0	-16.1 ±1.5	
				250	85.4	-8.6±1.4	
30-130	dBA	SPL	Fast	94	500	90.9	-3.2±1.4
					1000	94.1	Ref
					2000	95.6	+1.2±1.6
				4000	96.2	+1.0 ±1.6	
			8000	93.4	-1.1+2.1; -3.1		

C-weighting

Sett	Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. W	eighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
					31.5	91.0	-3.0 ±2.0
					63	93.3	-0.8 ±1.5
			125	93.9	-0.2 ±1.5		
				250	94.1	-0.0 ±1.4	
30-130	dBC	SPL	Fast	94	500	94.2	-0.0 ±1.4
					1000	94.1	Ref
					2000	94.2	-0.2±1.6
					4000	94.4	-0.8 ±1.6
				8000	91.5	-3.0 +2.1: -3.1	

Certificate No.: APJ23-146-CC003

(A+A) *L Page 3 of 4

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong Tel: (852) 2668 3423 Fax:(852) 2668 6946 Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

(A+A)*L Acoustics and Air Testing Laboratory Co. Ltd. 聲聲及空氣測試實驗室有限公司

5. Calibration Results Applied

The results apply to the particular unit-under-test only. All calibration points are within manufacture's specification as IEC 61672 Class 1.

Uncertainties of Applied Value:

94 dB	31.5 Hz	± 0.10
	63 Hz	± 0.05
	125 Hz	± 0.05
	250 Hz	± 0.05
	500 Hz	± 0.05
	1000 Hz	± 0.05
	2000 Hz	± 0.05
	4000 Hz	± 0.05
	8000 Hz	± 0.10
104 dB	1000 Hz	± 0.05
114 dB	1000 Hz	± 0.05

The uncertainties are evaluated for a 95% confidence level.

Note:

The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. (A+A)*L shall not be liable for any loss or damage resulting from the use of the equipment.

Certificate No.: APJ23-146-CC003



Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong Tel: (852) 2668 3423 Fax:(852) 2668 6946 Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com

Acoustics and Air Testing Laboratory Co. Ltd. 聲學及空氣測試實驗室有限公司 (A+A)*

Certificate of Calibration

for

Description:	Sound Level Calibrator
Manufacturer:	RION
Type No.:	NC-75
Serial No.:	34724244

Submitted by:

Customer:	Acuity Sustainability Consulting Limited
Address:	Unit E, 12/F, Ford Glory Plaza,
	Nos. 37-39 Wing Hong Street,
	Cheung Sha Wan, Kowloon,
	Hong Kong

Upon receipt for calibration, the instrument was found to be:

\checkmark	Within
	Outside

the allowable tolerance.

The test equipments used for calibration are traceable to National Standards via:

The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 27 July 2023

Date of calibration: 3 August 2023

Date of NEXT calibration: 2 August 2024

Calibrated by:

Calibration Technician

Certified by: Mr. Ng Yan Wa Laboratory Manager

Page 1 of 2

Certificate No.: APJ23-049-CC004

Date of issue: 3 August 2023

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo	Tan, Shatin, N.T., Hong Kong
Tel: (852) 2668 3423	Fax:(852) 2668 6946
Homepage: http://www.aa-lab.com	E-mail: inquiry@aa-lab.com



1. Calibration Precautions:

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

2. Calibration Specifications:

Calibration check

3. Calibration Conditions:

Air Temperature:	22.6 °C
Air Pressure:	1006 hPa
Relative Humidity:	52.9 %

4. Calibration Equipment:

Test Equipment	Туре	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV220061	HOKLAS
Sound Level Meter	RION NA-28	30721812	AV220120	HOKLAS

5. Calibration Results

5.1 Sound Pressure Level

Nominal value	Accept lower level	Accept upper level	Measured value		
dB	dB	dB	dB		
94.0	93.6	94.4	94.0		

Note:

The values given in this certification only related to the values measured at the time of the calibration.



Certificate No.: APJ23-049-CC004

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong Tel: (852) 2668 3423 Fax:(852) 2668 6946 Homepage: http://www.aa-lab.com E-mail : inquiry@aa-lab.com Page 2 of 2

Appendix J The Certification of Laboratory with HOKLAS Accredited Analytical Tests



Hong Kong Accreditation Service 香港認可處

Certificate of Accreditation

認可證書

This is to certify that 特此證明

ACUMEN LABORATORY AND TESTING LIMITED

浩科檢測中心有限公司

Flat/Rm D, 12/F, Ford Glory Plaza, Nos. 37-39 Wing Hong Street, Cheung Sha Wan, Kowloon, Hong Kong

香港九龍長沙淵永康街37-39號福源廣場12樓D室

Is accredited by the Hong Kong Accreditation Service (HKAS) to ISO/IEC 17025:2017 for performing specific laboratory activities as listed in the scope of accreditation within the test category of 攫香港認可處根據ISO/IEC 17025:2017認可 進行難於認可範圍內下遞測試類別中的指定實驗所活動

> Environmental Testing 環境測試

This accreditation to ISO/IEC 17025:2017 demonstrates technical competence for a defined scope and the implementation of a management system relevant to Isboratory operation (see joint IAF-ILAC-ISO Communique)). 此項 ISO/IEC 17025:2017 的經可資格證明社實驗所具續指注範疇內所須的技術能力並 實施一案與實驗所證作相關的質理體系 (見國際認可論壇、國際實驗所認可合作相識及國際標準化組織的綜合公領)。

The common seal of HKAS is affixed hereto by the authority of the HKAS Executive 現經香港認可處執行機關授權在此畫上香港認可處的印章

SHUM Wal-leung, Executive Administrator 執行幹事 沈偉良 Issue Date : 15 November 2021 笯發日期 : 二零二一年十一月十五日

Registration Number: HOKLAS 241 註冊號碼:



Date of First Registration: 16 July 2014 首次註冊日期:二零一四年七月十六日

This certificate is issued subject to the terms and conditions laid down by MKAS 本證書俗冊者通經可處訂立的導致及媒件發出 L002316



Hong Kong Accreditation Service 香港認可處

Certificate of Accreditation

認可證書

This is to certify that 特此證明

ALS TECHNICHEM (HK) PTY LIMITED

11/F, Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong 香港新界葵涌永業街1-3號忠信針織中心11樓

is accredited by the Hong Kong Accreditation Service (HKAS) to ISO/IEC 17025:2017 for performing specific laboratory activities as listed in the scope of accreditation within the test category of 遵香港部可處根據ISO/IEC 17025:2017認可 進行載於認可範圍內下述溯試類別中的指定實驗所活動

Environmental Testing

環境測試

This accreditation to ISO/IEC 17025:2017 demonstrates technical competence for a defined scope and the implementation of a management system relevant to laboratory operation (see joint IAF-ILAC-ISO Communique). 此項 ISO/IEC 17025:2017 的認可資格證明此實驗所具備指定範疇內所須的技術能力並

實施一套與實驗所逐作相關的管理體系 (見圖原認可論證、圖原實驗所認可含作相識及國際標準化相識的聯合公報)。

The common seal of HKAS is affixed hereto by the authority of the HKAS Executive 現經香港認可處執行機關授權在此蓋上香港認可處的印章

SHUM Wai-leung, Executive Administrator 執行幹事 沈偉良 Issue Date : 28 February 2020 簽發日期 : 二零二零年二月二十八日


Registration Number : HOKLAS 066 註冊號碼 :



Date of First Registration : 15 September 1995 首次註冊日期 : 一九九五年九月十五日

This certificate is issued subject to the terms and conditions laid down by HKAS 本證書按照書港認可處訂立的條款及條件發出 ∟001934

Appendix K Location Plan of Noise and Air Quality Monitoring Station

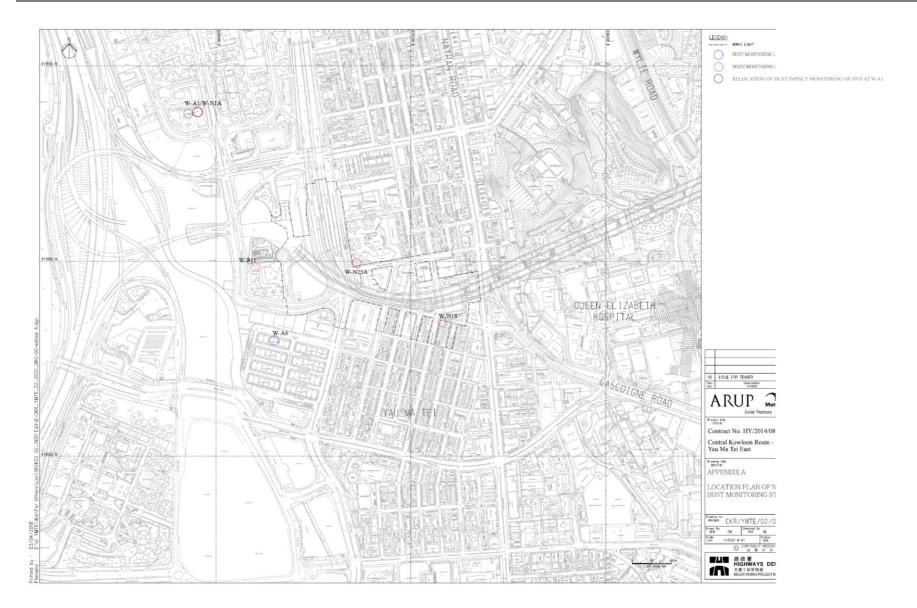

Appendix L Monitoring Data (Air Monitoring)

Location: Monitoring date: Parameter : Other Factors Yau Ma Tei Catholic Primary School (Hoi Wang Road) (W-A1) 2, 6, 12, 18, 24 and 30 July 2024 TSP 1-hour Nearby traffic

	1-hour TSP (μg/m ³)									
Date	Weather	Start Time	1 st Hour (μg/m ³)	2 nd Hour (μg/m ³)	3 rd Hour (μg/m ³)					
02/07/2024	Fine	9:13	67	57	62					
06/07/2024	Fine	9:10	55	60	66					
12/07/2024	Fine	10:57	60	65	64					
18/07/2024	Fine	9:14	59	64	66					
24/07/2024	Fine	9:16	55	64	65					
30/07/2024	Fine	9:37	58	51	56					
Min	imum: 51 μg/m	3		Maximum: 67 µg	$/m^3$					

Location: Monitoring date: Parameter : Other Factors Man Cheong Building (W-A6) 2, 6, 12, 18, 24 and 30 July 2024 TSP 1-hour Nearby traffic

	1-hour TSP (μg/m ³)										
Date	Weather	Start Time	1 st Hour (μg/m ³)	2 nd Hour (μg/m ³)	3 rd Hour (μg/m ³)						
02/07/2024	Fine	10:46	60	63	67						
06/07/2024	Fine	10:50	67	61	60						
12/07/2024	Fine	12:26	68	69	61						
18/07/2024	Fine	10:49	68	57	55						
24/07/2024	Fine	10:43	68	58	63						
30/07/2024	Fine	13:09	64	59	54						
ľ	Minimum: 54	µg/m ³		Maximum: 69 µg	$/m^3$						

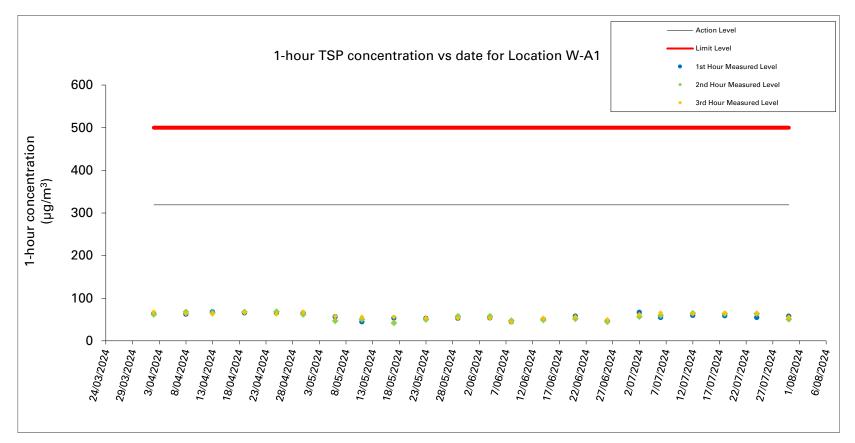


Figure 1: Graphical Illustration of Measured 1-hour TSP ($\mu g/m^3$) Levels at W-A1

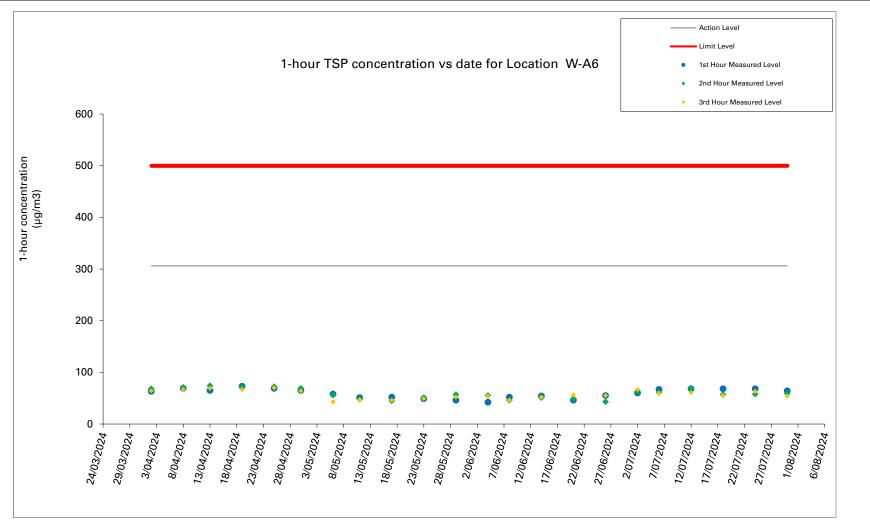


Figure 2: Graphical Illustration of Measured 1-hour TSP (µg/m³) Levels at W-A6

Location: Monitoring date: Parameter : Other Factors Yau Ma Tei Catholic Primary School (Hoi Wang Road) (W-A1) 2, 6, 12, 18, 24 and 30 July 2024 TSP 24-hour Nearby traffic

										Date of	f Calibration:	28-Jun-24		Slope =	28.5008
										Calibrati	on due date:	13-Jul-24		Intercept =	13.7744
										Date of	^f Calibration:	17-Jul-24		Slope =	31.6134
										Calibrati	on due date:	1-Aug-24		Intercept =	12.6506
Start Date	Weather Elapse Time Condition		С	hart Reading		Avg Air Temp	Avg Atmospheric Pressure	Flow Rate	Standard Air Volume	Filter W	eight (g)	Particulate weight	Corr.		
	Condition	Initial	Final	Actual (min)	Min	Max	Avg	(°C)	(hPa)	(m ³ /min)	(m ³)	Initial	Final	(g)	$(\mu g/m^3)$
2/07/2024	Fine	9111.3	9135.3	1440.0	40	40	40.0	30.5	1009.2	0.90	1299	2.7453	2.8125	0.0672	52
6/07/2024	Fine	9135.3	9159.3	1440.0	40	40	40.0	31.2	1008.6	0.90	1295	2.7470	2.8131	0.0661	51
12/07/2024	Fine	9159.3	9183.3	1440.0	40	41	40.5	30.1	1005.1	0.91	1317	2.6992	2.7384	0.0392	30
18/07/2024	Fine	9183.3	9207.3	1440.0	40	40	40.0	28.7	1008.3	0.85	1226	2.6751	2.7252	0.0501	41
24/07/2024	Fine	9207.3	9231.3	1440.0	40	40	40.0	30.6	994.6	0.83	1196	2.7023	2.8810	0.1787	149
30/07/2024	Fine	9231.3	9255.3	1440.0	40	40	40.0	27.9	1006.9	0.85	1226	2.7360	2.8224	0.0864	70
				,						Maximum:	149	$\mu g/m^3$	Minimum:	30	$\mu g/m^3$

Parameter	Monitoring date:2, 6, 12, 18, 24 and 30 July 2024Parameter :TSP 24-hourOther FactorsNearby traffic																
										Date of	Calibration:	28-Jun-24		Slope =	31.3219		
										Calibrati	on due date:	13-Jul-24		Intercept =	10.3461		
										Date of	Calibration:	17-Jul-24		Slope =	28.7108		
										Calibrati	on due date:	1-Aug-24		Intercept =	11.8172		
Start Date	Weather		Elapse Time		Chart Reading		Chart Reading		Chart Reading		Avg Atmospheric Pressure	Flow Rate	Standard Air Volume	Filter We	eight (g)	Particulate weight	Conc.
	Condition	Initial	Final	Actual (min)	Min	Max	Avg	(°C)	(hPa)	(m ³ /min)	(m ³)	Initial	Final	(g)	$(\mu g/m^3)$		
2/07/2024	Fine	11571.7	11595.7	1440.00	41	41	41.0	30.5	1009.2	0.96	1385	2.7380	2.7950	0.0570	41		
6/07/2024	Fine	11595.7	11619.7	1440.00	41	41	41.0	31.2	1008.6	0.96	1381	2.6895	2.7309	0.0414	30		
12/07/2024	Fine	11619.7	11643.7	1440.00	41	41	41.0	30.1	1005.1	0.96	1378	2.7067	2.7358	0.0291	21		
18/07/2024	Fine	11643.7	11667.7	1440.00	41	41	41.0	28.7	1008.3	1.00	1441	2.6907	2.7379	0.0472	33		
24/07/2024	Fine	11667.7	11691.7	1440.00	41	41	41.0	30.6	994.6	0.98	1407	2.6998	2.8283	0.1285	91		
30/07/2024	Fine	11691.7	11715.7	1440.00	40	41	40.5	27.9	1006.9	0.98	1416	2.7370	2.8282	0.0912	64		
												µg/m ³					

Acuity Sustainability Consulting Ltd.

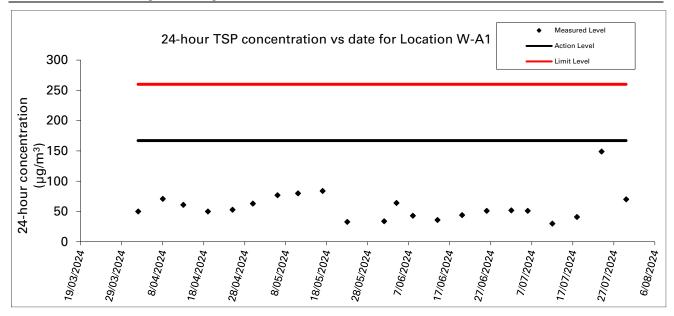


Figure 3: Graphical Illustration of Measured 24-hour TSP (µg/m³) Levels at W-A1


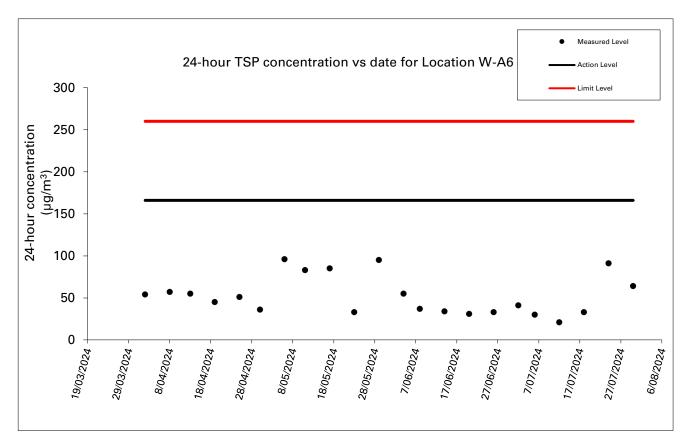


Figure 4: Graphical Illustration of Measured 24-hour TSP (µg/m³) Levels at W-A6

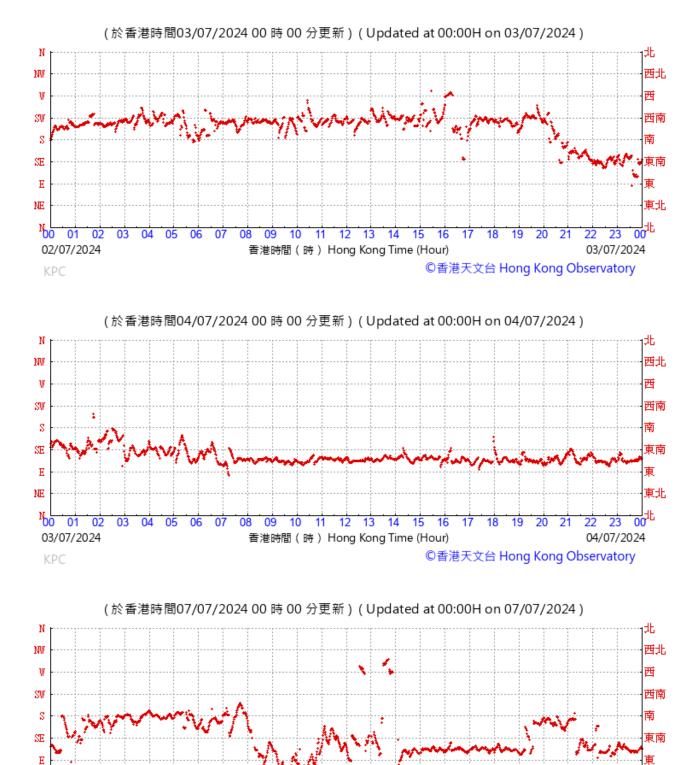

14

15

13

香港時間 (時) Hong Kong Time (Hour)

16 17

18 19

21

22 23

07/07/2024

20

©香港天文台 Hong Kong Observatory

東北

핸바

Wind direction data for 2, 3, 6, 7, 12, 13, 18, 19, 24, 25, 30 and 31 July 2024

03

02

04

07

08 09

10 11 12

06


05


NE


N00 01

KPC

06/07/2024

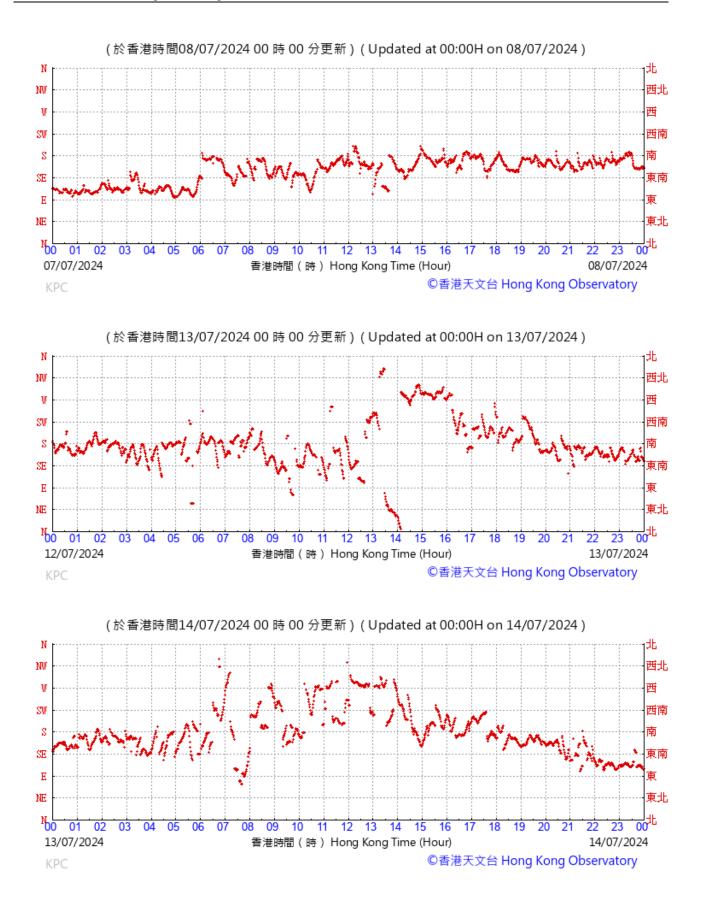

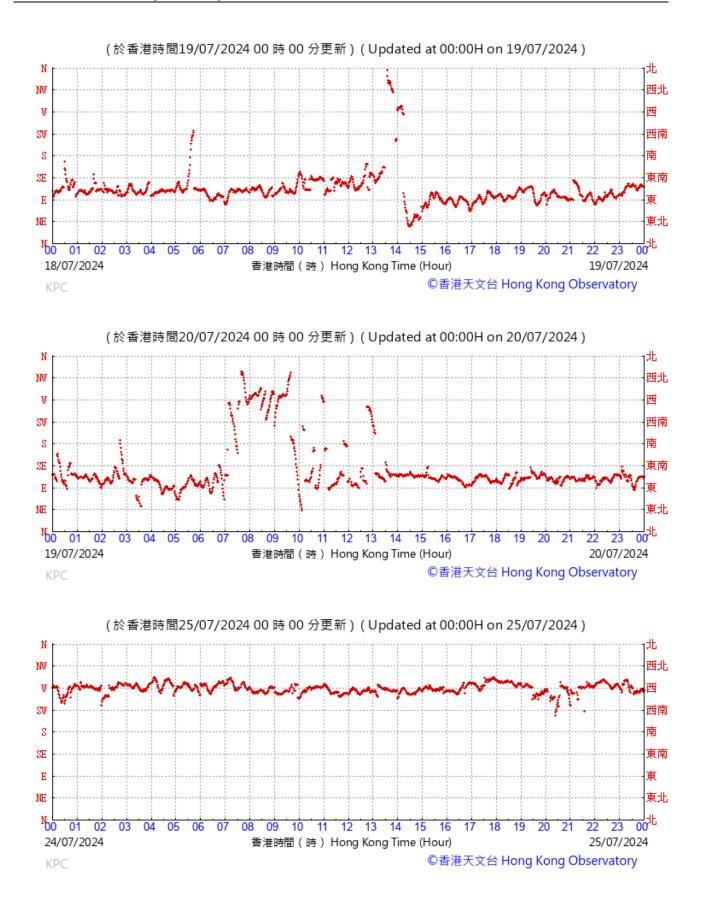

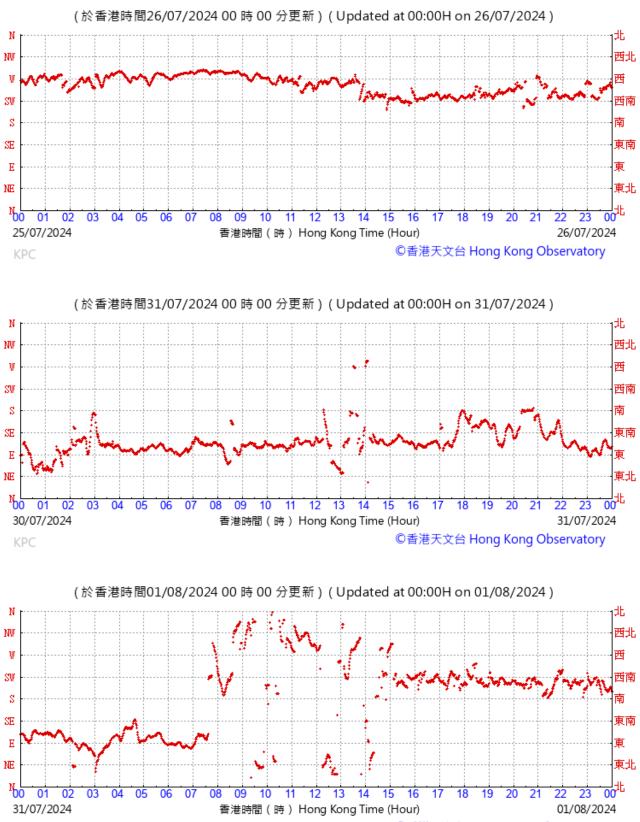


KPC





Wind speed data for 2, 3, 6, 7, 12, 13, 18, 19, 24, 25, 30 and 31 July 2024



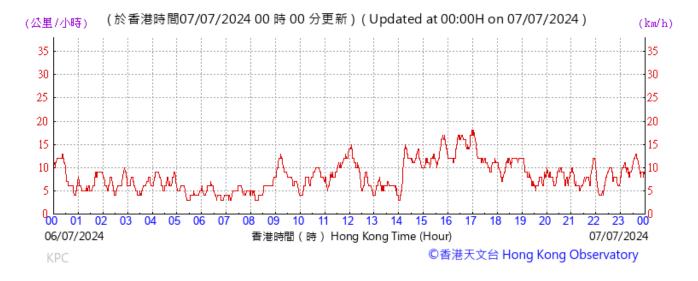



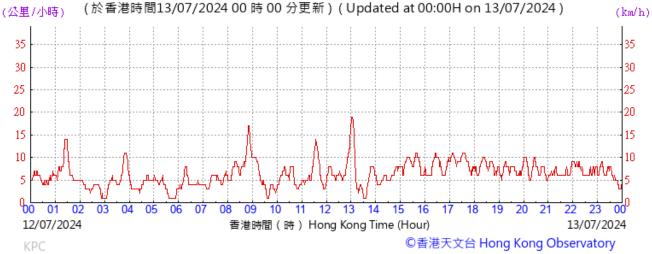

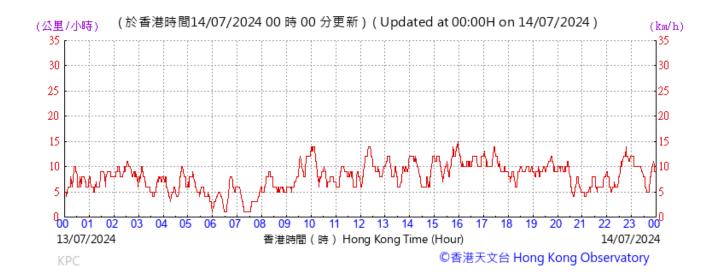








Acuity Sustainability Consulting Ltd.





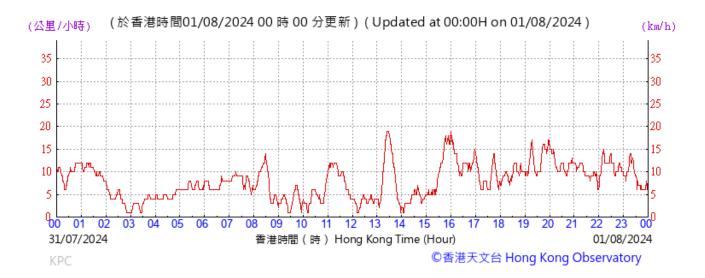

Appendix M Monitoring Data (Noise)

Location:

Yau Ma Tei Catholic Primary School (Hoi Wang Road) (W-N1A)

Monitoring date:	2, 6, 12, 18, 24 and 30 July 2024
Parameter :	L_{eq}, L_{10}, L_{90}
Other Factors	Nearby traffic

Noise Monitoring data:

Date	Weather	Start Time	-	End Time	L _{eq}	L ₁₀	L ₉₀	Wind speed (m/s)	Limit level
02/07/2024	Fine	9:13	-	9:43	68.8	72.2	64.9	3.6	70.0
06/07/2024	Fine	9:10	-	9:40	69.1	73.2	64.7	3.1	70.0
12/07/2024	Fine	10:59	-	11:29	67.9	69.9	65.8	2.5	70.0
18/07/2024	Fine	9:14	-	9:44	69.6	73.2	64.8	3.9	70.0
24/07/2024	Fine	9:16	-	9:46	69.6	72.2	65.2	3.5	70.0
30/07/2024	Fine	9:38	-	10:08	68.5	70.6	64.0	2.5	70.0

Remark: 1. No examination was scheduled at Yau Ma Tei Catholic Primary School during the monitoring date. The limit level of W-N1A would be 70 dB(A).

Location:

Hydan Place (W-N18)

Monitoring date: Parameter : Other Factors 2, 6, 12, 18, 24 and 30 July 2024 L_{eq}, L_{10}, L_{90} Nearby traffic

Noise Monitoring data:

Date	Weather	Start Time	-	End Time	L _{eq}	L ₁₀	L ₉₀	Wind speed (m/s)	Limit level
02/07/2024	Fine	13:50	-	14:20	69.6	72.5	60.9	4.4	75.0
06/07/2024	Fine	13:49	-	14:19	69.0	73.2	60.6	2.2	75.0
12/07/2024	Fine	13:30	-	14:00	69.5	71.4	68.0	1.2	75.0
18/07/2024	Fine	13:49	-	14:19	69.1	73.0	60.5	2.4	75.0
24/07/2024	Fine	13:53	-	14:23	68.9	73.0	60.5	3.6	75.0
30/07/2024	Fine	14:25	-	14:55	66.6	71.5	63.0	1.4	75.0

Location:

Prosperous Garden Block 1 (W-N25A)

Monitoring date:2, 6, 12, 18, 24 and 30 July 2024Parameter : L_{eq}, L_{10}, L_{90} Other FactorsNearby traffic

Noise Monitoring data:

Date	Weather	Start Time	-	End Time	L _{eq}	L ₁₀	L ₉₀	Wind speed (m/s)	Limit level
02/07/2024	Fine	13:06	-	13:36	69.7	73.4	59.8	4.7	75.0
06/07/2024	Fine	13:10	-	13:40	69.2	73.1	59.9	1.6	75.0
12/07/2024	Fine	9:15	-	9:45	70.4	71.6	60.7	1.7	75.0
18/07/2024	Fine	13:12	-	13:42	68.5	73.0	58.8	2.3	75.0
24/07/2024	Fine	13:09	-	13:39	68.9	73.1	60.5	4.2	75.0
30/07/2024	Fine	13:37	-	14:07	70.8	75.3	68.1	2.8	75.0

Location:

The Coronation Tower 1 (W-P11)

Monitoring date:2, 6, 12, 18, 24 and 30 July 2024Parameter : L_{eq}, L_{10}, L_{90} Other FactorsNearby traffic

Noise Monitoring data:

Date	Weather	Start Time	- End Time	L _{eq}	L_{10}	L ₉₀	Wind speed (m/s)	Limit level
02/07/2024	Fine	10:01	- 10:31	65.3	68.3	62.3	1.7	75.0
06/07/2024	Fine	10:03	- 11:15	64.9	68.1	61.9	1.9	75.0
12/07/2024	Fine	10:02	- 10:32	65.1	69.1	62.2	1.9	75.0
18/07/2024	Fine	10:06	- 13:30	65.6	68.6	62.0	2.1	75.0
24/07/2024	Fine	10:04	- 10:34	64.7	68.9	62.5	3.1	75.0
30/07/2024	Fine	10:31	- 11:01	65.5	68.6	63.2	2.2	75.0




Figure 1: Graphical Illustration of Measured Noise Levels at W-N1A

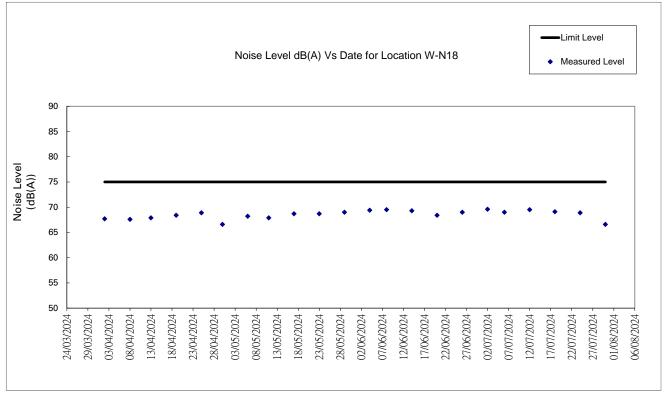


Figure 2: Graphical Illustration of Measured Noise Levels at W-N18

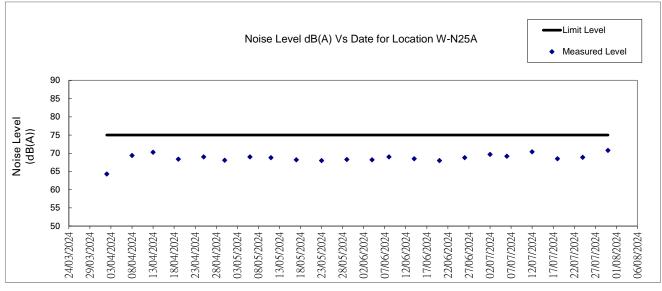


Figure 3: Graphical Illustration of Measured Noise Levels at W-N25A

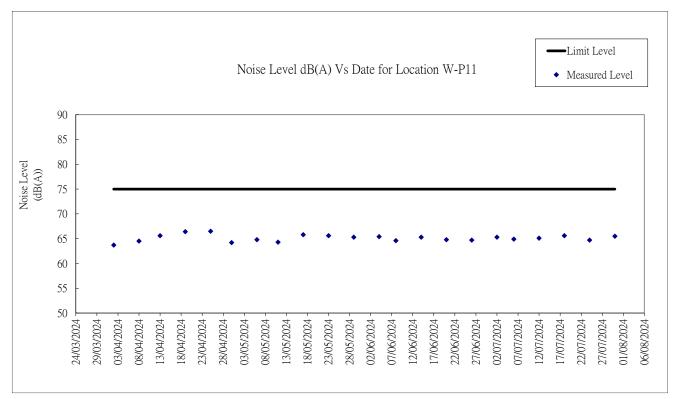


Figure 4: Graphical Illustration of Measured Noise Levels at W-P11

Appendix N Waste Flow Table

Monthly Summary Waste Flow Table

Name of Department: Highways Department

Monthly Summary Waste Flow Table for July 2024 [to be submitted not later than the 15th day of each month following reporting month] (All quantities shall be rounded off to 2 decimal place.)

			Actual Quantities of Ine	rt Construction Waste Generated Mont	hly	
Month	$ (a)=(b)+(c)+(d)+I+(f)+(g)+(h)+(i)+(j)+(k) \\ Total Quantity Generated $	(b) Hard Rock and Large Broken Concrete	(c) Reused in the Contract	(d) Reused in other Projects	(e) Disposed of as Public Fill	(f) Imported Fill
	(in 'tonnes)	(in 'tonnes)	(in 'tonnes)	(in 'tonnes)	(in 'tonnes)	(in 'tonnes)
Jan-24	3708.11	0.00	0.00	0.00	3482.35	0.00
Feb-24	3389.21	0.00	0.00	0.00	2397.59	466.88
Mar-24	4375.16	0.00	0.00	0.00	3359.54	767.55
Apr-24	2651.10	0.00	0.00	0.00	890.09	1631.93
May-24	2849.66	0.00	0.00	0.00	1895.76	739.82
Jun-24	1824.74	0.00	0.00	0.00	304.36	1347.51
Sub-total	18797.97	0.00	0.00	0.00	12329.69	4953.69
Jul-24	2379.28	0.00	0.00	0.00	88.71	2148.16
Aug-24	0.00					
Sep-24	0.00					
Oct-24	0.00					
Nov-24	0.00					
Dec-24	0.00					
Total	21177.25	0.00	0.00	0.00	12418.40	7101.85
2018	15.65	0.00	0.00	0.00	0.00	0.00
2019	71691.85	0.00	5534.00	8066.88	57313.64	415.55
2020	168891.36	0.00	15437.30	84381.54	68187.83	180.00
2021	213790.30	0.00	16567.28	79780.37	114965.52	1002.03
2022	140806.50	0.00	22476.00	20553.85	51490.05	44771.11
2023	126731.90	0.00	27490.00	104.07	92991.04	4240.52
Accumulated Total	743104.81	0.00	87504.58	192886.71	397366.48	57711.05

Contract No. / Works Order No.: <u>HY/2014/20</u>____

			-	Act	tual Quantities of <u>Non-ine</u>	ert Construction Waste	e Generated Monthly		
Month	(Me	(g) (h) Metals Paper/ cardboard packaging			(i) (Plastics Chemica		(j) cal Waste	(k) Others, e.g. General Refuse disposed at Landfill	
	(in '0	000kg)	(in '0	00kg)	(in '00	0kg)	(in '0	000kg)	(in 'tonnes)
	generated	recycled	generated	recycled	generated	recycled	generated	recycled	generated
Jan-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	225.76
Feb-24	0.00	399.61	0.00	0.00	0.00	0.34	0.00	0.00	124.79
Mar-24	0.00	78.31	0.00	0.0063	0.00	0.76	0.00	0.00	168.99
Apr-24	0.00	31.30	0.00	0.00	0.00	0.00	0.00	0.00	97.78
May-24	0.00	27.32	0.00	0.00	0.00	0.64	0.00	0.00	186.12
Jun-24	0.00	0.00	0.00	0.075	0.00	0.000	0.00	0.00	172.79
Sub-total	0.00	536.54	0.00	0.08	0.00	1.740	0.00	0.00	976.23
Jul-24	0.00	44.06	0.00	0.00	0.00	0.510	0.00	0.00	97.84
Aug-24									
Sep-24									
Oct-24									
Nov-24									
Dec-24									
Total	0.00	580.60	0.00	0.08	0.00	2.25	0.00	0.00	1074.07
2018	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	15.65
2019	0.00	106.04	0.00	0.20	0.00	1.47	2.11	0.00	251.96
2020	359.10	0.00	0.35	0.00	3.16	0.00	0.88	0.00	341.20
2021	945.79	0.00	0.20	0.00	3.34	0.00	0.00	0.00	525.77
2022	615.75	159.28	0.75	0.08	2.12	1.49	0.00	0.00	736.02
2023	0.00	716.48	0.00	0.33	0.00	4.46	0.00	0.00	1185.01
Accumulated Total	1920.64	1562.40	1.30	0.69	8.62	9.67	2.99	0.00	4129.68

Remark: Sub-total, Total and Accumulated Total are corrected to 2 decimal places. Construction waste records for June 2024 had been updated.

Appendix O Statistics on Complaint, Notifications of Summons and Successful Prosecutions

	Statistical Summary of Exc	ceedances
	Air Quality	
Reporting Period	Action Level	Limit Level
1 – 31 July 2024	0	0
	Noise	
Reporting Period	Action Level	Limit Level
1 – 31 July 2024	1	0

Statistical Summary of Environmental Complaints

Departing Deviad	Environmental Complaint Statistics				
Reporting Period	Frequency	Cumulative	Complaint Nature		
1 – 31 July 2024	1	19	Noise nuisance		

Statistical Summary of Environmental Non-compliance

Departing Deviad	Environmental Non-compliance Statistics				
Reporting Period	Frequency	Cumulative	Details		
1 – 31 July 2024	0	0	N/A		


Statistical Summary of Environmental Summons

Departing Devied		Environmental Summons Stat	tistics
Reporting Period	Frequency	Cumulative	Details
1 – 31 July 2024	0	0	N/A

Statistical Summary of Environmental Prosecution

Departing David]	Environmental Prosecution Sta	atistics
Reporting Period	Frequency	Cumulative	Details
1 – 31 July 2024	0	0	N/A

Appendix P Monitoring Schedule of the Coming Month

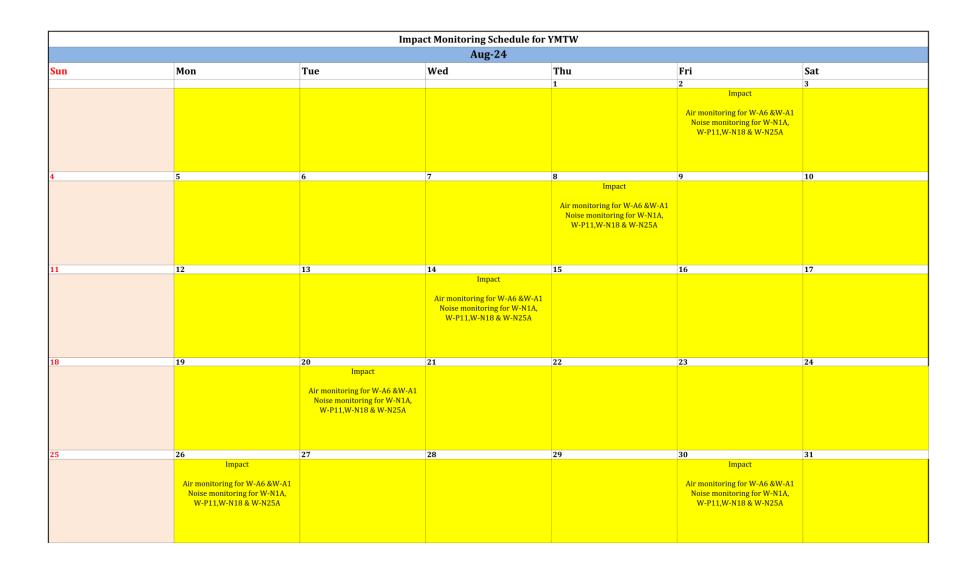


Appendix Q Interim Report for the Complaint


Interim Report on Environmental Complaint

Project	Central Kowloon Route, Yau Ma Tei West Section
Complaint Code	EC019_CKRYMTW20240706_001
Complaint description	The complainant was received on 14 Jun 2024, about construction noise from the site area near Hoi Yu House, Hoi Fu Court at 2330, starting from 6 May 2024. Further complaint was received on 6 Jul 2024.
Parameter	Construction Noise
Investigation finding	The complainant was received on 14 Jun 2024, about construction noise from the site area near Hoi Yu House, Hoi Fu Court at 2330, starting from 6 May 2024, starting from 6 May 2024. Further complaint was received on 6 Jul 2024.
	As confirmed by the Contractor, the night works near the concerned area ¹ during the concerned time period are the following:
	Emergency works were performed from 1900 on 14 May 2024 to 0900 on 15 May 2024. Urgent roadworks due to road subsidence were performed to ensure the safety of road users. The work had been reported to EPD via the online system and only the PMEs listed in the report were used ² . QPME label was provided on PME. SilentCUBE was used as noise mitigation measure.
	For construction works undertaken within restricted hours, the Contractor applied for valid Construction Noise Permits (CNP) (Permit No: GW-RE0437-24) which was granted from EPD, effective from 23 Apr 2024 to 29 Jun 2024 with coverage of the construction site near the concerned area ³ . Underground utility works were performed from 0100 to 0530 on 22, 23, and24 May 2024. PMEs used included hand-held breaker, concrete saw, excavator, dump truck, dump truck with grab, crane lorry, vibratory compactor, power rammer, vibratory roller, road marking material boiler, and portable generator. The aforementioned PME were allowed to be operated in the Working Zone during 0100 to 0530 from Tuesday to Saturday, not being a general holiday and not immediately following a general holiday. The number of each type of the PMEs used did not exceed the number listed on the CNP. The PMEs were not used for more than 14 days during the validity period of the CNP. Only one group of the PMEs was operating at any time. As confirmed by the Contractor, the conditions 3.d.4. to 3.d.10. and condition 4.d.3. to 4.d.6. of CNP GW-RE0437-24 were followed as noise mitigation measure. The Contractor had followed the requirements as stipulated in CNP. No violation and non-compliance of CNP was observed or recorded.
	On 29 Jun 2024, replacement of traffic sign on existing sign gantry was carried out from 0100 to 0530. The Contractor had applied for valid Construction Noise Permits (CNP) (Permit No: GW-RE687-24) which was granted from EPD, effective from 18 Jun 2024 to 10 Aug 2024 with coverage of the construction site near the concerned area ³ . The construction works were carried out at Yau Ma Tei interchange near the Yau Ma Tei Shelther. PMEs used included 1 lorry with crane, 1 lorry with elevation platform, 1 lorry with flashing directional sign, and 1 hand-held drill. The aforementioned PME were allowed to be operated in the Working Zone during 0100 to 0530 on any day not being a general holiday between Tuesday and Saturday if the preceding day is not a general holiday. Only one group of the PMEs was operating at any time. As confirmed by the Contractor, the conditions 3.d.4. to 3.d.9. and condition 4.d.3. to 4.d.6. of CNP GW-RE687-24 were followed as noise mitigation measure. The Contractor had followed the requirements as stipulated in CNP. No violation and non-compliance of CNP was observed or recorded.
	Lifting of steel element and nut installation were carried out from 0100 to 0530 during Tuesday to Saturday since 4 Jul 2024. The Contractor had applied for valid Construction Noise Permits (CNP) (Permit No: GW-RE771-24) which was granted from EPD, effective from 28 Jun 2024 to 31 Aug 2024 with coverage of the construction site near the concerned area ³ . The construction works were carried out at section of Hoi Wang Road near the Coronation. PMEs used included 1 lorry with crane and 1 lorry with flashing

	Zone during 0100 Saturday if the pre- operating at any the condition 4.d.3. to measure. The Contained and non-complianed Considering the fi- manual and the gr	to 0530 on any day ecceding day is not a me. As confirmed b to 4.d.9. of CNP G tractor had followed ce of CNP was obse fulfillment of stipu ranted CNP, it is co	lated requirements by the Contractor for EM&A oncluded that there was no non-compliance of the		
Actions taken / to be taken	 Project regarding noise quality impact from construction site. The Contractor had followed EM&A Manual, granted CNP and the CNMMP strictly to implement mitigation measures in order to minimize nuisance to the public. In view of public concerns, the following additional remedial measures are taken: Carry out site inspection to ensure all PMEs are well-maintained and in proper function to avoid excessive noise; Provide training to workers of using PME carefully to minimize noise; Reschedule the operation time of the noisy equipment to less sensitive hours if possible; and The Contractor is reminded to consider the use of temporary movable noise barrier when feasible and applicable. 				
Remarks (Shown in next page)		on of Emergency W Zone of CNP GW-F	Yorks RE0437-24, CNP GW-RE0687-24, and CNP GW-		
Prepared by ET (Acuity Sustainability Consulting Limited)	Kako Ho	Ho			
Reviewed by ETL (Acuity Sustainability Consulting Limited)	Kevin Li	K.			
Verified by IEC (ERM-Hong Kong, Limited)	Mandy To	Mandejz.			
Date	09 July 20	024			

Remark 1: Concerned Area

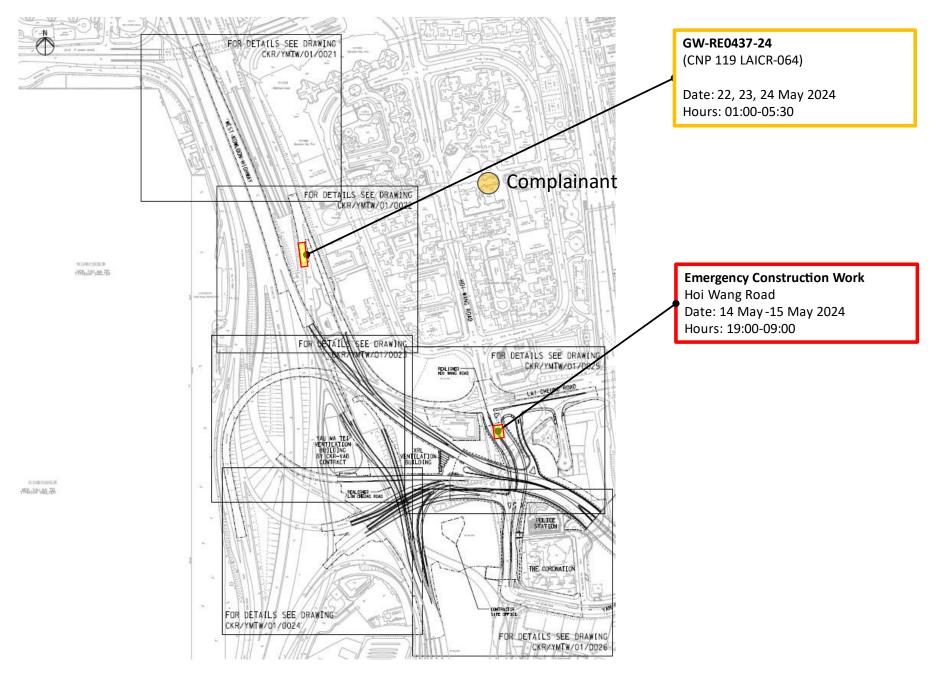

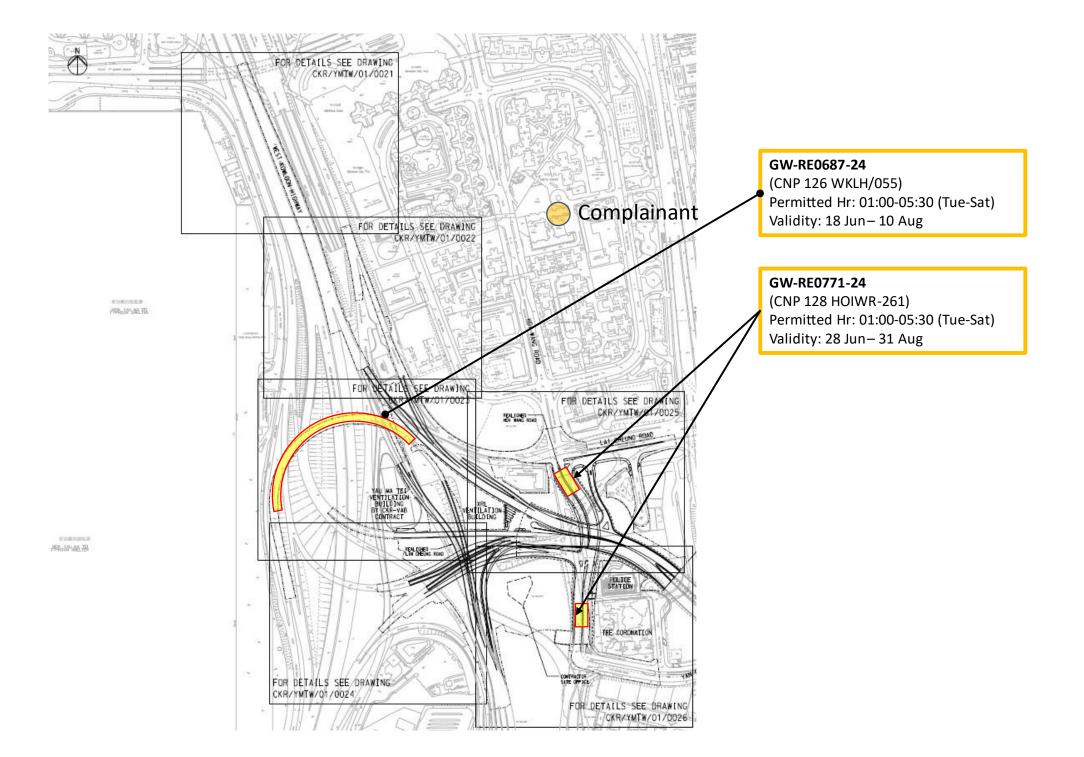

Remark 2: Notification of Emergency Works

Tsoi Cheuk Yip, Tony

From:	Record of Emergency Work During Restricted Hours <admin@nco-emergencywork.hk></admin@nco-emergencywork.hk>
Sent:	Tuesday, May 14, 2024 5:29 PM
To:	Tsoi Cheuk Yip, Tony
Subject:	[Acknowledgement] Record for Emergency Construction Work: 2024-05-14 19:00

CAUTION: This email originated from outside of the company. DO NOT click links or open attachments unless you recognise the sender

Allow sender Block sender

If no, why? :	
Is hand-held breaker used? ?	NO
If yes, what type? :	
Is Noise barrier provided for hand-held breaker? :	NO
If no, why? :	no breaker

2

This email acknowledges your Record for Emergency Construction Work submitted at 09:28 on 14/05/2024. Information appended below:

Date and time of receiving notification :	14/05/2024 17:28:44
Record Reference :	20240514-003
From :	Build King - SK ecoplant Joint Venture
Name & Post of PIC/Contact Person :	Benny LAM/ Site Agent
Telephone :	36228300
Fax :	36228302
Email :	tony.tsoi@buildking.hk
Date of work :	2024-05-14 19:00
HyD Emergency Serial Number :	M938990
Police ref :	
Name of Contractor :	Build King - SK ecoplant Joint Venture
Description and justification of Emergency Work :	Urgent roadworks due to road subsidence
Location of work :	
district:	Yau Tsim Mong
- Affected TPUs:	252

Works Details :


Noise barrier provided? :


Noise barrier details :


Details Location of Work		Date & Time	Details of work program	
Section of Hoi Wang Road junction at Lai Cheung Roa		Start:: 14/05/2024 19:00 End:: 15/05/2024 09:00	Excavation, backfill, reinstatement, road marking	
List of PME used and/or PCW carried out :	lorry,	,	ixer, crane lorry, asphalt paver, grab d roller, vibratory roller, power	
Noise control measure implemented :	QPMI	E, SilentCUBE		

YES

SilentCUBE

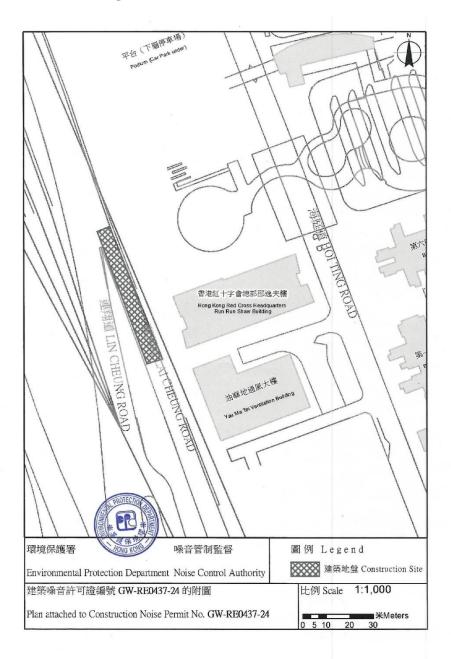

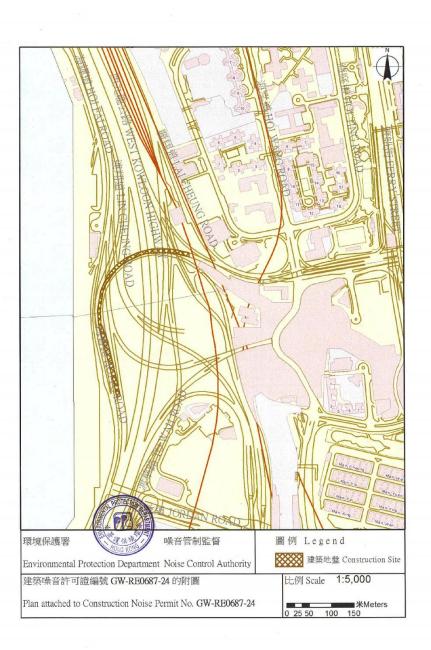

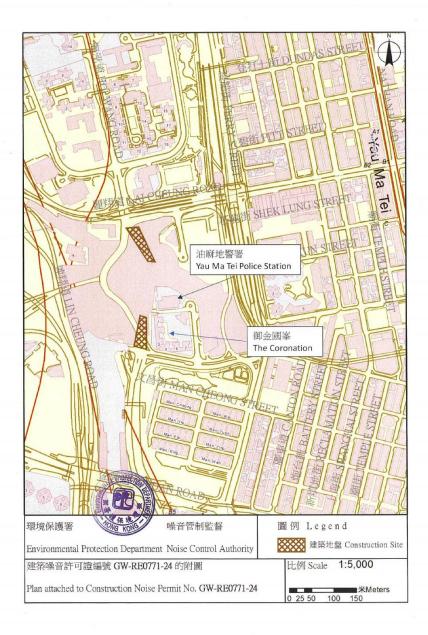

Central Kowloon Route Buildings, Electrical and Mechanical Works Contract No. HY/2019/13 (Yau Ma Tei West Area)

Gammon Construction Limited

Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works

Monthly EM&A Report No. 46 (July 2024)

Version 1.1 Date of Report: 8 August 2024

Certified By

BC'.

(Environmental Team Leader:

Ms. Betty Choi)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties

CINOTECH CONSULTANTS LTD

Room 1710, Technology Park, 18 On Lai Street, Shatin, NT, Hong Kong Tel: (852) 2151 2083 Fax: (852) 3107 1388 Email: info@cinotech.com.hk





Environmental Permit No. EP-457/2013/D

Central Kowloon Route

Independent Environmental Checker Verification

Works Contract:	Buildings, Electrical and Mechanical Works (HY/2019/13)		
Reference Document/Plan			
Document/Plan to be Certified/ Verified:	Monthly EM&A Report No.46 (Version 1.1) for Kai Tak East & Yau Ma Tei West Areas		
Date of Report:	08 August 2024		
Date received by IEC:	08 August 2024		

Reference EP Condition

Environmental Permit Condition:

Submission of Monthly EM&A Report of the Project

3.4 Four hard copies and one electronic copy of monthly EM&A Report shall be submitted to the Director within 2 weeks after the end of each reporting month throughout the entire construction period. The EM&A Reports shall include a summary of all non-compliance. The submissions shall be certified by the ET Leader and verified by the IEC as complying with the requirements as set out in the EM&A Manual before submission to the Director. Additional copies of the submission shall be provided to the Director upon request by the Director.

3.4

IEC Verification

I hereby verify that the above referenced document/plan complies with the above referenced condition of EP-457/2013/D.

Mandy 20.

Ms Mandy To Independent Environmental Checker Date:

08 August 2024

Our ref: 0436942_IEC Verification Cert_BEM_Monthly EM&A Rpt No.46_20240808.docx

		Page
EX	XECUTIVE SUMMARY	1
1	INTRODUCTION	3
Pu Pro Co	ckground rpose of the Report oject Organizations nstruction Activities undertaken during the Reporting Month mmary of EM&A Requirements	
	atues of Environmental Licensing and Permitting	
2	AIR QUALITY	6
	onitoring Requirements	
3	NOISE	6
	onitoring Requirements	
4	WASTE MANAGEMENT	7
	onitoring Requirements sults and Observations	
5	LANDSCAPE AND VISUAL	8
	onitoring Requirements sults and Observations	
6	ENVIRONMENTAL AUDIT	9
Im Im Su	e Audits plementation Status of Environmental Mitigation Measures plementation Status of Event and Action Plans mmary of Complaint, Warning, Notification of any Summons and Successful Prosec atus of Required Submission under Environmental Permit	
7	FUTURE KEY ISSUES	11
8	CONCLUSIONS AND RECOMMENDATIONS	12
Co	nclusions	

TABLE OF CONTENTS

LIST OF TABLES

Table I	Summary of Complaint/Summons/Prosecution in the Reporting Month
Table 1.1	Key Project Contacts
Table 1.2	Summary of Environmental Licensing and Permit Status
Table 4.1	Quantities of Waste Generated from the Project
Table 6.1	Observations and Recommendations of Site Inspections
Table 6.2	Status of Required Submission under Environmental Permit

LIST OF FIGURES

Figure 1.1	Site Layout Plan
Figure 1.2	Project Organisation for Environmental Monitoring and Audit

LIST OF APPENDICES

Appendix A	Construction	Programme
------------	--------------	-----------

- Appendix B Summary of Waste Generation and Disposal Records
- Appendix C Environmental Mitigation Implementation Schedule (EMIS)
- Appendix D Summaries of Environmental Complaint, Warning, Summon and Notification of Successful Prosecution

EXECUTIVE SUMMARY

Introduction

- This is the 46th Monthly Environmental Monitoring and Audit (EM&A) Report prepared by the Environmental Team (ET), Cinotech Consultants Ltd., for Contract No. HY/2019/13 "Central Kowloon Route – Buildings, Electrical and Mechanical Works". This report summarized the monitoring results and audit findings of the EM&A programme under the issued EP No. EP-457/2013/D, and in accordance with the EM&A programme in Yau Ma Tei West Area during the reporting period from 1st July 2024 – 31st July 2024.
- 2. The major site activities undertaken in Yau Ma Tei Area in the reporting month included:
 - Super-structure works
 - ABWF works
 - E&M Installation

Environmental Monitoring Works

- 3. Environmental monitoring for the Project was performed in accordance with the EM&A Manual and the monitoring results were checked and reviewed. Joint weekly site inspections with the representative of ET, Engineer Representative and the Contractor were conducted on 2, 9, 16, 23, & 30 July 2024, whereas joint site inspection with the representative of IEC was conducted on 16 July 2024. The implementation of the environmental mitigation measures, Event and Action Plans and environmental complaint handling procedures were also checked.
- 4. A summary of the non-compliance (exceedance) during the reporting month (July 2024) and the investigation results and/or follow-up actions is provided below:

Air Quality Monitoring

- No Action/Limit Level exceedance for 1-hour TSP was recorded.
- No Action/Limit Level exceedance for 24-hour TSP was recorded.

Landscape and Visual Monitoring

• No non-conformity for landscape and visual was recorded.

Complaint Handling, Prosecution and Public Engagement

5. Summary of complaint/summons/prosecution in the reporting month is tabulated in **Table I**.

Table 1 Summary of Complaint/Summons/Frosecution in the Reporting Wonth					
Event	Event Details		Follow-up/ Remedial	Status/ Remarks	
Event	Number	Brief Description	Actions		
Complaints	0	_	_		
Received	0		_	-	
Notification of	0				
Summons and					
Prosecutions	0	-	-	-	
Received					

Table I Summary of Complaint/Summons/Prosecution in the Reporting Month

Reporting Changes

6. There were no reporting changes during the reporting month.

Future Key Issues

- 7. The key works or activities will be anticipated in the coming two months are as follows:
 - ABWF works
 - E&M Installation

1 INTRODUCTION

Background

- 1.1 Central Kowloon Route (CKR) is a 4.7km long dual 3-lane trunk road across Central Kowloon linking Yau Ma Tei Interchange in West Kowloon and the road network at Kai Tak Development and Kowloon Bay in East Kowloon. The underground tunnel section will be about 3.9km long. In particular, an underground tunnel of about 370m long in Kowloon Bay to the north of To Kwa Wan Typhoon Shelter will be constructed.
- 1.2 The Environmental Impact Assessment Report for Central Kowloon Route Design and Construction (Register No.: AEIAR-171/2013) was approved under the Environmental Impact Assessment Ordinance (EIAO) on 11 July 2013. An Environmental Permit (EP No.: EP-457/2013) was issued on 9 August 2013. Variations of Environmental Permit (VEP) was subsequently applied and an EP (EP No. EP-457/2013/C) was issued on 16 January 2017. The latest EP (EP No. EP-457/2013/D) was issued by Environmental Protection Department (EPD) on 15 June 2021.
- 1.3 The construction of the CKR had been divided into different sections. This Contract No. HY/2019/13 Central Kowloon Route Buildings, Electrical and Mechanical Works ("The Project") will include the architectural, civil and structural construction works of Yau Ma Tei Ventilation Building (YVB), Ho Man Tin Ventilation Building (HVB), Kai Tak Ventilation Building (KVB) and Central Kowloon Route Administration Building (ADB) for the CKR. The landscaping and electrical and mechanical (E&M) works within the building sites will be involved as well.
- 1.4 Cinotech Consultants Limited was assigned as the Environmental Team (ET) to undertake the EM&A works for the Project. The construction of this Contract was commenced on 12th October 2020.

Purpose of the Report

1.5 This is the 46th Monthly EM&A Report which summarises the impact monitoring results and audit findings for the EM&A programme in Yau Ma Tei West Area during the reporting period from 1st July 2024 – 31st July 2024. The Yau Ma Tei West Area site layout plan for the Project is shown in Figure 1.1.

Project Organizations

- 1.6 Different Parties with different levels of involvement in the project organization include:
 - Project Proponent Highways Department (HyD)
 - Engineer Representative (ER) Arup Mott MacDonald Joint Venture (AMMJV)
 - Environmental Team (ET) Cinotech Consultants Limited (Cinotech)
 - Independent Environmental Checker (IEC) Environmental Resources Management Hong Kong Limited (ERM)
 - Contractor Gammon Construction Limited (GCL)

1.7 The key contacts of the Project are shown in **Table 1.1**.

Table 1.1 Rey 110 jeet Contacts					
Party	Role	Contact Person	Phone No.		
AMMJV	Engineer Representative	Mr. Tommy Wong	3695 0419		
Cinotech	Environmental Team	Ms. Betty Choi	2151 2072		
ERM	RM Independent Environmental Checker	Ms. Mandy To	2271 3113		
GCL	Contractor	Mr. Sampson Lo	9752 9118		

Table 1.1 Key Project Contacts

1.8 The Organizational Structure for Environmental Management is shown in **Figure 1.2**.

Construction Activities undertaken during the Reporting Month

- 1.9 The construction programme is presented in **Appendix A**.
- 1.10 The major site activities undertaken in the reporting month included:
 - Super-structure works
 - ABWF works
 - E&M Installation

Summary of EM&A Requirements

- 1.11 The EM&A programme requires air quality monitoring, landscape and visual monitoring and environmental site audit. The EM&A requirements for each parameter are described in the following sections, including:
 - Environmental requirements and mitigation measures, as recommended in the EM&A Manual under the EP.
- 1.12 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 6 of this report.

Statues of Environmental Licensing and Permitting

1.13 All permits/licenses obtained for the Project are summarized in **Table 1.2**.

Table 1.2 Summary of Environmental Licensing and Permit Status

	Valid F	Status				
Permit / License No.	Permit / License No. From					
Environmental Permit (EP)						
EP-457/2013/D	15 Jun 2021	N/A	Valid			
Notification of Construction Works	s under Air Pollution	Control Ordinance	ee (APCO)			
457325	19 Jun 2020	End of Project	Valid			
Billing Account for Construction W	Vaste Disposal		1			
7037679	26 Jun 2020	N/A	Valid			
Registration of Chemical Waste Pr	oducer – YVB		<u> </u>			
5117-253-G2347-55	25 Aug 2020	N/A	Valid			
Wastewater Discharge Licence - Y	Wastewater Discharge Licence - YMT					
WT00036898-2020	25 Nov 2020	30 Nov 2025	Valid			
Construction Noise Permit (YVB S	ite - General Works)					
GW-RE0208-24	5 Mar 2024	4 Sep 2024	Valid			

2 AIR QUALITY

Monitoring Requirements

2.1 As all of the air quality (1-hour TSP and 24-hour TSP) monitoring works in Yau Ma Tei West Area are currently covered under the Contract No. HY/2014/20 (Central Kowloon Route - Yau Ma Tei West), the corresponding monitoring parameters, equipment, methodology, results and established Action and Limit Levels could be referred to Section 3 of the EM&A report for Contract No. HY/2014/20 during this reporting month.

Observations

- 2.2 No Action/Limit Level exceedance was recorded for all 1-hour TSP and 24-hour TSP monitoring in the reporting month.
- 2.3 Site audits were carried out on a weekly basis to monitor and audit the timely implementation of air quality mitigation measures within the site boundaries of this Project. The summary of site audits is shown in **Table 6.1** of this report.

3 NOISE

Monitoring Requirements

3.1 As all of the construction noise monitoring works in Yau Ma Tei West Area are currently covered under the Contract No. HY/2014/20 (Central Kowloon Route - Yau Ma Tei West), the corresponding monitoring parameters, equipment, methodology, results and established Action and Limit Levels could be referred to Section 3 of the EM&A report for Contract No. HY/2014/20 during this reporting month.

Observations

- 3.2 No Action/Limit Level exceedance was recorded for all construction noise monitoring in the reporting month.
- 3.3 Site audits were carried out on a weekly basis to monitor and audit the timely implementation of construction noise mitigation measures within the site boundaries of this Project. The summary of site audits is shown in **Table 6.1** of this report.

4 WASTE MANAGEMENT

Monitoring Requirements

4.1 Waste generated from this Project includes inert construction and demolition (C&D) materials and non-inert C&D materials. Inert C&D waste includes soil, broken rock, broken concrete and building debris, while non-inert C&D materials are made up of C&D waste which cannot be reused or recycled and has to be disposed of at the designated landfill sites.

Results and Observations

(in '000m³)

0.060

Jul 2024

4.2 The quantities of different types of waste generated in the reporting month are summarised in **Table 4.1**. Details of the amount of wastes generated by the major site activities of this Project during the reporting month is shown in **Appendix B**.

Table 4.1 Quantities of Waste Generated from the Project								
	Quantity							
	Inert C&I	D Materials		Noi	n-inert C&D Mate	rials		
Reporting	Total Disposed as		Others, e.g.	Metals	Paper/cardboard	Plastics		
Period	iod Quantity Public Fill		general	(in	Packaging	(in		
	Generated	(in '000m ³)	refuse (in	'000kg)	(in '000kg)	'000kg)		

 $(000m^3)$

0.219

 Table 4.1 Quantities of Waste Generated from the Project

0.060

4.3 Site audits were carried out on a weekly basis to monitor and audit to ensure that proper storage, transportation, and disposal practices of waste materials generated during construction activities, such as construction and demolition (C&D) materials and general refuse are being implemented. The summary of site audits is shown in **Table 6.1** of this report. The implementation status of the waste/chemical management measures in the reporting period are summarized in **Appendix C**.

0

0

0

Chemical waste (in '000kg)

0

5 LANDSCAPE AND VISUAL

Monitoring Requirements

5.1 According to the EM&A Manual, site audits would be undertaken during the construction phase of the Project to check that the proposed landscape and visual mitigation measures are properly implemented and maintained as per their intended objectives. Site inspections of the implementation of landscape and visual mitigation measures would be undertaken at least once every two weeks during the construction period.

Results and Observations

- 5.2 Bi-weekly inspection of the implementation of landscape and visual mitigation measures within the site boundaries of this Project was conducted on 9 & 23 July 2024. The implementation status of the landscape and visual mitigation measures in the reporting period are summarized in **Appendix C**. The summary of observations and recommendations made for landscape and visual mitigation measures during site audits are shown in **Table 6.1** of this report.
- 5.3 No non-compliance of the landscape and visual impact was recorded in the reporting month.

6 ENVIRONMENTAL AUDIT

Site Audits

- 6.1 Site audits were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site.
- 6.2 Site audits were conducted on 2, 9, 16, 23 & 30 July 2024 in the reporting month. Joint site inspection with the representative of IEC was conducted on 16 July 2024. No non-compliance was observed during the site audit.

Implementation Status of Environmental Mitigation Measures

- 6.3 According to Environmental Permit, the approved EIA Report (Register No.: AEIAR-171/2013), and the EM&A Manual of the Project, the mitigation measures detailed in the documents are recommended to be implemented during the construction phase. An Environmental Mitigation Implementation Schedule (EMIS) is provided in **Appendix C**.
- 6.4 The ET weekly site inspections were carried out during the reporting month and the observations and follow-up actions in Yau Ma Tei West Area are summarized in **Table 6.1**.

Parameters	Date	Observations	Follow-up Actions
Water Quality	N/A	No environmental deficiency was identified in the reporting period.	N/A
Air Quality	N/A	No environmental deficiency was identified in the reporting period.	N/A
Noise	16 July 2024	General refuse should be avoided accumulation.	General refuse has been removed.
Waste / Chemical Management	N/A	No environmental deficiency was identified in the reporting period.	N/A
Land Contamination	N/A	No environmental deficiency was identified in the reporting period.	N/A
Landscape and Visual	N/A	No environmental deficiency was identified in the reporting period.	N/A
Permits /Licences	N/A	No environmental deficiency was identified in the reporting period.	N/A

 Table 6.1 Observations and Recommendations of Site Inspections

Implementation Status of Event and Action Plans

6.5 The Event and Action Plans for air quality and construction noise could be referred to Appendices D and E of the EM&A report in Contract No. HY/2014/20 respectively.

Air Quality Monitoring

- No Action/Limit Level exceedance for 1-hour TSP was recorded.
- No Action/Limit Level exceedance for 24-hour TSP was recorded.

Construction Noise Monitoring

- No documented complaint on construction noise was received; no Action Level exceedance for day time construction noise monitoring was recorded.
- No Limit Level exceedance for day time construction noise monitoring was recorded in the reporting month.

Landscape and Visual Monitoring

• No non-conformity for landscape and visual was recorded.

Summary of Complaint, Warning, Notification of any Summons and Successful Prosecution

6.6 No environmental complaints, warning, notifications of summons and successful prosecutions were received in the reporting month. The summary of environmental complaint, warning, summon and notification of successful prosecution for the Project is presented in **Appendix D**

Status of Required Submission under Environmental Permit

6.7 Status of required submission under EP-457/2013/D during the reporting period are summarized in **Table 6.2**.

Table 6.2 Status of Required Submission under Environmental Permit

EP Condition (EP-457/2013/D)	Submission	Submission Date
Condition 3.4	Monthly EM&A Report (June 2024)	12 July 2024

7 FUTURE KEY ISSUES

- 7.1 Major site activities undertaken for the coming two months include:
 - ABWF works
 - E&M Installation
- 7.2 Key environmental issues in the coming two months include:
 - Stockpile accumulation on-site;
 - Water spraying for dust generating activities and on haul road;
 - Wastewater and runoff discharge from site;
 - Coverage of open manholes to avoid dirty runoff to drainage system;
 - Noise from operation of the equipment, especially for excavation works and machinery onsite;
 - Accumulation of general refuse and construction waste on-site;
 - Proper storage of construction materials on-site; and
 - Storage of chemicals/fuel and chemical waste/waste oil on-site.

8 CONCLUSIONS AND RECOMMENDATIONS

Conclusions

8.1 This is the 46th Monthly EM&A Report which presents the EM&A works undertaken in Yau Ma Tei West Area during the reporting month from 1st July 2024 – 31st July 2024 in accordance with the EM&A Manual and the requirements under the EP.

Air Quality Monitoring

8.2 No Action/Limit Level exceedance was recorded for all 1-hour and 24-hour TSP monitoring in the reporting month.

Construction Noise Monitoring

8.3 No Action/Limit Level exceedance was recorded for all noise monitoring in the reporting month. HY/2014/20

Landscape and visual

8.4 No non-compliance was recorded in the reporting month.


Site Audit


8.5 5 ET joint weekly environmental site inspections were conducted in the reporting month. Joint weekly site inspections with the representative of ET, Engineer Representative and the Contractor were conducted on 2, 9, 16, 23, & 30 July 2024, whereas joint site inspection with the representative of IEC was conducted on 16 July 2024. All environmental deficiencies observed during site inspections were rectified by the Contractor.

Complaint, Notification of Summons and Successful Prosecution

8.6 No environmental complaint and no notifications of summons and successful prosecutions were received in the reporting month.

FIGURES

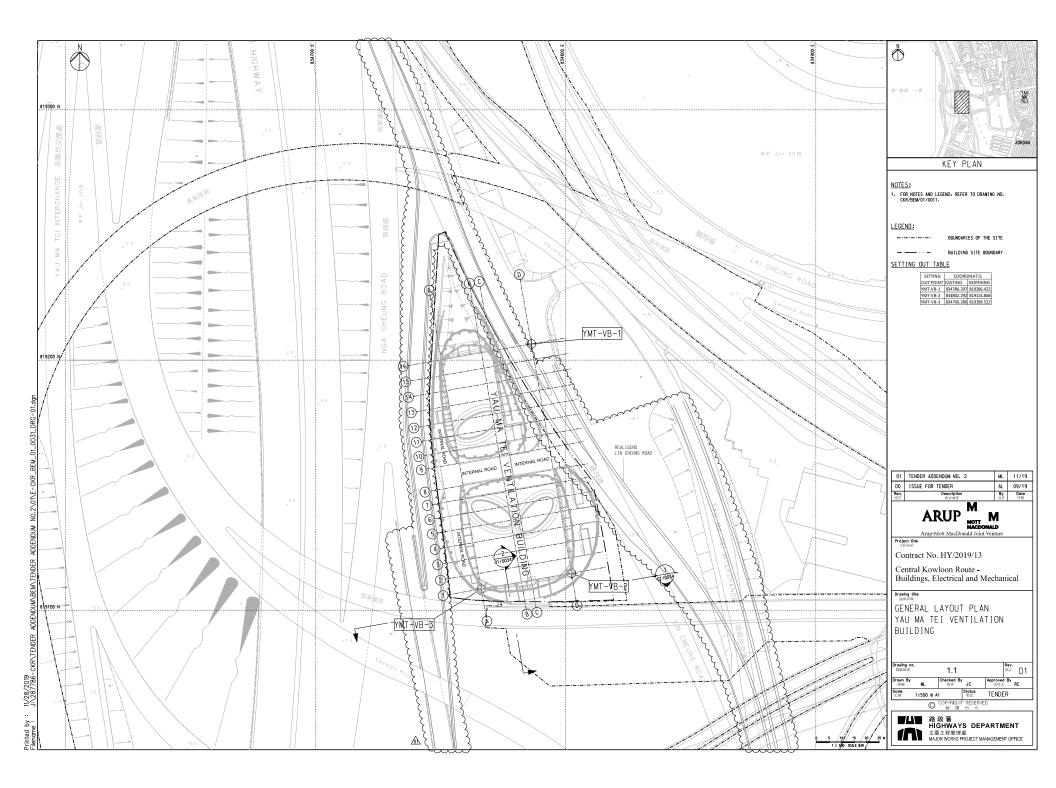


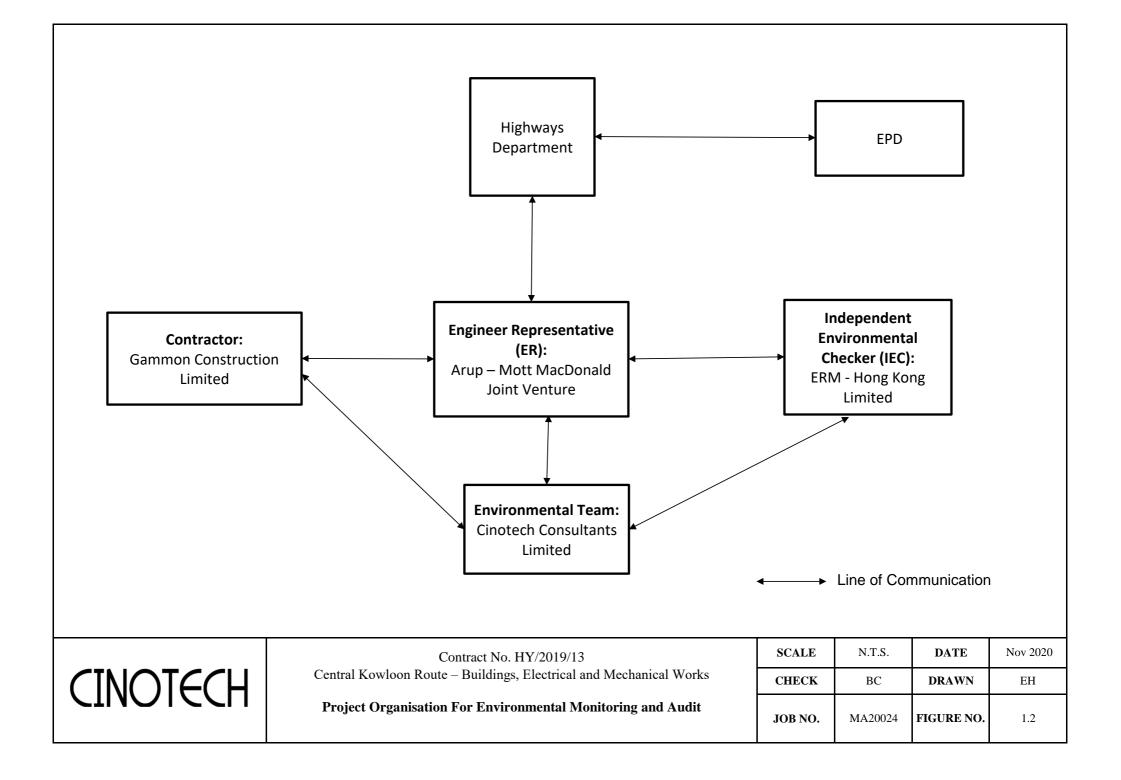

APPENDIX A CONSTRUCTION PROGRAMME



Contract No. HY/2019/13 Central Kowloon Route - Buildings, Electrical and Mechanical Works Summary Programme

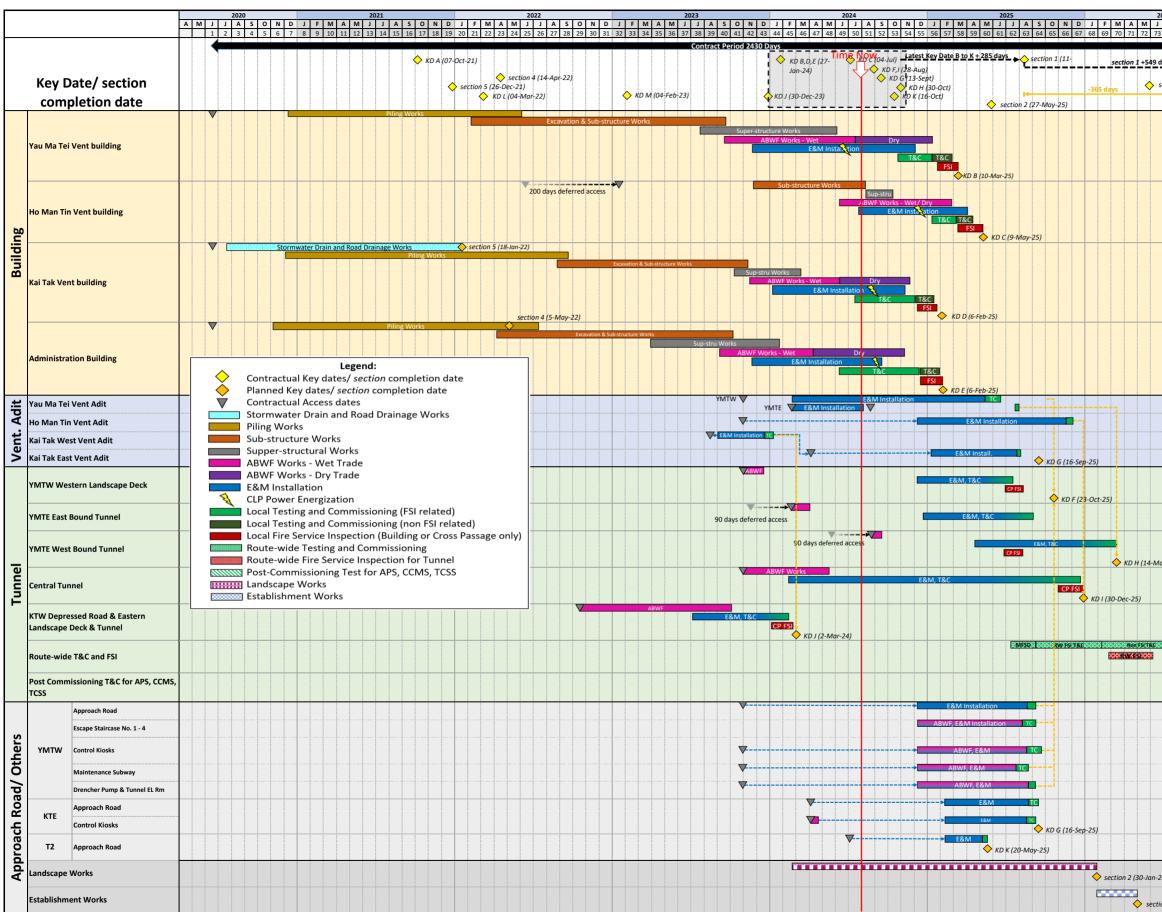



026											20	27								20	28		
1	Α	S	0	Ν	D	J	F	Μ	Α	М	1	1	Α	S	0	Ν	D	1	F	М	Α	м	J
74		76	77	78		80			83	84	85	86	87	88	89		91		93	94	95	96	97
																		-					
1																							
lays							\diamond	sect	ion 6	5 (11	-Feb	-27)											
	<u>+</u> -																						
ectio	n 3 (14-1	Иау-	26)																			
		sect	0.0	/11	A	261																	
	\diamond	seci	1011 1	(11	Aug	-20)																	
	ĩ																						
	1 -																						
	11 -																						
	i .																						
	÷.																						
	1																						
	i .																						
	i																						
	i -																						
	i.																						
	1																						
	L																						
	1																						
	1																						
	1																						
	1																						
_	1																						
	1																						
	L																						
	Ι.																						
_																							
	i .																						
	÷.																						
	i.																						
	i .																						
	i .																						
	i -																						
ar-26)																						
	L																						
	1																						
	L																						
																_							
	8																						
	0	sect	ion 1	(11	-Aud	-261																	
1					-																		
		1	7	~	-	5	Po	st-Co	mm	issid	nin	g Tes		~	2	~	~	~					
																-			₹ 	ecti	on 6		
	-															-			~				_
+																							
								_	_	_	_								_				
61																							
6)																							
on 3	12	10.	161																				
511 5	2-11	ay-2																					

APPENDIX B SUMMARY OF WASTE GENERATION AND DISPOSAL RECORDS

Monthly Summary Waste Flow Table

[PS Clauses 25.24(11)S & 25.34(16)(a)]

Annex 4 to Appendix C

Name of Department: HyD

Contract No.: HY/2019/13

Central Kowloon Route - Buildings, Electrical and Mechanical Works

Yau Ma Tei Site Area

	Monthly Summary	y Waste Flow Table for <u>2024 (</u> year)
--	-----------------	--

		Actual Quantit	es of Inert C&D	Materials Genera	ted Monthly			Actual	Quantites of C&	D Waste Generat	ed Monthly	
	Total Quantity	Hard Rock and	Reused in the	Reused in	Disposed as	Imported Fill	Metals	Paper /	Plastics	Chemical	Marine	Others, e.g.
	Generated	Large Broken	Contract	other Projects	Public Fill	(see Note 5)		cardboard	(see Note 3)	Waste	Sediment	general refuse
		Concrete	(see Note 5)	(see Note 5)	(see Note 5)			packaging		(see Note 5)	(see Note 7)	(see Note 5)
		(see Note 5)										
Month	(in '000m3)	(in '000m3)	(in '000m3)	(in '000m3)	(in '000m3)	(in '000m3)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m3)	(in '000m3)
Jan	0.019	0.000	0.000	0.000	0.019	0.000	0.000	0.000	0.000	0.000	0.000	0.413
Feb	0.153	0.000	0.000	0.000	0.153	0.000	0.000	0.000	0.000	0.000	0.000	0.215
Mar	0.550	0.000	0.000	0.000	0.550	0.000	0.000	0.000	0.000	0.000	0.000	0.334
Apr	0.147	0.000	0.000	0.000	0.147	0.000	0.000	0.000	0.000	0.000	0.000	0.312
May	0.010	0.000	0.000	0.000	0.010	0.000	0.000	0.000	0.000	0.000	0.000	0.327
Jun	0.004	0.000	0.000	0.000	0.004	0.000	0.000	0.000	0.000	0.000	0.000	0.252
Sub-Total	0.884	0.000	0.000	0.000	0.884	0.000	0.000	0.000	0.000	0.000	0.000	1.853
Jul	0.060	0.000	0.000	0.000	0.060	0.000	0.000	0.000	0.000	0.000	0.000	0.219
Aug	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Sep	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Oct	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Nov	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Dec	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Total (2024)	0.943	0.000	0.000	0.000	0.943	0.000	0.000	0.000	0.000	0.000	0.000	2.072
Total (whole)	88.224	0.000	0.000	57.554	30.670	0.000	0.000	0.000	0.000	0.000	0.000	5.864

Note:

(1) The performance targets are given in PS Clause 25.24

(2) The waste flow table shall also include C&D materails that are specified in the Contract to be imported for use at the Sites.

(3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials, and water barriers

(4)

The summary table shall be submitted to the Project Manager monthly together with the Waste Flow Table for review and monitoring in accordance with the PS Clause 25.24

(5) Density values and Bulk Factors adopted:

Hard Rock and Large Broken Concrete:	2.4 T/m3 (in-situ)	Bulk Factor:	1.25
Soil / Fill:	2.0 T/m3 (in-situ)	Bulk Factor:	1.1
Marine Sediment:	1.7 T/m3 (in-situ)	Bulk Factor:	1.3
General Refuse:	400 kg/m3		
Chemical Waste (mainly used lubricant):	900 kg/m3		
Tree Trunk / Tree Stump:	850 kg/m3 (in-situ)	Bulk Factor:	1.1

(6) The reported and forecast volume figures are in "bulk" volume, with Bulk Factor applied as per Note (5)

(7) This figure refers to marine sediment disposed via dumping at sea. Treated Sediment for Reuse on-site will be categorized into "Reused in the Contract"

APPENDIX C ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE (EMIS)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
	n Dust Impact			<u> </u>			1 2 2 2	•
S4.3.10	D1	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	- APCO - To control the dust impact to meet HKAQO and TM-EIA criteria	۸
\$4.3.10		Mitigation measures in form of regular watering under a good site practice should be adopted. Watering once per hour on exposed worksites and haul road should be conducted to achieve dust removal efficiencies of 91.7%. While the above watering frequencies are to be followed, the extent of watering may vary depending on actual site conditions but should be sufficient to maintain an equivalent intensity of no less than 1.3 L/m2 to achieve the dust removal efficiency.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	- APCO - To control the dust impact to meet HKAQO and TM-EIA criteria	٨
S4.3.10	D3	Proper watering at exposed spoil should be undertaken throughout the construction phase.	Minimize dust impact at the	Contractor	All construction sites	Construction stage	- APCO - To control the dust	٨
		Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading.	nearby sensitive receivers				impact to meet HKAQO and TM-EIA criteria	۸
		Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads.						٨
	A stocky	A stockpile of dusty material should not be extended beyond the pedestrian barriers, fencing or traffic cones.						۸
		The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle.						۸
		Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.						٨

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
		When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided and properly maintained as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period.						۸
		The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials.						۸
		Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously.						٨
		Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet						٨
		Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding.						N/A
		Any skip hoist for material transport should be totally enclosed by impervious sheeting.						N/A
		Every stock of more than 20 bags of cement or dry-pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides						٨
		Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed.						N/A
		Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system.						N/A

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
		Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabilizer within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.						N/A
\$4.3.10	D6	Implement regular dust monitoring under EM&A programme during the construction stage.	Monitoring of dust impact	Contractor	Selected rep. dust monitoring station	Construction stage	- TM-EIA	٨
Construction	n Noise (Airbor		•	•				
\$5.4.1	N1	Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme.	Control construction airborne noise	Contractor	All construction sites	Construction stage	- Annex 5, TM-EIAO	۸
		Machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.						۸
		Plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs.						٨
		Silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works.						٨
		Mobile plant should be sited as far away from NSRs as possible and practicable.						۸
		Material stockpiles, mobile container site office and other structures should be effectively utilized, where practicable, to screen noise from on-site construction activities.						N/A
S5.4.1	N2	Install temporary hoarding located on the site boundaries between noisy construction activities and NSRs. The conditions of hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level zone of NSRs through partial screening	Contractor	All construction sites	Construction stage	- Annex 5, TM-EIAO	٨

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
S5.4.1	N3	Install movable noise barriers (typical design is wooden framed barrier with a small-cantilevered on a skid footing with 25mm thick internal sound absorptive lining), acoustic mat or full enclosure, screen the noisy plants including air compressors, generators and handheld breakers, etc.	Sreen the noisy plant items to be used at all construction sites	Contractor	All construction sites where practicable	Construction stage	- Annex 5, TM-EIAO	N/A
S5.4.1	N4	Use 'Quiet plants'	Reduce the noise levels of plant items	Contractor	All construction sites where practicable	Construction stage	- Annex 5, TM-EIAO	٨
S5.4.1	N5	Loading/ unloading activities should be carried out inside the full enclosure of mucking out points.	Reduce the noise levels of loading/ unloading activities	Contractor	Mucking out locations	Construction stage	- Annex 5, TM-EIAO	۸
S5.4.1	N6	Sequencing operation of construction plants where practicable.	Operate sequentially within the same work site to reduce the construction airborne noise	Contractor	All construction sites where practicable	Construction stage	- Annex 5, TM-EIAO	٨
\$5.4.1	N7	Implement a noise monitoring programme under EM&A programme.	Monitor the construction noise levels at the selected representative locations		Selected rep. noise monitoring station	Construction stage	- TM-EIAO	٨
	ity (Construction							
S6.9.1.1	W1	<u>Construction Runoff</u> At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the contractor prior to the commencement of construction.	To minimize water quality impact from the construction site runoff and general construction activities		All construction sites where practicable	Construction stage	 Water Pollution Control Ordinance ProPECC PN 1/94 TM-EIAO TM-DSS 	^

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
		The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/ sediment trap. The sediment/ silt traps should be incorporated in the permanent drainage channels to enhance deposition rates.						۸
		The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt/ sand traps should be 5 minutes under maximum flow conditions. Sizes may vary depending upon the flow rate, but for a flow rate of 0.1 m3/s a sedimentation basin of 30 m3 would be required and for a flow rate of 0.5 m3/s the basin would be 150 m3. The detailed design of the sand/ silt traps shall be undertaken by the contractor prior to the commencement of construction.						Λ
		All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. Exposed slope surfaces should be covered by tarpaulin or other means.						N/A
		The overall slope of the site should be kept to a minimum to reduce the erosive potential of surface water flows, and all traffic areas and access roads protected by coarse stone ballast. An additional advantage accruing from the use of crushed stone is the positive traction gained during prolonged periods of inclement weather and the reduction of surface sheet flows.						N/A
		All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas.						۸
		Measures should be taken to minimize the ingress of site drainage into excavations. If the excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.						Λ

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
		Open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50m3 should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.						٨
		Manholes should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.						٨
		Precautions be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes.						۸
		All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and site wheel washing facilities should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel wash bay to the public road should be paved with sufficient backfall toward the wheel wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.						٨
		Oil interceptors should be provided in the drainage system downstream of any oil/ fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain.						Λ
		Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts.						۸

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
		All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby.						۸
		Adopt best management practices.	•					٨
		All earth works should be conducted sequentially to limit the amount of construction runoff generated from exposed areas during the wet season (April to September) as far as practicable.						۸
\$6.9.1.2	W2	<u>Tunneling Works and Underground Works</u> Cut-&-cover tunneling work should be conducted sequentially to limit the amount of construction runoff generated from exposed areas during the wet season (April to September) as far as practicable.	To minimize construction water quality impact from tunneling works	Contractor	All tunneling portion	Construction stage	- Water Pollution Control Ordinance - ProPECC PN 1/94 - TM-EIAO - TM-DSS	N/A
		Uncontaminated discharge should pass through sedimentation tanks prior to off-site discharge.	WOIKS				- IM-D22	۸
		The wastewater with a high concentration of SS should be treated (e.g. by sedimentation tanks with sufficient retention time) before discharge. Oil interceptors would also be required to remove the oil, lubricants and grease from the wastewater.						N/A
		Direct discharge of the bentonite slurry (as a result of D-wall) is not allowed. It should be reconditioned and reused wherever practicable. Temporary storage locations (typically a properly closed warehouse) should be provided on site for any unused bentonite that needs to be transported away after all the related construction activities area completed. The requirements in ProPECC PN 1/94 should be adhered to in the handling and disposal of bentonite slurries.						N/A

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
\$6.9.1.3		Sewage Effluent Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.	To minimize water quality from sewage effluent	Contractor	All construction sites where practicable	Construction stage	- Water Pollution Control Ordinance - TM-DSS	٨
\$6.9.1.5		Groundwater from Potential Contaminated Area: No direct discharge of groundwater from contaminated areas should be adopted. A discharge license under the WPCO through the Regional Office of EPD for groundwater discharge should be applied. Prior to the excavation works within these potentially contaminated areas, the groundwater quality should be reviewed during the process of discharge license application. The compliance to the Technical Memorandum on Standards for Effluents Discharged into Drainage on Sewerage Systems, Inland and Coastal Waters (TM-DSS) and the existence of prohibited substance should be confirmed. If the review results indicated that the groundwater to be generated from the excavation works would be contaminated, the contaminated groundwater should be either properly treated in compliance with the requirements of the TM-DSS or properly recharged into the ground.	To minimize groundwater quality impact from contaminated area	Contractor	Excavation areas where contamination is found	Construction stage	- Water Pollution Control Ordinance - TM-EIAO - TM-DSS	^

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
		If wastewater treatment is deployed, the wastewater treatment unit shall deploy suitable treatment process (e.g. oil interceptor / activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (e.g. TPH) to undetectable range. All treated effluent from wastewater treatment plant shall meet the requirements as stated in TM- DSS and should be discharged into the foul sewers.						۸
		If groundwater recharging wells are deployed, recharging wells should be installed as appropriate for recharging the contaminated groundwater back into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in the Section 2.3 of TM-DSS. The baseline groundwater quality shall be determined prior to the selection of the recharge wells, and submit a working plan (including the laboratory analytical results showing the quality of groundwater at the proposed recharge location(s) as well as the pollutant levels of groundwater to be recharged) to EPD for agreement. Pollution levels of groundwater at the recharge well. Prior to recharge, any prohibited substances such as TPH products should be removed as necessary by installing the petrol interceptor.						N/A
S6.9.1.6	W6	Accidental Spillage All the tanks, containers, storage area should be bunded and the locations should be locked as far as possible from the sensitive watercourse and stormwater drains. The Contractor should register as a chemical waste producer if chemical wastes would be generated. Storage of chemical waste arising from the construction activities should be stored with suitable labels and warnings.	To minimize water quality impact from accidental spillage	Contractor	All construction site where practicable	Construction stage	 Water Pollution Control Ordinance ProPECC PN 1/94 TM-EIAO TM-DSS 	Λ
		Disposal of chemical wastes should be conducted in compliance with the requirements as stated in the Waste Disposal (Chemical Waste) (General) Regulation.						٨

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
Waste Mana S7.4.1	igement (Const WM1	On-site sorting of C&D material	Separation of	Contractor	All construction	Construction	· DEVB (W) No. 6/2010	^
57.4.1	WINI	Geological assessment should be carried out by competent persons on site during excavation to identify materials which are not suitable to use as aggregate in structural concrete (e.g. volcanic rock, Aplite dyke rock, etc.). Volcanic rock and Aplite dyke rock should be separated at the source sites as far as practicable and stored at designated stockpile area preventing them from delivering to crushing facilities. The crushing plant operator should also be reminded to set up measures to prevent unsuitable rock from ending up at concrete batching plants and be turned into concrete for structural use. Details regarding control measures at source site and crushing facilities should be submitted by the Contractor for the Engineer to review and agree. In addition, site records should also be kept for the types of rock materials excavated and the traceability of delivery will be ensured with the implementation of Trip Ticket System and enforced by site supervisory staff as stipulated under DEVB TC(W) No. 6/2010 for tracking of the correct delivery to the rock crushing facilities for processing into aggregates. Alternative disposal option for the reuse of volcanic rock and Aplite Dyke rock, etc. should be explored.	Separation of unsuitable rock from ending up at concrete batching plants and be turned into concrete for structural use	Contractor	sites	stage	· DEVB (w) №. 6/2010	
\$7.5.1	WM2	<u>Construction and Demolition Material</u> Maintain temporary stockpiles and reuse excavated fill material for backfilling and reinstatement.	Good site practice to minimize the waste generation and recycle the	Contractor	All construction sites	Construction stage	Land (Miscellaneous Provisions) Ordinance Waste Disposal Ordinance	^
		Carry out on-site sorting.	C&D materials as				· ETWB TCW No.	^
		Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate	far as practicable so as to reduce the amount for final				19/2005	۸
		Adopt 'selective demolition' technique to demolish the existing structures and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible.	disposal					N/A
		Implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified.						٨
		Implement an enhanced Waste Management Plan similar to ETWBTC (Works) No. 19/2005 – "Environmental Management on Construction Sites" to encourage on-site sorting of C&D materials and to minimize their generation during the course of construction.						۸

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
\$7.5.1	WM3	C&D Waste Standard formwork or pre-fabrication should be used as far as practicable in order to minimize the arising of C&D materials. The use of more durable formwork or plastic facing for the construction works should be considered. Use of wooden hoardings should not be used, as in other projects. Metal hoarding should be used to enhance the possibility of recycling. The purchasing of construction materials will be carefully planned in order to avoid over ordering and wastage. The Contractor should recycle as much of the C&D materials as possible onsite. Public fill and C&D waste should be segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal. Where practicable, concrete and masonry can be crushed and used as fill. Steel reinforcement bar can be used by scrap steel mills. Different areas of the sites should be considered for such segregation and	Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	C	 Land (Miscellaneous Provisions) Ordinance Waste Disposal Ordinance ETWB TCW No. 19/2005 	^ N/A
\$7.5.1		storage. <u>Excavated Contaminated Soils</u> Details of the mitigation measures on handling of the contaminated soil shall be referred to Section on Land Contamination below.	The contaminated soil will be excavated for on- site reuse	Contractor	PBH4	t of construction works within	 Practice Guide (PG) for Investigation and Remediation of Contaminated Land GN/GM for land contamination 	Λ
S7.5.1	WM5	Land-based and Marine-based Sediment All construction plant and equipment shall be designed and maintained to minimize the risk of silt, sediments, contaminants or other pollutants being released into the water column or deposited in the locations other than designated location. All vessels shall be sized such that adequate draft is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash.	To control pollution due to marine sediment	Contractor	Along CKR alignment	Construction	• ETWB TCW No. 34/2002	^ N/A

11

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
		Before moving the vessels which are used for transporting dredged material, excess material shall be cleaned from the decks and exposed fittings of vessels and the excess materials shall never be dumped into the sea except at the approved locations.						N/A
		Adequate freeboard shall be maintained on barges to ensure that decks are not washed by wave action.						N/A
		The Contractors shall monitor all vessels transporting material to ensure that no dumping outside the approved location takes place. The Contractor shall keep and produce logs and other records to demonstrate compliance and that journeys are consistent with designated locations and copies of such records shall be submitted to the engineers.						N/A
		The Contractors shall comply with the conditions in the dumping licence.						^
		All bottom dumping vessels (Hopper barges) shall be fitted with tight fittings seals to their bottom openings to prevent leakage of material.						N/A
		The material shall be placed into the disposal pit by bottom dumping.						N/A
		Contaminated marine mud shall be transported by spit barge of not less than 750m3 capacity and capable of rapid opening and discharge at the disposal site.						N/A
		Discharge shall be undertaken rapidly and the hoppers shall be closed immediately. Material adhering to the sides of the hopper shall not be washed out of the hopper and the hopper shall remain closed until the barge returns to the disposal site.						N/A
		For Type 3 special disposal treatment, sealing of contaminant with geosynthetic containment before dropping designated mud pit would be a possible arrangement. A geosynthetic containment method is a method whereby the sediments are sealed in geosynthetic containers and, the containers would be dropped into the designated contaminated mud pit where they would be covered by further mud disposal and later by the mud pit capping at the disposal site, thereby fulfilling the requirements for fully confined mud disposal.						N/A

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
\$7.5.1	WM6	<u>Chemical Waste</u> Chemical waste that is produced, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, should be handled in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.	Control the chemical waste and ensure proper storage, handling and disposal	Contractor	All construction sites	Construction stage	 Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling and Storage of Chemical 	۸
		Containers used for the storage of chemical wastes should be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed, have a capacity of less than 450 L unless the specification has been approved by EPD, and display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the regulation.					Waste	۸
		The storage area for chemical wastes should be clearly labelled and used solely for the storage of chemical waste, enclosed on at least 3 sides, have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20% of the total volume of waste stored in that area, whichever is the greatest, have adequate ventilation, covered to prevent rainfall entering, and arranged so that incompatible materials are adequately separated.						۸
		Disposal of chemical waste should be via a licensed waste collector, be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Centre which also offers a chemical waste collection service and can supply the necessary storage containers, or be to a reuser of the waste, under approval from EPD.						۸
S7.5.1	WM7	<u>General Refuse</u> General refuse generated on-site should be stored in enclosed bins or compaction units separately from construction and chemical wastes.	Minimize production of the general refuse and	Contractor	All construction sites	Construction stage	• Waste Disposal Ordinance	۸
		A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law.	avoid odour, pest and litter impacts					*
		Aluminum cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. Separate labelled bins for their deposit should be provided if feasible.						^

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures N	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
		Office wastes can be reduced through the recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme should be considered by the Contractor.						^
Land Contai	mination							
S8.9 & Appendix 8.4	LC2	Excavation of the Contaminated Soil Prior to commencement of the excavation works at the contamination zone, the zone should be clearly marked out on site and the surface levels recorded. Excavation of contaminated material should be undertaken using dedicated earth-moving plant.	The contaminated soil will be excavated for on- site reuse	Contractor	PBH4	t of	Practice Guide (PG) for Investigation and Remediation of Contaminated Land - Guidance Notes for Contaminated Land	N/A
		The excavated contaminated soils would be stockpiled at designated area on site and covered by sheet to prevent dispersion of contamination during stockpiling.				contaminated area	Assessment and Remediation • Guidance Manual for Use of Risk-Based Remediation Goals (RBRGs) for Contaminated Land Management	N/A
		The Contractor should pay attention to the selection of suitable groundwater lowering schemes and discharge points if the groundwater table is higher than the contaminated soils during excavation. The Contractor should also obtain a valid Water Pollution Control Ordinance (WPCO) discharge licence from EPD where applicable.						N/A
Hazard to Li	ife							
S9.18	H8	The driver and his assistant should be physically healthy, experienced and have good safe driving records. The driver should hold a proper driving licence for the approved transport truck. Dedicated training programme and regular road safety briefing sessions/ workshops should be provided to enhance their safe driving attitude and practice. Smoking should be strictly prohibited.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	/	^
S9.18	H9	Emergency response plans in case of road accident should be prepared and implemented. The driver and his assistant should be familiar with the emergency procedures including evacuation, and proper communication/ fire-fighting equipment should be provided to the driver and his assistant.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	/	۸

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
Landscape a	nd Visual							
S10.10.1 Table 10.11		<u>Good Site Management</u> Large temporary stockpiles of excavated material shall be covered with unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance.		Contractor	Within Project site	Construction Phase	/	^
S10.10.1 Table 10.11	LV4	in order to create a neat and tidy visual appearance. <u>Screen Hoarding</u> Decorative screen hoarding should be erected to screen the public from the construction area. It should be designed to be compatible with the existing urban context.	Minimize visual impact	Contractor	Within Project site	Construction Phase	/	^
S10.10.1 Table 10.11	LV5	<u>Lighting Control during Construction</u> All lighting in the construction site shall be carefully controlled to minimize light pollution and night-time glare to nearby residencies and GIC. The Contractor shall consider other security measures, which shall minimize the visual impacts.	Minimize visual impact	Contractor	Within Project site	Construction Phase	/	^
S10.10.1 Table 10.11	LV6	<u>Erosion Control</u> The potential for soil erosion shall be reduced by minimizing the extent of vegetation disturbance on site and by providing a protective cover over newly exposed soil.	Minimize landscape impact	Contractor	Within Project site	Construction Phase	/	۸

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
\$10.10.1 Table 10.11	LV7	<u>Tree Protection & Preservation</u> Carefully protected during construction. Tree protection measures will be detailed at the Tree Removal Application stage and plans submitted to the relevant Government Department for approval in due course in accordance with ETWB TC no. 3/2006.	visual impact	Contractor	Within Project site		 'Guidelines for Tree Risk Management and Assessment Arrangement on an Area Basis and on a Tree Basis', Greening, Landscape and Tree Management (GLTM) Section, DEVB Latest recommended horticultural practices from GLTM Section, 	N/A
S10.10.1 Table 10.11	LV8	<u>Tree Transplantation</u> For trees unavoidably affected by the Project that have to be removed, where practical transplantation will be chosen as the top priority method of removal. If this is not possible or practical compensatory planting will be provided for trees unavoidably felled (See LV10). For trees unavoidably affected by the Project works that are transplanted, transplantation must be carried out in accordance with ETWB TCW 2/2004 and 3/2006.	visual impact	Contractor	Within Project site and designated off- site locations		ETWB TCW 3/2006 Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DEVB ETWB TCW 2/2004	N/A
S10.10.1 Table 10.11	LV9	<u>Compensatory Planting</u> For trees unavoidably affected by the Project that have to be removed, where practical transportation will be chosen as the top priority method of removal but if this is not possible or practical compensatory planting will be provided for trees unavoidably felled. All felled trees shall be compensated for by planting trees to the satisfaction of relevant Government projects. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006.	enhance landscape	Contractor	Within Project site		ETWB TCW 3/2006 Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DEVB ETWB TCW 2/2004	N/A

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
S10.10.1 Table 10.11	LV10	Screen Planting Tall screen/buffer trees, shrubs and climbers should be planted, in so far as is possible, to soften and screen proposed structures such as roads and central strip, vertical edges and buildings and to enhance streetscape greening effect where appropriate. Indiscriminate use of trees for screening must be avoided and the principle of 'right tree for the right place' must be followed. This detail will be provided at the Detailed Design stage. This measure may additionally form part of the compensatory planting and will improve and create a pleasant pedestrian environment.	Minimize visual impact and also enhance landscape	Contractor	Within Project site	Construction Phase	 Guidelines on Greening of Noise Barriers, issued April 2012, GLTMS, DevB ETWB TCW 2/2004 	N/A
S10.10.1 Table 10.11	LV11	<u>Green Roof</u> Roof greening will be established on ventilation and administration buildings to reduce exposure to untreated concrete surfaces and particularly mitigate visual impact to VSRs at high levels.	Minimize landscape and visual impact	Contractor	Within Project site	Construction Phase	/	N/A
S10.10.1 Table 10.11	LV12	<u>Reinstatement</u> All works areas, excavated areas and disturbed areas for tunnel construction and temporary road diversion or any other proposed works shall be reinstated to former conditions or better, with reasonable landscape treatment and to the satisfaction of the relevant Government departments. (Specific mitigation for disturbance to public open space is detailed separately under LV14)	Minimize landscape impact	Contractor	Within Project site	Construction Phase	/	N/A
S10.10.1 Table 10.11	LV13	Reprovising of Public Open Space All areas of public open space affected by the Project will be reprovisioned either at the same location following the completion of temporary works, or at a separate site, as agreed with relevant Government departments. Open space should be re-provisioned in an enhanced manner.	Minimize landscape impact	Contractor	Within Project site	Construction Phase	Open space should be re-provided in an enhanced manner.	N/A
Cultural Her	ritage Impact (Construction Phase)	<u> </u>	<u> </u>		<u> </u>		
S11.4.4	CHI	The contractor should be alerted during the construction on the possibility of locating archaeological remains and as a precautionary measure, AMO shall be informed immediately in case of discovery of antiquities or supposed antiquities in the subject sites.	To preserve any cultural heritage items which may be removed and damaged by the excavation	Contractor	During construction works for cut and cover tunnels	During the Construction Phase	• AMOs requirements	N/A

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementati on Agent	Location / Timing	Implementatio n Stage	Requirements and/ or standards to be achieved	Implementation Status
EM&A Proj	ect							
\$13.2		An Independent Environmental Checker needs to be employed as per the EM&A Manual	Control EM&A Performance	Highways Department	All construction sites	Construction stage	 EIAO Guidance Note No. 4/2010 TM-EIAO 	٨
\$13.2-13.4	EM2	An Environmental Team needs to be employed as per the EM&A Manual.	Perform environmental monitoring & auditing	Highways Department/ Contractor	All construction sites	Construction stage	 • EIAO Guidance Note No. 4/2010 • TM-EIAO 	۸
		Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures;						^
		An environmental impact monitoring needs to be implemented by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with.						٨

Remarks: E	M&A Programme under EP-457/2013/D
^	Compliance of mitigation measure;
N/A N/A(1)	Not applicable at this stage; Not observed;
*	Recommendation was made during site audit but improved/retified by the contractor;
#	Recommendation was made during site audit but not yet improved/retified by the contractor;
Х	Non-compliance of mitigation measure;
•	Non-compliance but rectified by the contractor.

APPENDIX D SUMMARIES OF ENVIRONMENTAL COMPLAINT, WARNING, SUMMON AND NOTIFICATION OF SUCCESSFUL PROSECUTION

Complaint Log on Reporting Month (July 2024)

Log	Ref.	Location	Received Date	Details of Complaint/warning/ summon and prosecution	Investigation/ Mitigation Action	Status
N	/A	N/A	N/A	N/A	N/A	N/A

Remarks: No environmental complaint and warning/summon and prosecution was received in the reporting period.

Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions and Public Engagement Activities

Reporting Period	Site Location	Frequency	Cumulative	Details
July 2024	Kai Tak East	Environmental Complaint Statistics		
		0	3	N/A
		Environmental Non-compliance Statistic		
		0	0	N/A
		Environmental Summon and Prosecution Statistic		
		0	0	N/A
	Yau Ma Tei West	Environmental Complaint Statistics		
		0	0	N/A
		Environmental Non-compliance Statistic		
		0	0	N/A
		Environmental Summon and Prosecution Statistic		
		0	0	N/A
	Ho Man Tin	Environmental Complaint Statistics		
		0	3	N/A
		Environmental Non-compliance Statistic		
		0	0	N/A
		Environmental Summon and Prosecution Statistic		
		0	0	N/A
