## **Appendix H Regular Construction Noise Monitoring Results**

Daytime Noise Monitoring Results at Station E-N12a (19 Hing Yan Street)


Date	Weather Condition	Noise Level for 30-min, dB(A) +				Limit Level,	Exceedance
		Time	L90	L10	Leq	dB(A)	(Y/N)
1-Dec-20	Sunny	14:00	66.9	67.7	67.0	75	N
7-Dec-20	Sunny	14:00	65.4	66.9	66.5	75	N
18-Dec-20	Sunny	14:00	59.2	61.4	60.3	75	N
24-Dec-20	Fine	10:05	59.8	60.8	60.2	75	N
30-Dec-20	Sunny	11:30	61.4	62.7	61.9	75	N


Daytime Noise Monitoring Results at Station E-N21a (Block B of Merit Industrial Centre)

Date	Weather Condition	Nois	e Level for	<sup>.</sup> 30-min, d	Limit Level,	Exceedance	
		Time	L90	L10	Leq	dB(A)	(Y/N)
1-Dec-20	Sunny	12:15	68.1	69.1	68.7	75	N
7-Dec-20	Sunny	9:30	62.7	68.5	65.2	75	N
18-Dec-20	Sunny	10:30	62.3	64.2	63.1	75	N
24-Dec-20	Fine	9:30	61.2	61.9	61.4	75	N
30-Dec-20	Sunny	14:00	59.2	59.9	59.7	75	Ň

<sup>&</sup>lt;sup>+</sup> - Façade measurement.

<sup># -</sup> A correction of +3dB(A) was made to the free field measurement.
\* - Limit Level of 70dB(A) applies to education institutes while 65dB(A) applies during school

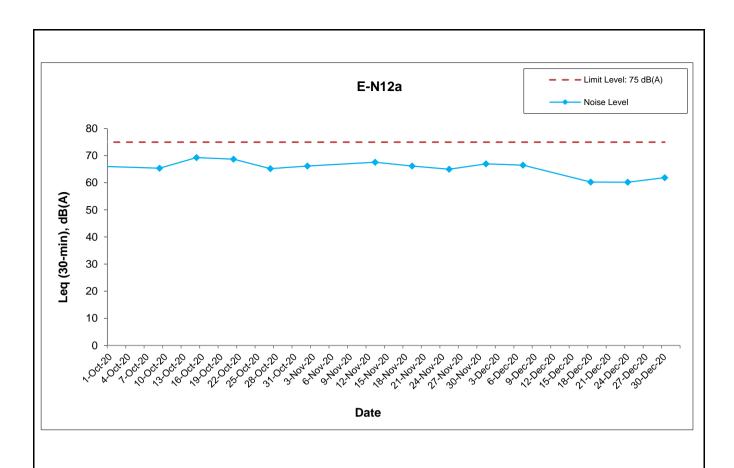

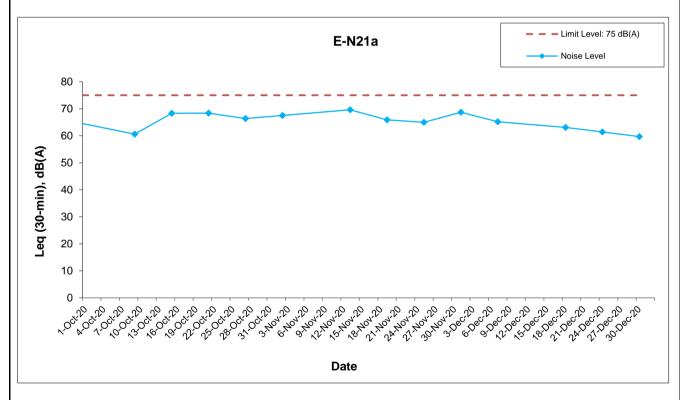

Central Kowloon Route - Kai Tak West (Contract No. HY/2014/07)

**AECOM** 

**Graphical Presentation of Impact Noise Monitoring Results** 

Date: January 2021

Appendix H
