## **Appendix H Regular Construction Noise Monitoring Results**

Daytime Noise Monitoring Results at Station E-N12a (19 Hing Yan Street)

Date	Weather Condition	Noise Level for 30-min, dB(A) +				Limit Level,	Exceedance
		Time	L90	L10	Leq	dB(A)	(Y/N)
5-Jul-21	Fine	12:20	65.2	67.9	66.7	75	N
16-Jul-21	Fine	13:00	67.8	69.9	68.9	75	N
22-Jul-21	Cloudy	14:00	66.8	68.5	67.9	75	N
28-Jul-21	Sunny	14:00	64.0	66.9	65.7	75	N


Daytime Noise Monitoring Results at Station E-N21a (Block B of Merit Industrial Centre)


Date	Weather Condition	Noise Level for 30-min, dB(A) #				Limit Level,	Exceedance
		Time	L90	L10	Leq	dB(A)	(Y/N)
5-Jul-21	Fine	11:05	66.9	68.2	67.8	75	N
16-Jul-21	Fine	14:30	70.1	71.9	71.3	75	N
22-Jul-21	Cloudy	15:05	67.9	69.1	68.8	75	N
28-Jul-21	Sunny	14:00	65.5	67.8	66.6	75	N

<sup>&</sup>lt;sup>+</sup> - Façade measurement.

<sup>#</sup> - A correction of +3dB(A) was made to the free field measurement.

<sup>\* -</sup> Limit Level of 70dB(A) applies to education institutes while 65dB(A) applies during school examination

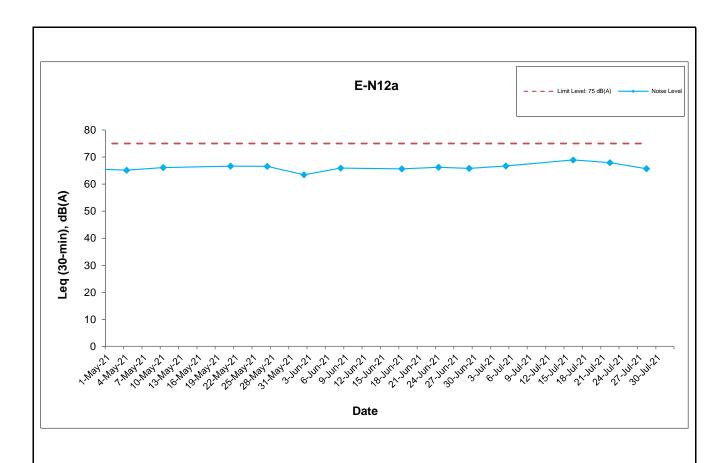

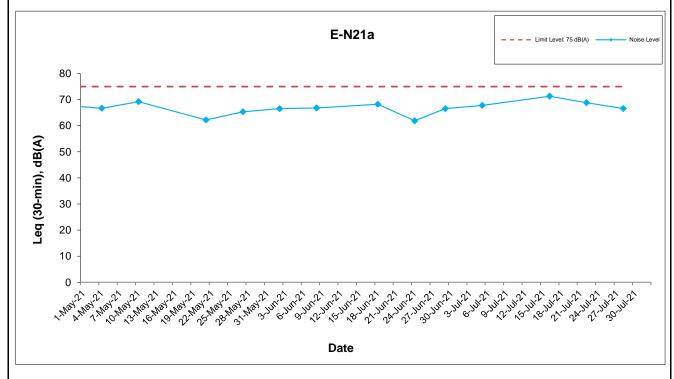

This Drawing has been prepared for the use of ACOUN's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by ACOUN or as required by laws AECOUN accepts no responsibility, and denies any liability whatever, to any parly that uses or relies on this drawing without AECOUN's express withen conse

Central Kowloon Route - Kai Tak West (Contract No. HY/2014/07)



**Graphical Presentation of Impact Noise Monitoring Results** 

Date: August 2021 Appendix H
