## **Appendix H Regular Construction Noise Monitoring Results**

Daytime Noise Monitoring Results at Station E-N12a (19 Hing Yan Street)

Date	Weather Condition	Nois	e Level for	· 30-min, d	Limit Level,	Exceedance	
		Time	L90	L10	Leq	dB(A)	(Y/N)
5-Mar-20	Fine	13:20	63.8	68.0	66.5	75	N
11-Mar-20	Fine	11:10	60.5	68.5	66.1	75	N
17-Mar-20	Sunny	14:30	65.5	69.0	67.5	75	N
23-Mar-20	Sunny	12:15	64.2	68.1	66.9	75	Ν


Daytime Noise Monitoring Results at Station E-N21a (Block B of Merit Industrial Centre)


Date	Weather Condition	Noise Level for 30-min, dB(A) #				Limit Level,	Exceedance
		Time	L90	L10	Leq	dB(A)	(Y/N)
5-Mar-20	Fine	14:10	61.8	65.6	63.9	75	N
11-Mar-20	Fine	13:00	63.5	66.5	65.6	75	N
17-Mar-20	Sunny	11:05	63.5	66.0	64.9	75	N
23-Mar-20	Sunny	11:20	67.4	69.5	68.3	75	N

<sup>+ -</sup> Façade measurement.
# - A correction of +3dB(A) was made to the free field measurement.

<sup>++ -</sup> Free field measurement

<sup>\* -</sup> Limit Level of 70dB(A) applies to education institutes while 65dB(A) applies during school

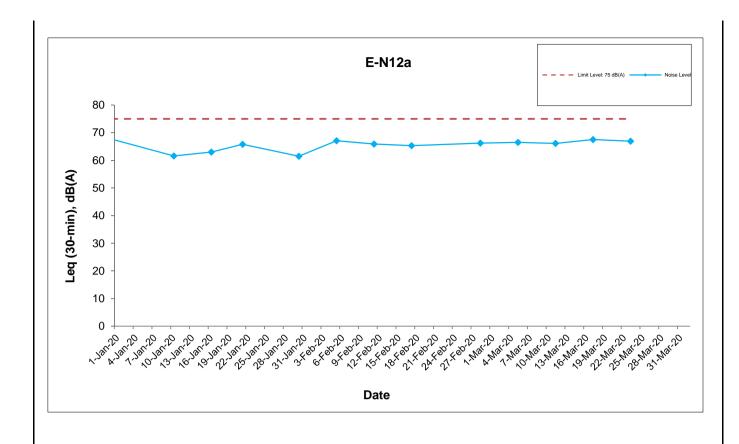

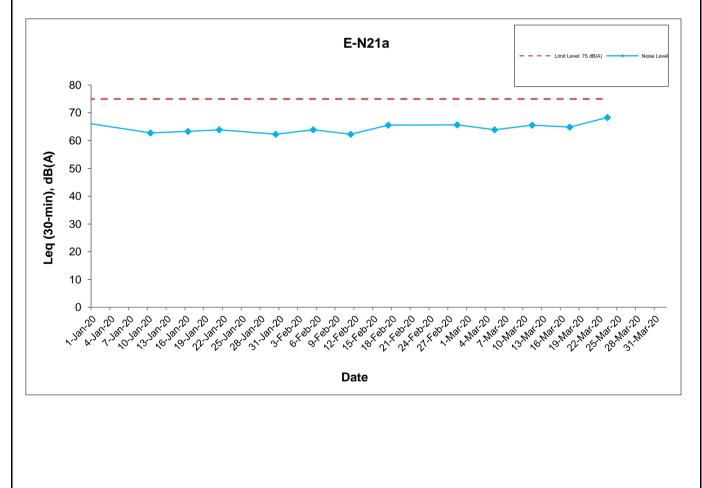

Central Kowloon Route - Kai Tak West (Contract No. HY/2014/07)

is Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agre

