## **Appendix H Regular Construction Noise Monitoring Results**

Daytime Noise Monitoring Results at Station E-N12a (19 Hing Yan Street)

Date	Weather Condition	Noise Level for 30-min, dB(A) <sup>+</sup>				Limit Level,	Exceedance
		Time	L90	L10	Leq	dB(A)	(Y/N)
4-May-21	Sunny	13:55	63.2	67.0	65.1	75	N
10-May-21	Sunny	10:50	64.5	66.9	66.1	75	N
21-May-21	Sunny	13:50	62.6	70.1	66.6	75	N
27-May-21	Sunny	14:00	64.3	68.1	66.5	75	N


Daytime Noise Monitoring Results at Station E-N21a (Block B of Merit Industrial Centre)


Date	Weather Condition	Noise Level for 30-min, dB(A) #				Limit Level,	Exceedance
		Time	L90	L10	Leq	dB(A)	(Y/N)
4-May-21	Sunny	14:45	64.8	68.2	66.7	75	Ν
10-May-21	Sunny	10:00	68.1	69.9	69.2	75	N
21-May-21	Sunny	14:38	60.5	63.5	62.2	75	N
27-May-21	Sunny	14:50	63.2	67.4	65.3	75	N

<sup>&</sup>lt;sup>+</sup> - Façade measurement.

<sup># -</sup> A correction of +3dB(A) was made to the free field measurement.

<sup>\* -</sup> Limit Level of 70dB(A) applies to education institutes while 65dB(A) applies during school examination

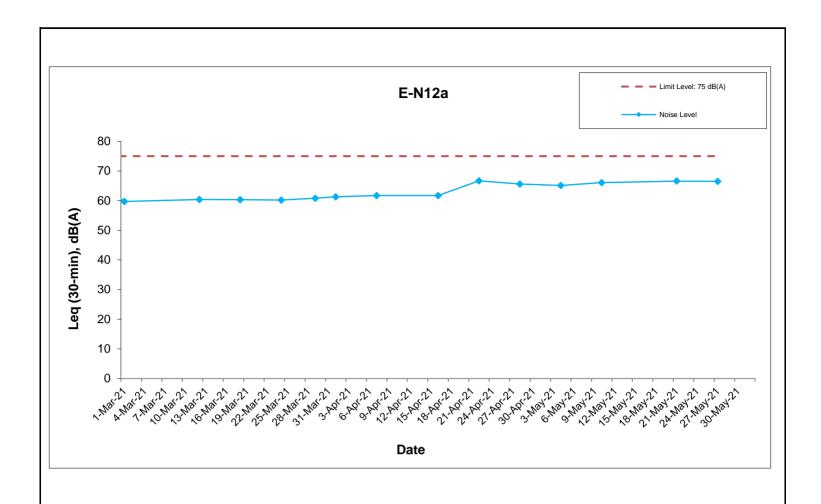

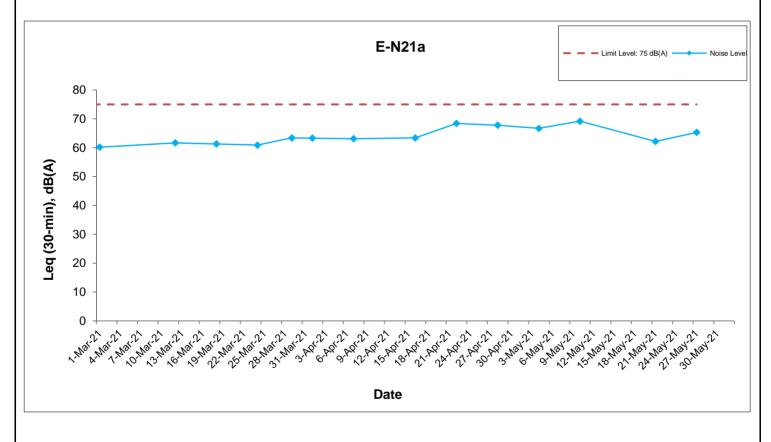

Central Kowloon Route - Kai Tak West (Contract No. HY/2014/07)

ared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as o

**A**ECOM

**Graphical Presentation of Impact Noise Monitoring Results** 

Date: June 2021 Appendix H
