


Appendix F - 24-hour TSP Monitoring Results

Location M-A3 - S.K.H. Tsoi Kung Po Secondary School

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate weight (g)	Elapse Time		Sampling Time (hrs.)	Flow Rate (m ³ /min.)		Av. Flow (m ³ /min)	Total vol. (m ³)	Conc. (µg/m ³)	Action Level (µg/m ³)	Limit Level (µg/m ⁴)
				Initial	Final		Initial	Final		Initial	Final					
2-Jan-26	Sunny	287.7	769.1	2.8145	2.8376	0.0231	14467.3	14491.3	24.0	1.25	1.26	1.25	1806.5	12.8	153.0	<u>260.0</u>
7-Jan-26	Fine	287.2	769.8	2.7842	2.8125	0.0283	14491.3	14515.3	24.0	1.26	1.25	1.26	1808.8	15.6		
13-Jan-26	Sunny	291.9	764.9	2.8218	2.8383	0.0165	14515.3	14539.3	24.0	1.24	1.24	1.24	1789.6	9.2		
19-Jan-26	Fine	292.1	763.3	2.8043	2.8172	0.0128	14539.3	14563.3	24.0	1.24	1.24	1.24	1787.2	7.2		
24-Jan-26	Sunny	290.5	767.3	2.7920	2.8287	0.0366	14563.3	14587.3	24.0	1.25	1.25	1.25	1796.2	20.4		
29-Jan-26	Cloudy	291.7	766.3	2.7979	2.8174	0.0194	14587.3	14611.3	24.0	1.25	1.24	1.24	1791.7	10.8		
													Min	7.2		
													Max	20.4		
													Average	12.7		

24-hr TSP Concentration Levels

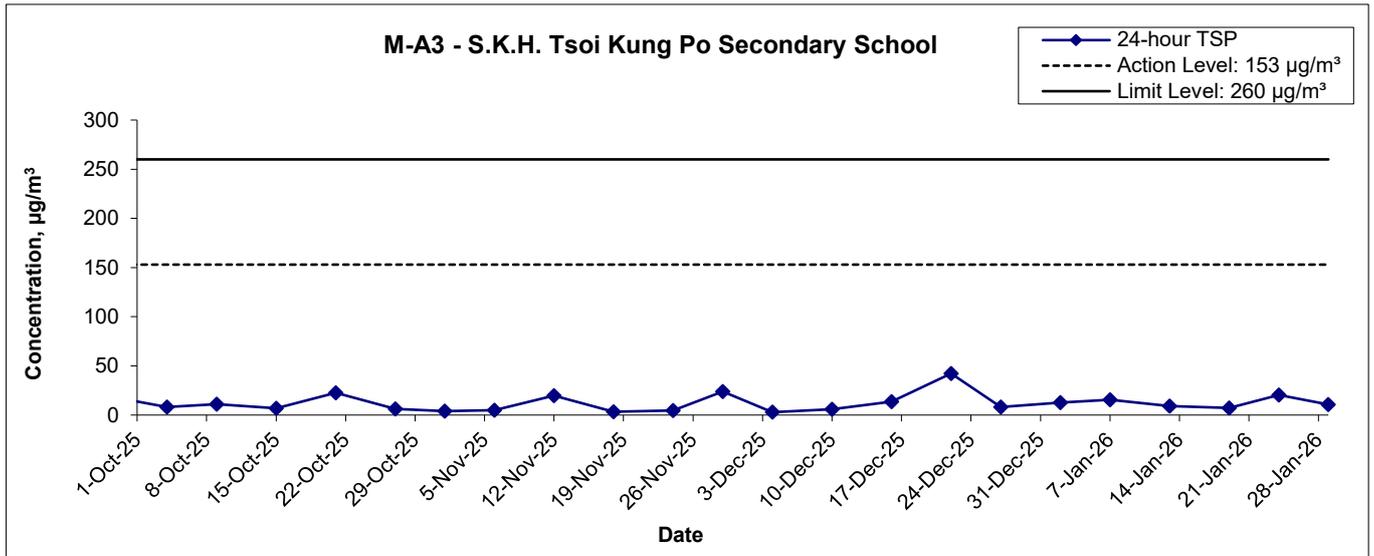

Title Contract No. HY/2019/13 Central Kowloon Route – Buildings, Electrical and Mechanical Works Graphical Presentation of 24-hour TSP Monitoring Results	Scale N.T.S	Project No. MA20024	
	Date Jan 26	Appendix F	
