

Appendix H

Construction Noise Monitoring Results


Noise Impact Monitoring Result for Contract No. HY/2018/08 Central Kowloon Route – Central Tunnel

M-N3 - SKH Tsoi Kung Po Secondary School

Date	Start Time	Measured Noise Level Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
4-Mar-20	14:00	70.0	71.5	68.0	0.8	Fine
10-Mar-20	09:05	68.5	71.5	64.5	2.6	Fine
16-Mar-20	13:05	69.4	72.5	65.5	1.9	Fine
24-Mar-20	09:02	69.5	71.0	66.5	3.3	Fine
30-Mar-20	09:00	69.8	73.0	68.0	2.5	Fine
	Max	70.0				
	Min	68.5				
	Limit Level	70.0				

Note:

Free field noise levels were adjusted with a correlation of +3 dB(A).

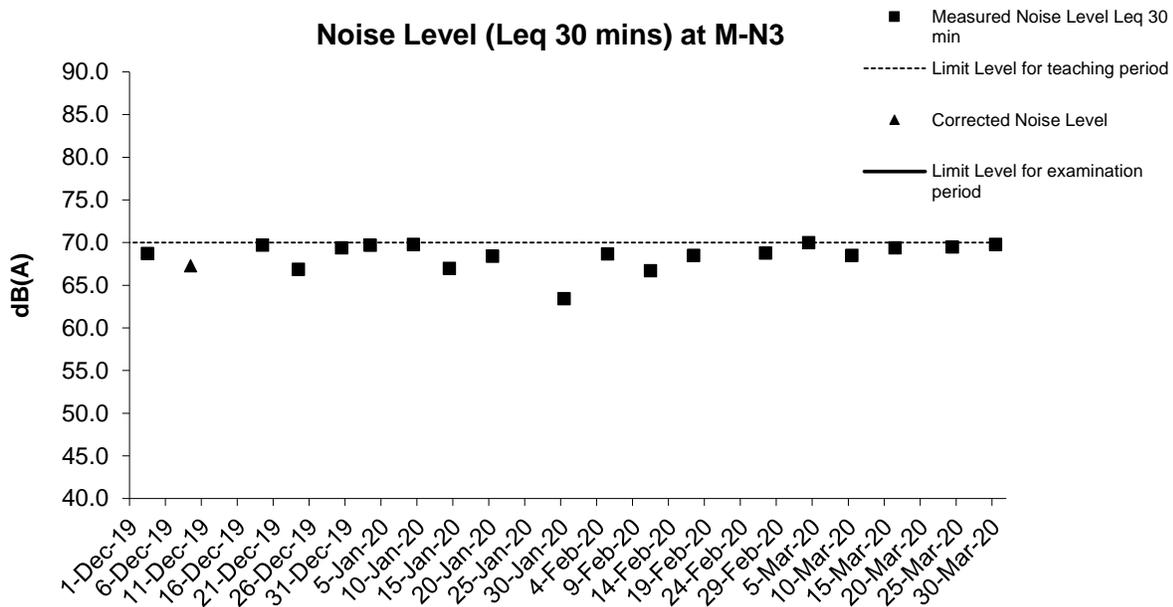

Remark: Corrected Noise Level was applied on 9 December 2019; Corrected Noise Level = Measured Noise Level - Baseline Noise Level (i.e. 67.7 dB(A))
